

STORAGE MATERIALS

1851 Madison Avenue #300 Council Bluffs, IA 51503
(888) 968–1222 <https://storagematerials.com/>

BUILDING LOADS / DESCRIPTION:

WIDTH: 90 LENGTH: 225 HEIGHT: 20.5 /24
(BUILDING DIMENSIONS ARE NOMINAL. REFER TO PLANS).

THIS STRUCTURE IS DESIGNED UTILIZING THE LOADS INDICATED
AND APPLIED AS REQUIRED BY : IBC 18 .

THE CONTRACTOR IS TO CONFIRM THAT THESE LOADS COMPLY
WITH THE REQUIREMENTS OF THE LOCAL BUILDING DEPARTMENT.

ROOF DEAD LOAD:	<u>2.50</u>	PSF (ROOF PANELS & PURLINS)		
COLLATERAL LOAD:	<u>3.00</u>	PSF	SNOW EXPOSURE:	<u>1.0000</u>
ROOF LIVE LOAD:	<u>20.00</u>	PSF	WIND EXPOSURE:	<u>C</u>
ROOF SNOW LOAD:	<u>7.00</u>	PSF	INTERNAL PRESSURE COEFF.:	
GROUND SNOW LOAD:	<u>10</u>	PSF	<u>0.18</u> / <u>−0.18</u>	
BASIC WIND SPEED:	<u>110</u>	MPH	SPECTRAL RESPONSE COEFF.	MAPPED SPECTRAL RESPONSE ACC.
SEISMIC ZONE:	<u>C</u>		Sds	<u>0.33</u> Ss <u>0.32</u>
THERMAL FACTOR:	<u>1.00</u>		Sd1	<u>0.13</u> St <u>0.08</u>
IMPORTANCE FACTORS:			DESIGN BASE SHEAR, V:	
WIND LOAD	<u>1.00</u>		EXPANDED FORMULA	<u>0.667*le*Sms*W/R</u>
SNOW LOAD	<u>1.0000</u>		LONGITUDINAL	<u>20.77</u>
SEISMIC LOAD	<u>1.00</u>		TRANSVERSE	<u>20.22</u>

GENERAL NOTES:

1) MATERIALS : MINIMUM YIELD:
HOT ROLLED BAR $F_y = 50.0000$ ksi MIN.
STRUCTURAL STEEL SHEET $F_y = 50.0000$ ksi MIN.
STRUCTURAL STEEL PLATE $F_y = 50.0000$ ksi MIN.
COLD FORMED SHAPES $F_y = 55.0000$ ksi MIN.
WALL SHEETING $F_y = 60.0000$ ksi MIN.
ROOF SHEETING $F_y = 60.0000$ ksi MIN.
BOLTS A307 & A325
THE METAL BUILDING MANUFACTURER RESERVES THE RIGHT TO
SUBSTITUTE THE ABOVE MATERIALS WITH EQUAL OR BETTER MATERIAL.

2) BOLT TIGHTENING REQUIREMENTS:
ALL HIGH STRENGTH BOLTS ARE A325 UNLESS NOTED OTHERWISE.
HIGH STRENGTH BOLTS SHALL BE TIGHTENED BY THE TURN OF THE NUT METHOD
IN ACCORDANCE WITH THE LATEST EDITION AISC "SPECIFICATION FOR
STRUCTURAL JOINTS USING ASTM A325 OR A490 BOLTS". A325 BOLTS SHALL BE
INSTALLED WITH OUT WASHERS WHEN TIGHTENED BY THE "TURN OF THE NUT"
METHOD. ALL BOLTED CONNECTIONS, FOR SHEAR/BEARING CONNECTION TYPE
WITH BOLT THREADS EXCLUDED FROM THE SHEAR PLANE SHALL BE SNUG TIGHT
ONLY.

3) ALL STRUCTUAL STEEL TO RECEIVE A RUST INHIBITIVE PRIMER. THIS PAINT
IS NOT INTENDED FOR LONG TERM EXPOSURE TO THE ELEMENTS.

BUILDER / CONTRACTOR RESPONSIBILITIES

IT IS THE RESPONSIBILITY OF THE BUILDER/CONTRACTOR TO INSURE THAT ALL PROJECT
PLANS AND SPECIFICATIONS COMPLY WITH THE APPLICABLE REQUIREMENTS OF ANY
GOVERNING BUILDING AUTHORITIES. THE SUPPLYING OF SEALED ENGINEERING DATA AND
DRAWINGS FOR THE METAL BUILDING SYSTEM DOES NOT IMPLY OR CONSTITUTE AN
AGREEMENT THAT THE METAL BUILDING SYSTEM MANUFACTURER OR ITS DESIGN ENGINEER
IS ACTING AS THE ENGINEER OF RECORD OR DESIGN PROFESSIONAL FOR A CONSTRUCTION
PROJECT.

THE CONTRACTOR MUST SECURE ALL REQUIRED APPROVALS AND PERMITS FROM THE
APPROPRIATE AGENCY AS REQUIRED. APPROVAL OF THE METAL BUILDING SYSTEM
MANUFACTURER'S DRAWINGS AND CALCULATIONS INDICATE THAT THE METAL BUILDING
SYSTEM MANUFACTURER CORRECTLY INTERPRETED AND APPLIED THE REQUIREMENTS OF THE
CONTRACT DRAWINGS AND SPECIFICATIONS. (SECT. 4.2.1 AISC CODE OF STANDARD
PRACTICES, 9TH ED.) WHERE DISCREPANCIES EXIST BETWEEN THE METAL BUILDING SYSTEM
MANUFACTURER'S STRUCTURAL STEEL PLANS AND THE PLANS FOR OTHER TRADES, THE
STRUCTURAL STEEL PLANS SHALL GOVERN. (SECT. 3.3 AISC CODE OF STANDARD PRACTICE
9TH ED.)

DESIGN CONSIDERATIONS OF ANY MATERIALS IN THE STRUCTURE WHICH ARE NOT
FURNISHED BY THE METAL BUILDING SYSTEM MANUFACTURER ARE THE RESPONSIBILITY OF
THE CONTRACTORS AND ENGINEERS OTHER THAN THE METAL BUILDING SYSTEM
MANUFACTURER'S ENGINEER UNLESS SPECIFICALLY INDICATED.

THE CONTRACTOR IS RESPONSIBLE FOR ALL ERECTION OF STEEL AND ASSOCIATED WORK
IN COMPLIANCE WITH THE METAL BUILDING SYSTEM MANUFACTURER "FOR CONSTRUCTION"
DRAWINGS.

ALL BRACING AS SHOWN AND PROVIDED BY THE METAL BUILDING SYSTEM
MANUFACTURER FOR THIS BUILDING IS REQUIRED AND SHALL BE INSTALLED BY THE
ERECTOR AS A PERMANENT PART OF THE STRUCTURE.

TEMPORARY SUPPORTS, SUCH AS TEMPORARY GUYS, BRACES, FALSE WORK, CRIBBING
OR OTHER ELEMENTS REQUIRED FOR THE ERECTION OPERATION WILL BE DETERMINED AND
FURNISHED AND INSTALLED BY THE ERECTOR. THESE TEMPORARY SUPPORTS WILL SECURE
THE STEEL FRAMING, OR ANY PARTLY ASSEMBLED STEEL FRAMING, AGAINST LOADS
COMPARABLE IN INTENSITY TO THOSE FOR WHICH THE STRUCTURE WAS DESIGNED,
RESULTING FROM WIND, SEISMIC FORCES AND ERECTION OPERATIONS, BUT NOT THE LOADS
RESULTING FROM THE PERFORMANCE OF WORK BY OR THE ACTS OF OTHERS, NOR SUCH
UNPREDICTABLE LOADS AS THOSE DUE TO TORNADO, EXPLOSION, OR COLLISION. (SECT.
7.9.1 AISC CODE OF STANDARD PRACTICE, 9TH ED.)


WARNING: IN NO CASE SHOULD GALVALUME STEEL PANELS BE USED IN CONJUNCTION
WITH LEAD OR COPPER. BOTH LEAD AND COPPER HAVE HARMFUL CORROSION EFFECTS ON
THE ALUMINUM ZINC ALLOY COATING WHEN THEY ARE USED IN CONTACT WITH GALVALUME
STEEL PANELS. EVEN RUN-OFF FROM COPPER FLASHING, WIRING, OR TUBING ONTO
GALVALUME SHOULD BE AVOIDED.

APPROVAL NOTES

THE FOLLOWING CONDITIONS APPLY IN THE EVENT THAT THESE DRAWINGS ARE USED AS
APPROVAL DRAWINGS: IT IS IMPERATIVE THAT ANY CHANGES TO THESE DRAWINGS BE MADE
IN CONTRASTING INK (PREFERABLY RED INK), HAVE ALL INSTANCES OF CHANGE CLEARLY
INDICATED, AND BE LEGIBLE AND UNAMBIGUOUS. A SIGNATURE AND DATE IS REQUIRED ON
ALL PAGES. MANUFACTURER RESERVES THE RIGHT TO RE-SUBMIT DRAWINGS WITH
EXTENSIVE OR COMPLEX CHANGES REQUIRED TO AVOID MISFABRICATION. THIS MAY IMPACT
THE DELIVERY SCHEDULE. APPROVAL OF THESE DRAWINGS INDICATES CONCLUSIVELY THAT
THE METAL BUILDING SYSTEM MANUFAACTURER HAS CORRECTLY INTERPRETED THE
CONTRACT REQUIREMENTS, AND FURTHER CONSTITUTES AGREEMENT THAT THE BUILDING AS
DRAWN WITH INDICATED CHANGES REPRESENTS THE TOTAL OF THE MATERIALS TO BE
SUPPLIED BY MANUFACTURER. ANY CHANGES NOTED ON THHE DRAWINGS NOT IN
COMFORMANCE WITH THE TERMS AND REQUIREMENTS OF THE CONTRACT BETWEEN
MANUFACTURER AND ITS CUSTOMER ARE NOT BINDING ON MANUFACTURER UNLESS
SUBSEQUENTLY SPECIFICALLY ACKNOWLEDGED AND AGREED TO IN WRITING BY CHANGE
ORDER OR SEPARATE DOCUMENTATION. MANUFACTURER RECONGNIZES THAT RUBBER
STAMPS ARE ROUTINELY USED FOR INDICATING APPROVAL, DISAPPROVAL, REJECTION, OR
MERE REVIEW OF THE DRAWINGS SUBMITTED. HOWEVER, MANUFACTURER DOES NOT ACCEPT
CHANGES OR ADDITIONS TO CONTRACTURAL TERMS AND CONDITIONS THAT MAY APPEAR
WITH USE OF A STAMP OR SIMILIAR INDICATIOIN OF APPROVAL, DISAPPROVAL, ETC. SUCH
LANGUAGE APPLIED TO MANUFACTURER'S DRAWINGS BY THE CUSTOMER, ARCHITECT,
ENGINEER, OR ANY OTHER PARTY WILL BE CONSIDERED AS UNACCEPTABLE ALTERNATIONS
TO THESE DRAWING NOTES, AND WILL NOT ALTER THE CONTRACTUAL RIGHTS AND
OBLIGATIONS EXISTING BETWEEN MANUFACTURER AND ITS CUSTOMER.


IMPORTANT NOTE: FINAL DETAILING, FABRICATION, AND DELIVERY DATE OF THIS PROJECT
CANNOT BE COMPLETED UNTIL THE SIGNED APPROVALS ARE RETURNED TO THE METAL
BUILDING MANUFACTURER.

			PURCHASER: CUSTOMER PROJECT: BRANDON CUTTS JOB NUMBER: Q25−0843B
	.././..	FOR CONSTRUCTION	
	.././..	FOR APPROVAL	
REV.	DATE	REVISION	

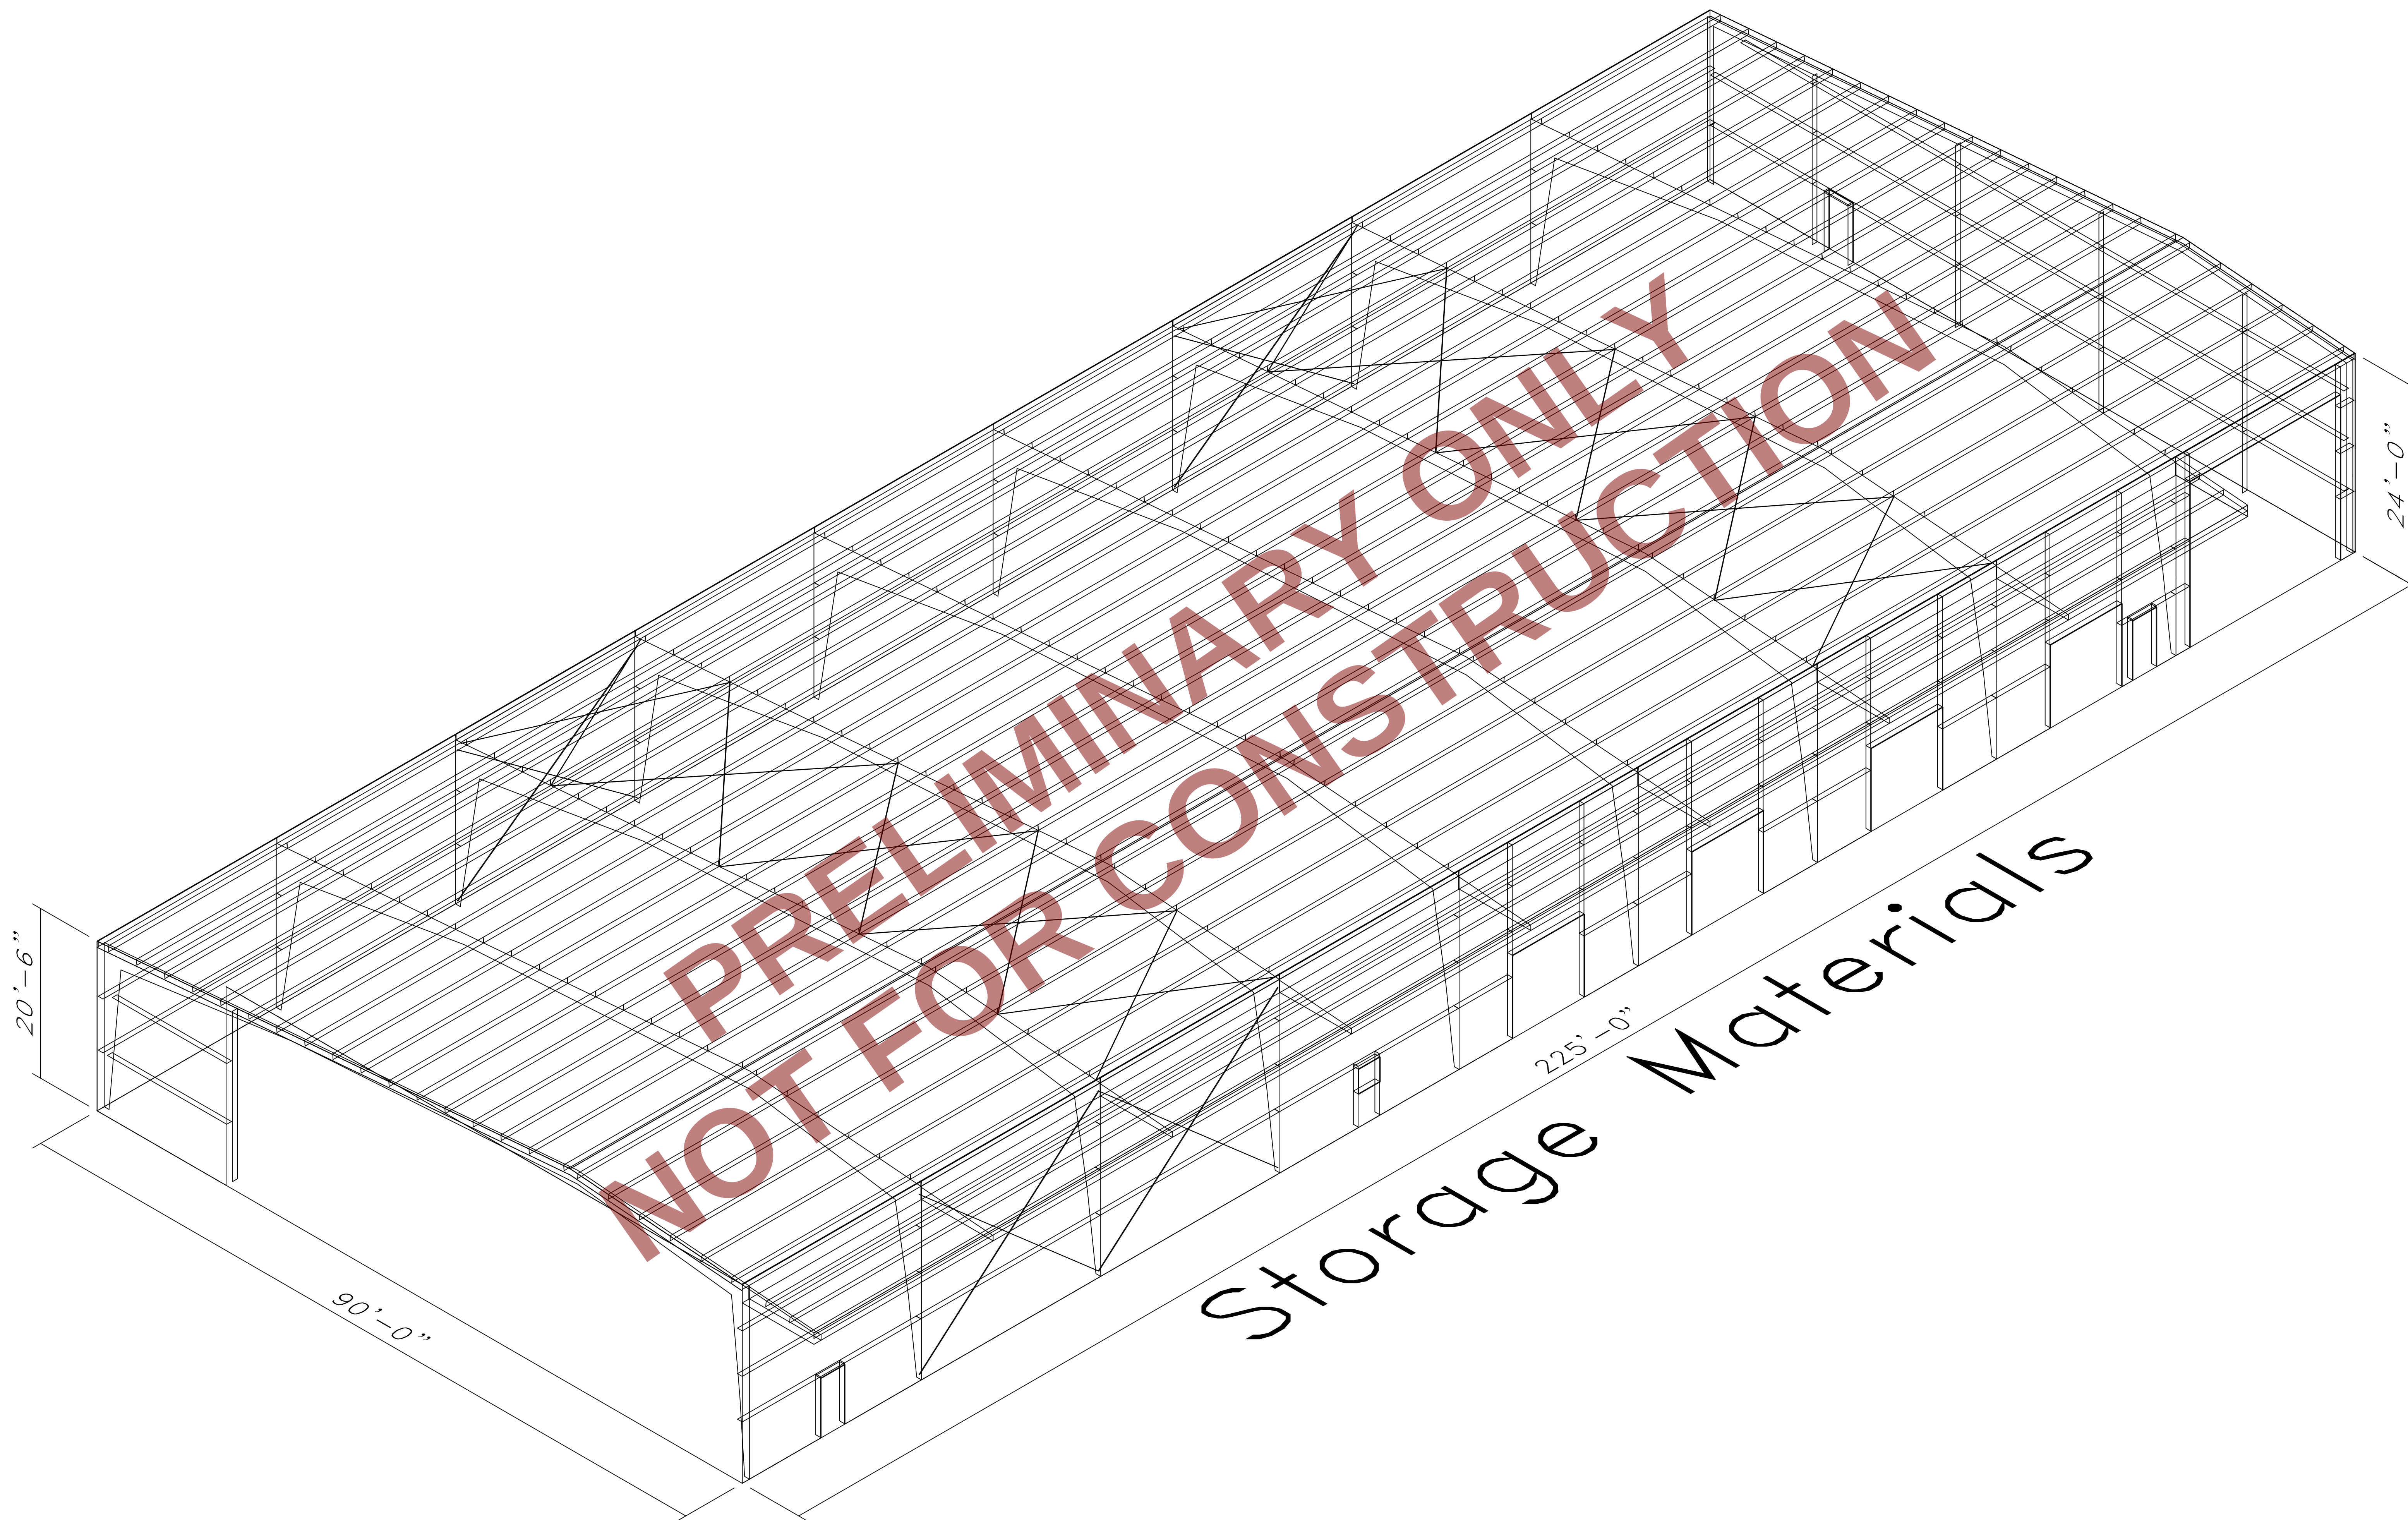

PRELIMINARY ONLY
NOT FOR CONSTRUCTION

Storage Materials











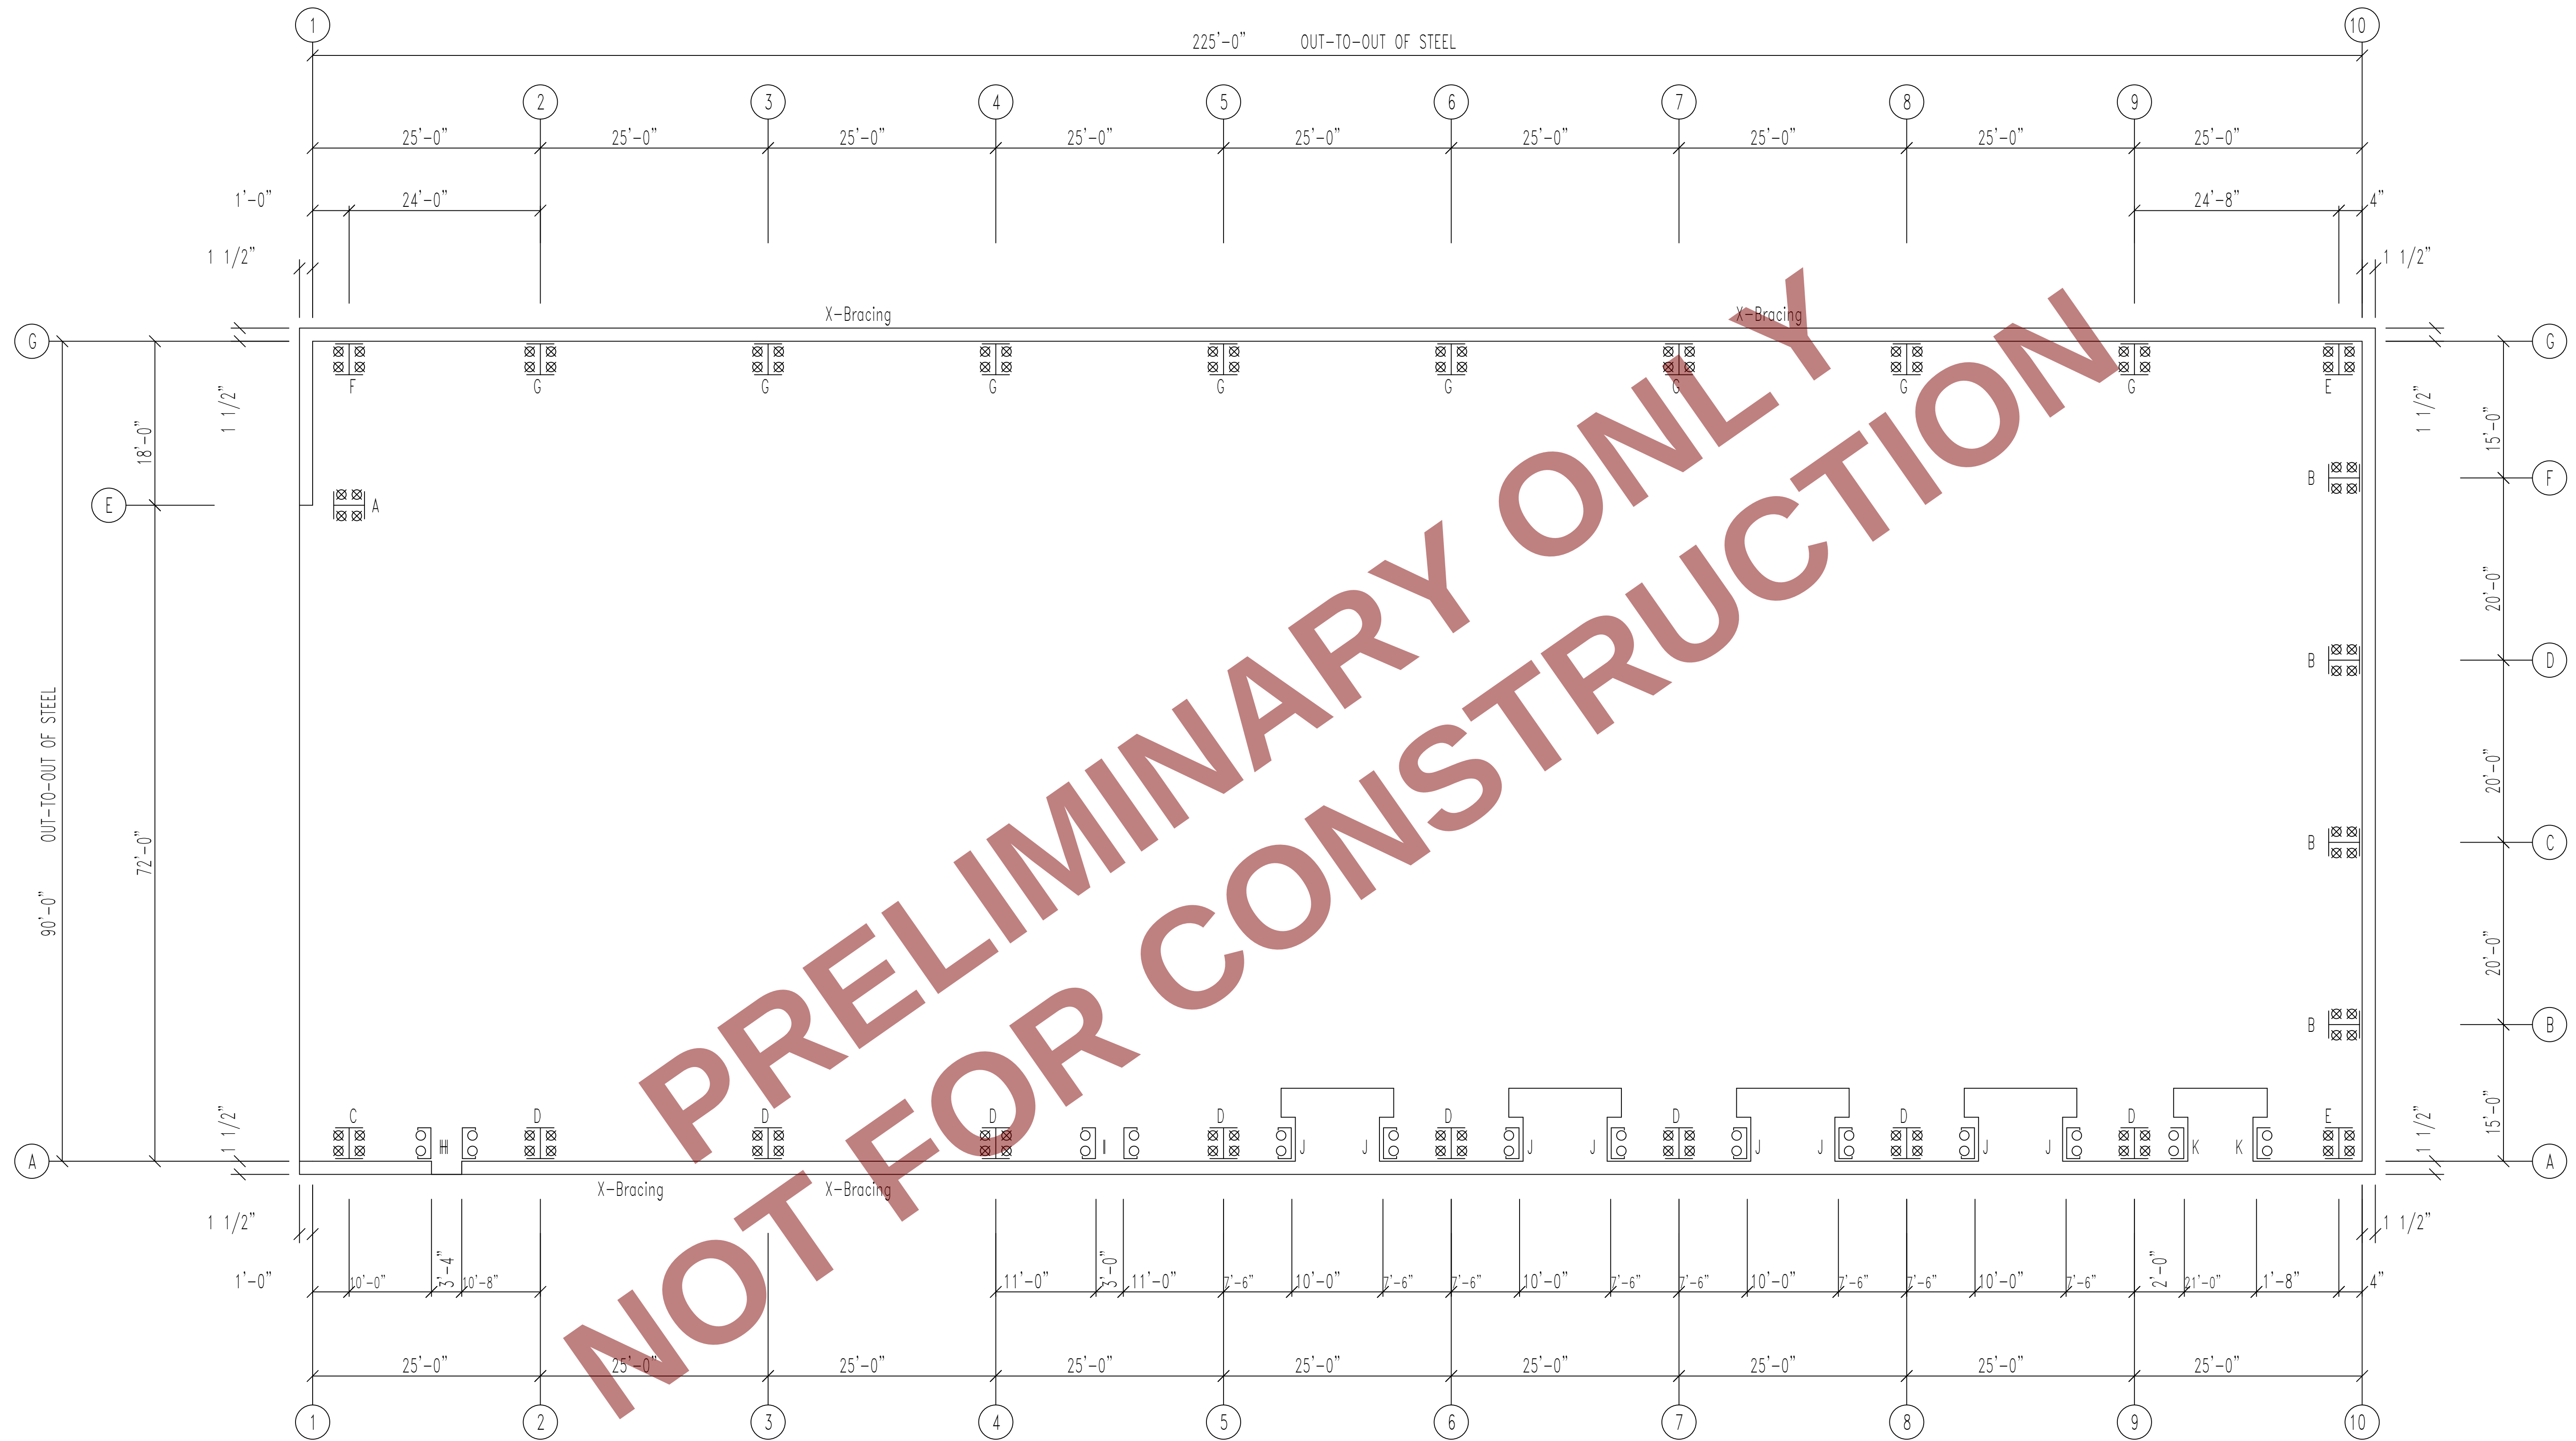


ANCHOR BOLT PLAN
NOTE: All Base Plates @ 100'-0" (U.N.)

STORAGE MATERIALS

1851 Madison Avenue #300 Council Bluffs, IA 51503
(888) 968-1222 <https://storagematerials.com>

DESCRIPTION: ANCHOR BOLT PLAN						
CUSTOMER: CUSTOMER				PROJECT: BRANDON CUTTS		
LOCATION:						
DRN. BY ART	CK'D BY AER	DATE 3/ 3/26	SCALE N.T.S.	REV. 00	QUOTATION NO. Q25-0843B	SHEET NO. OF

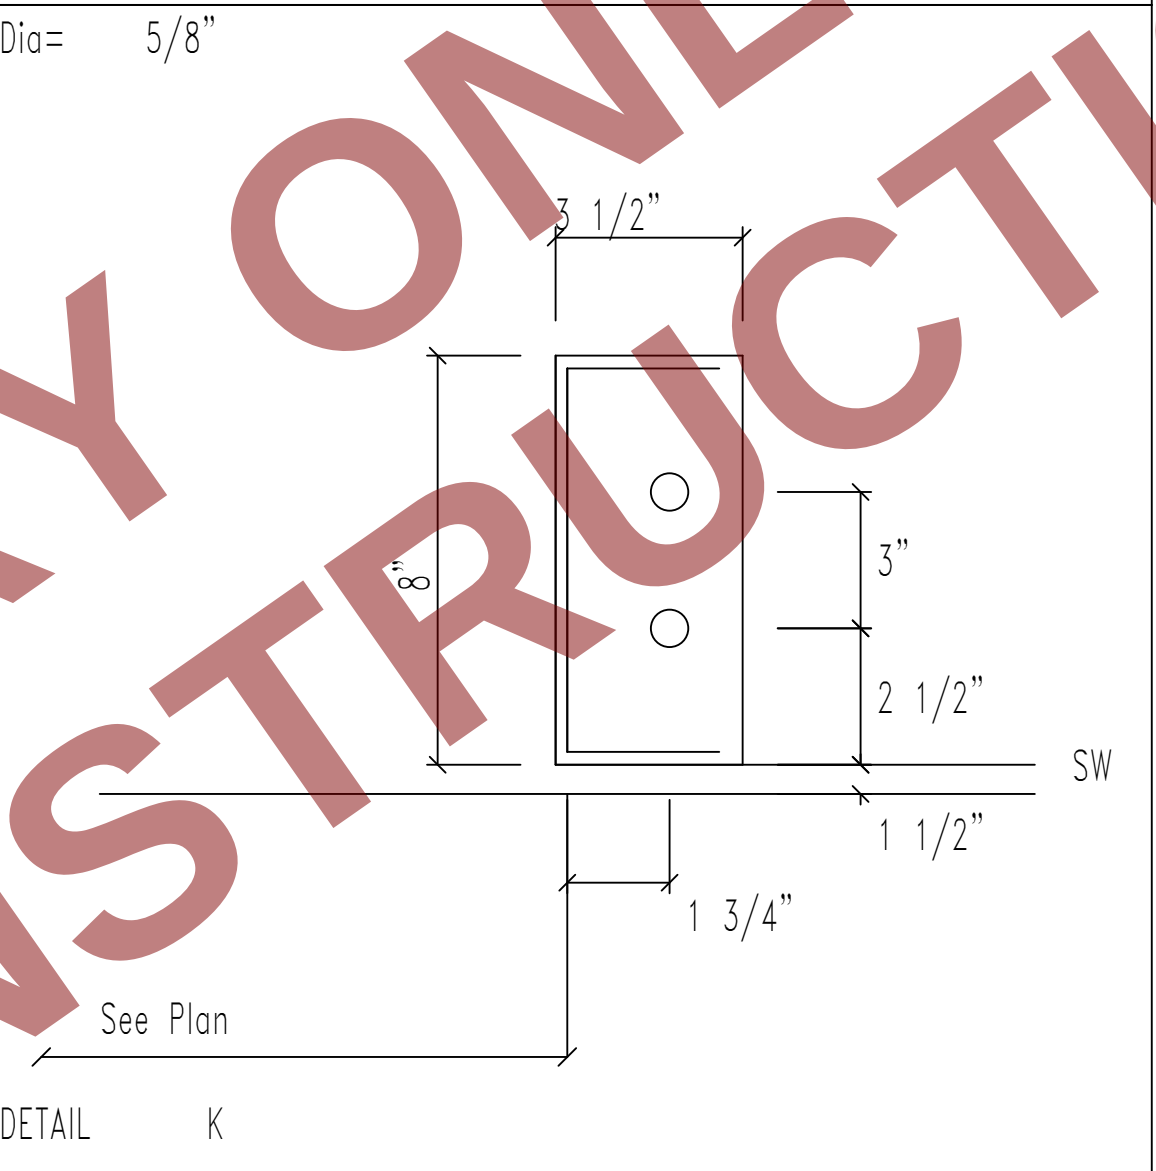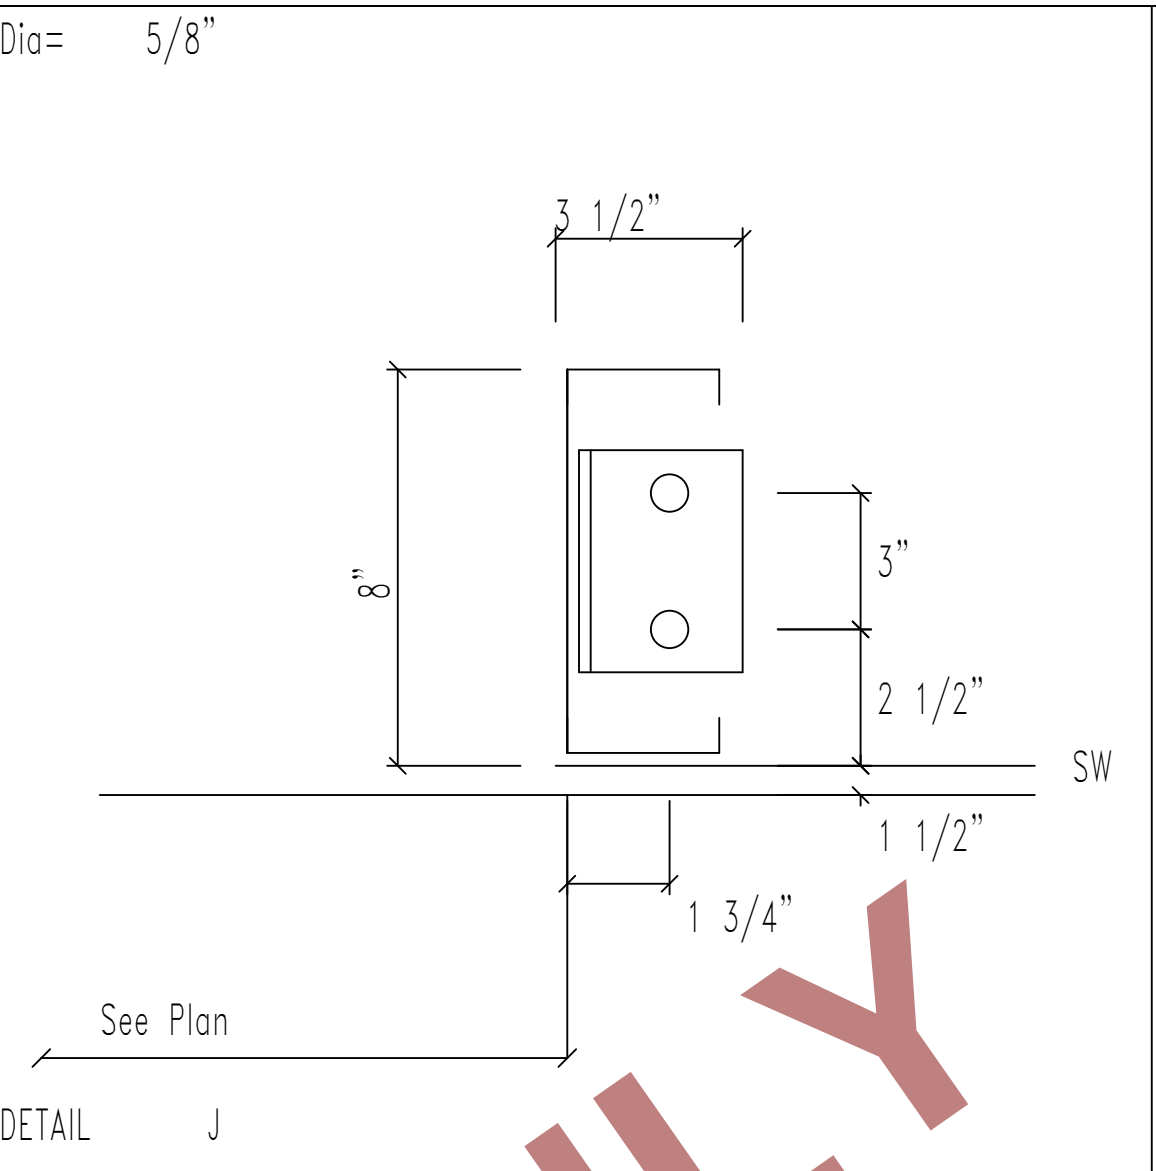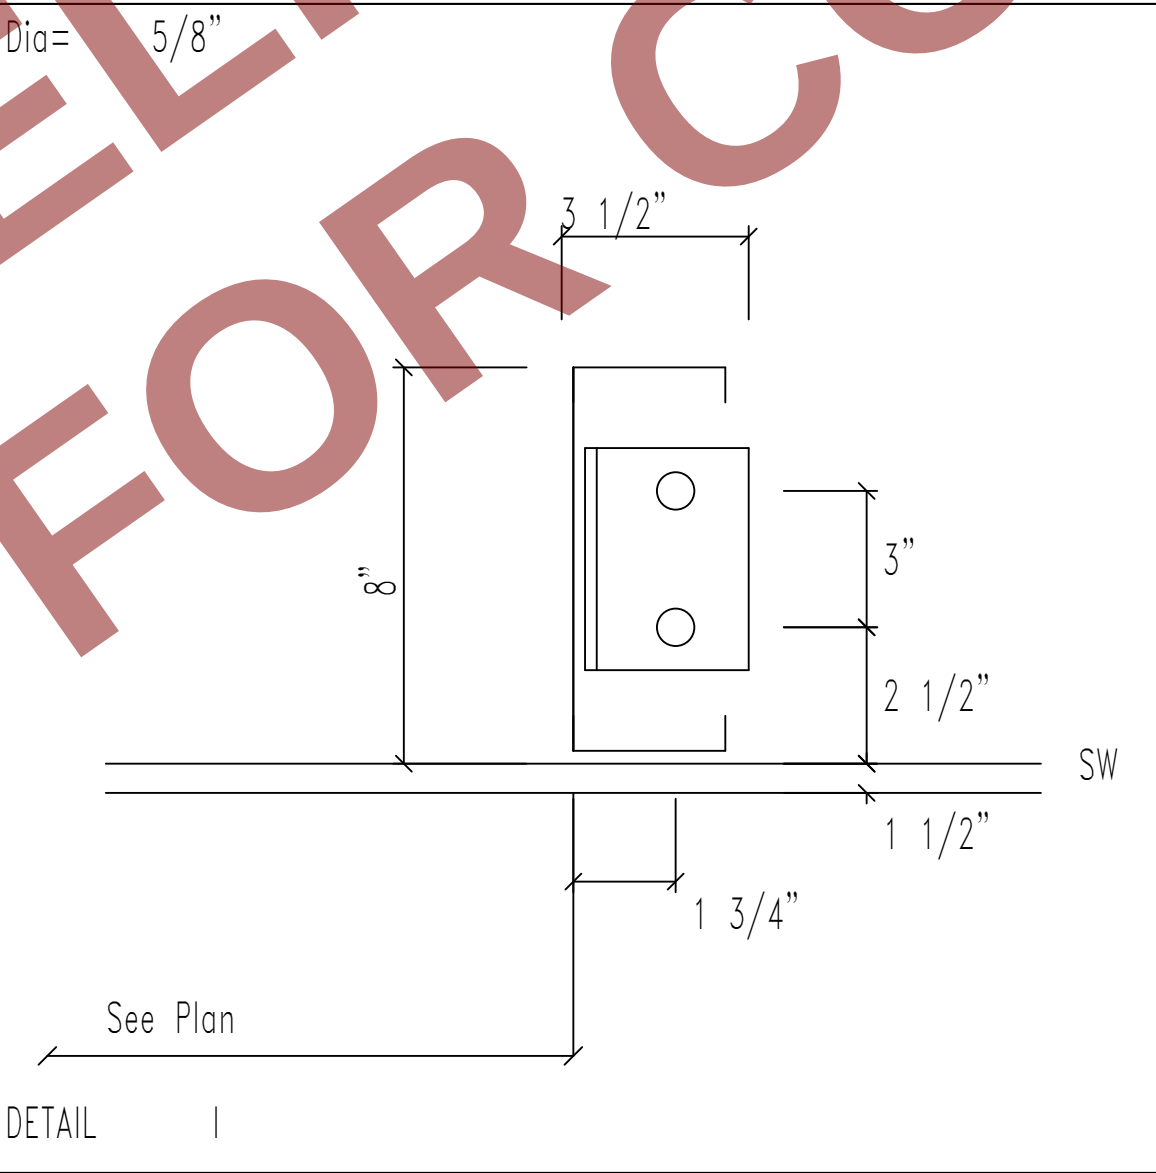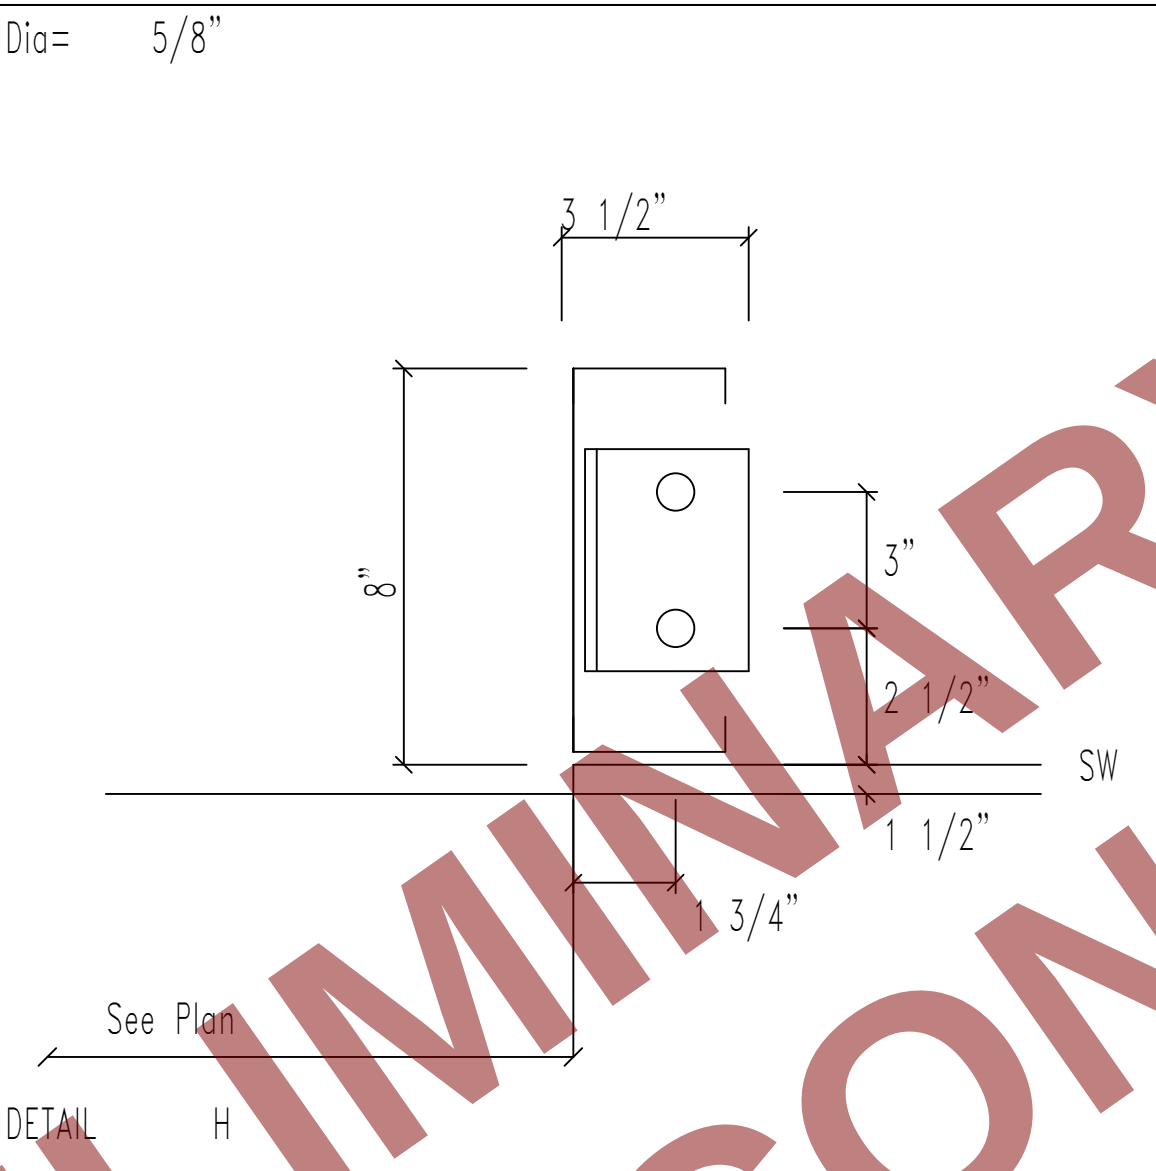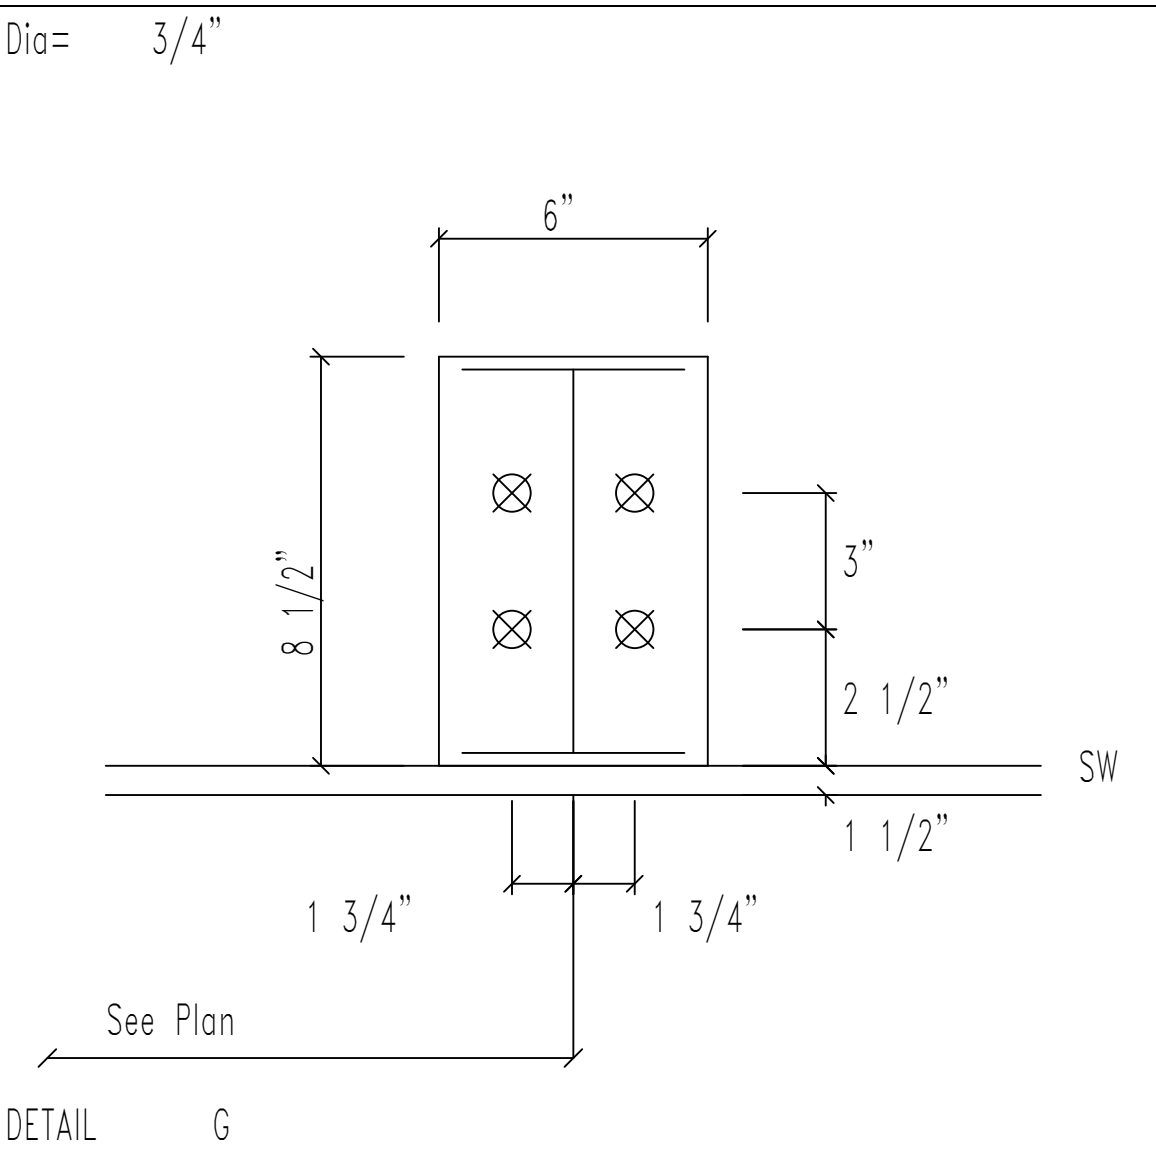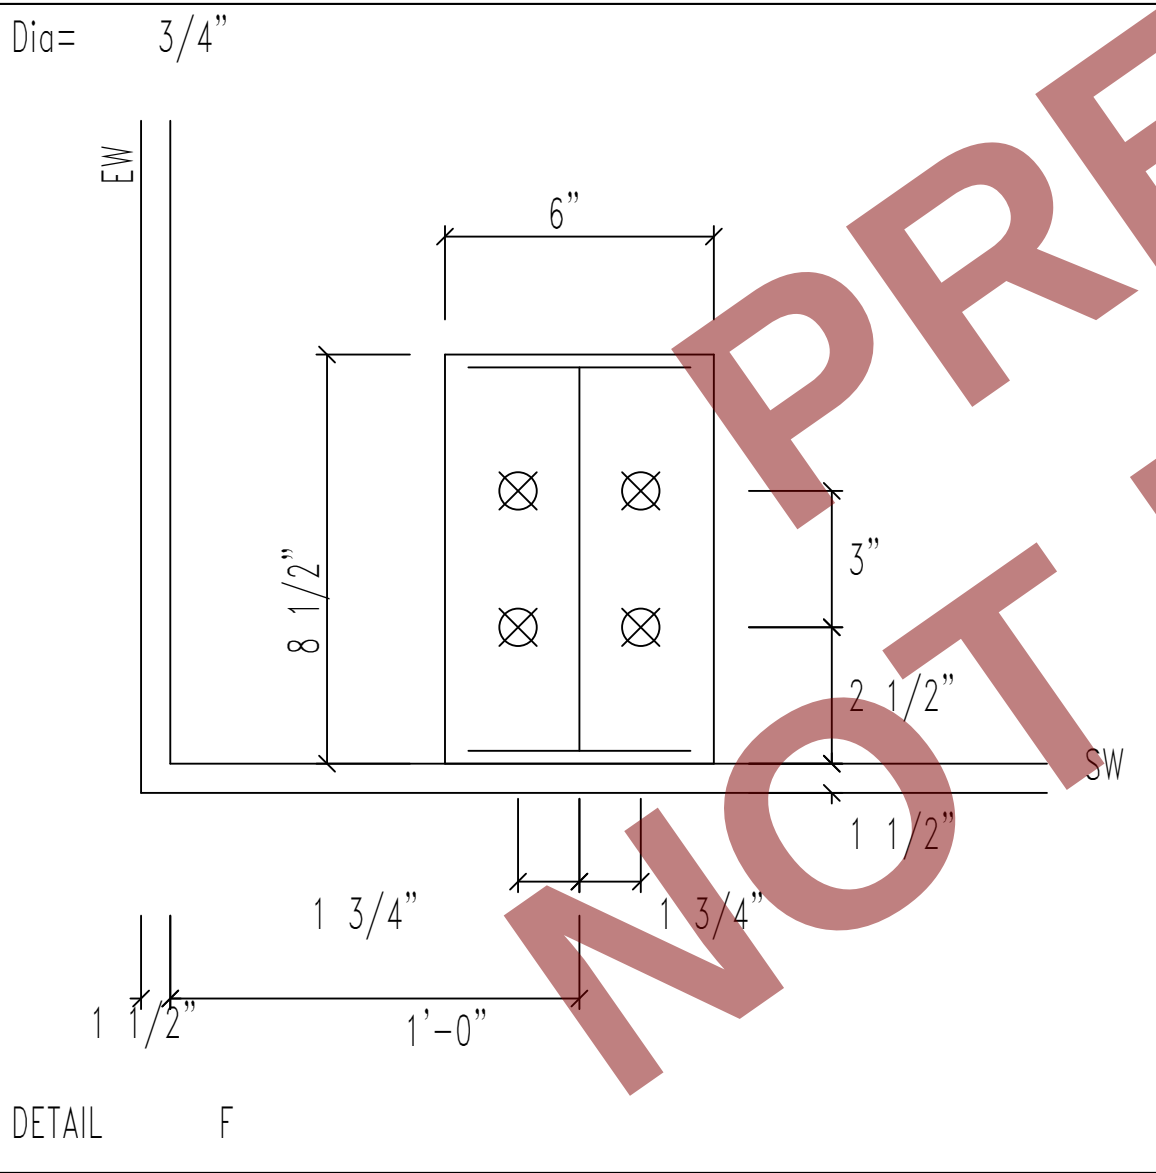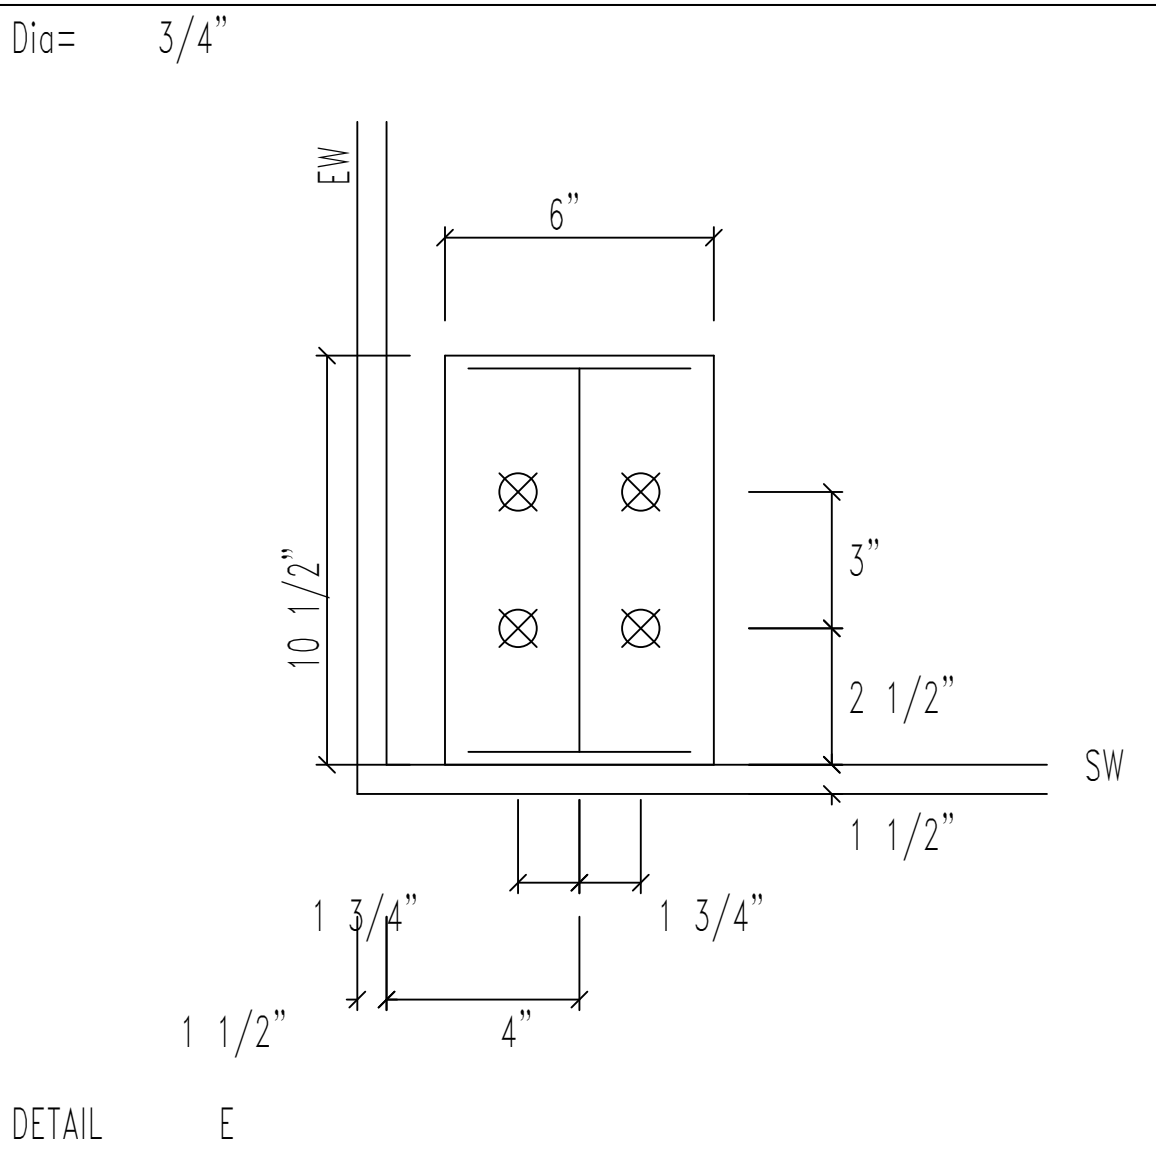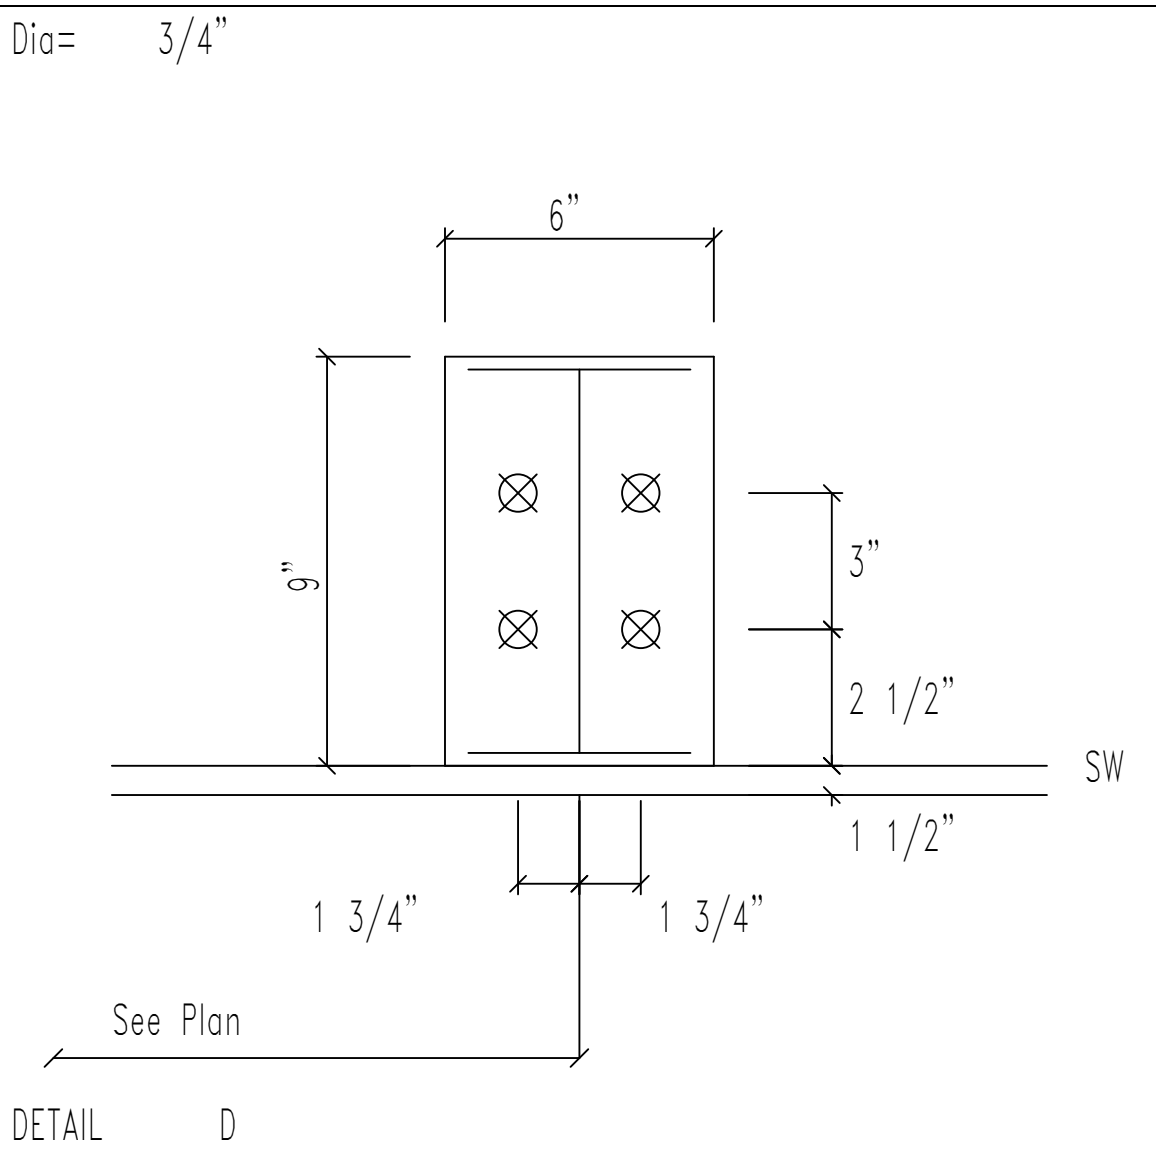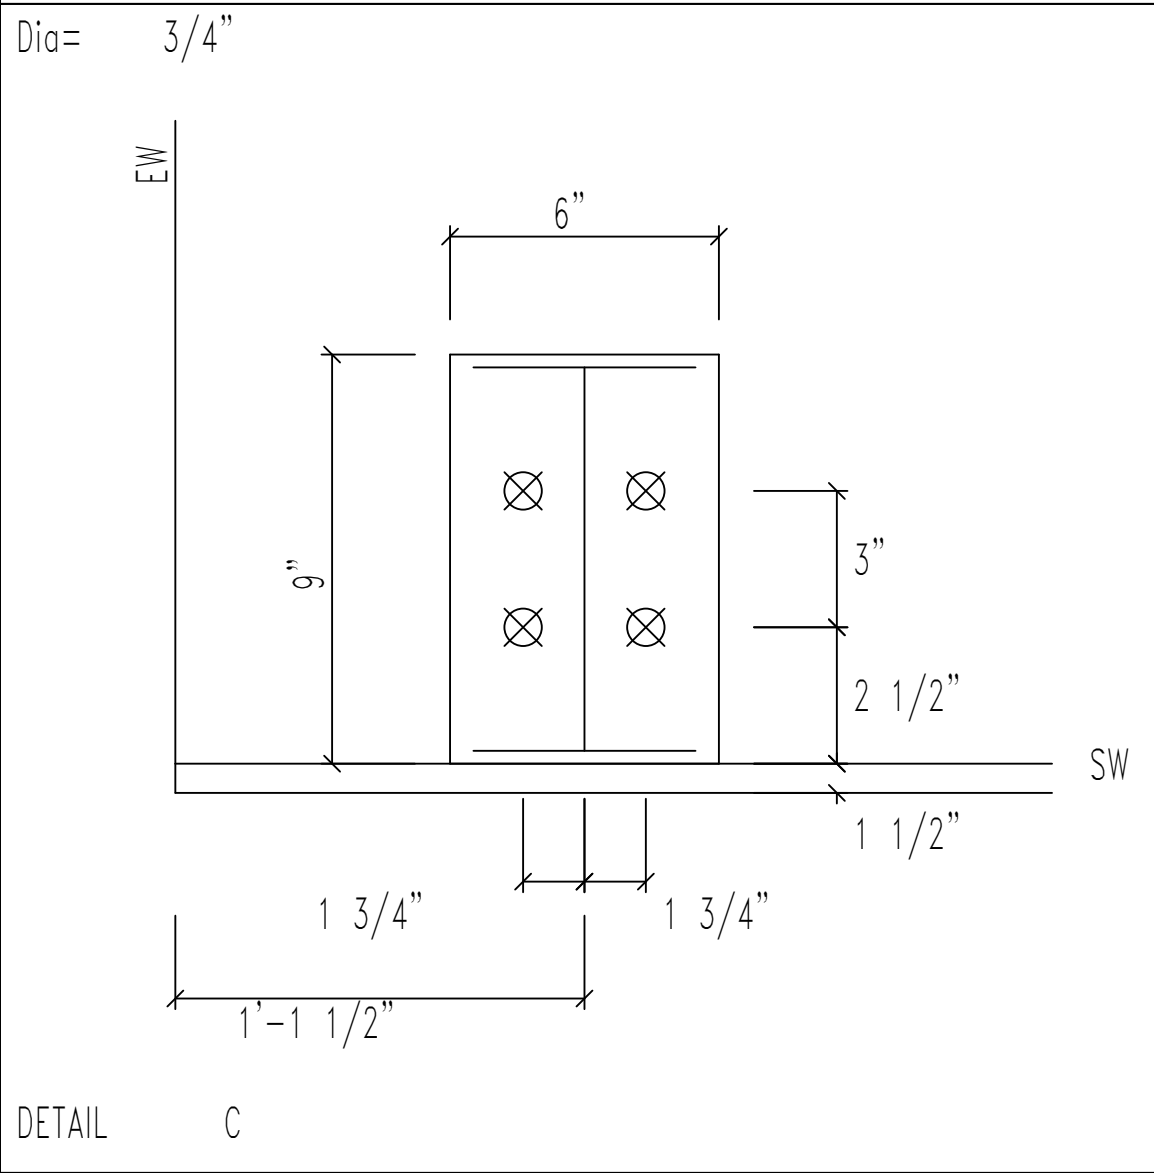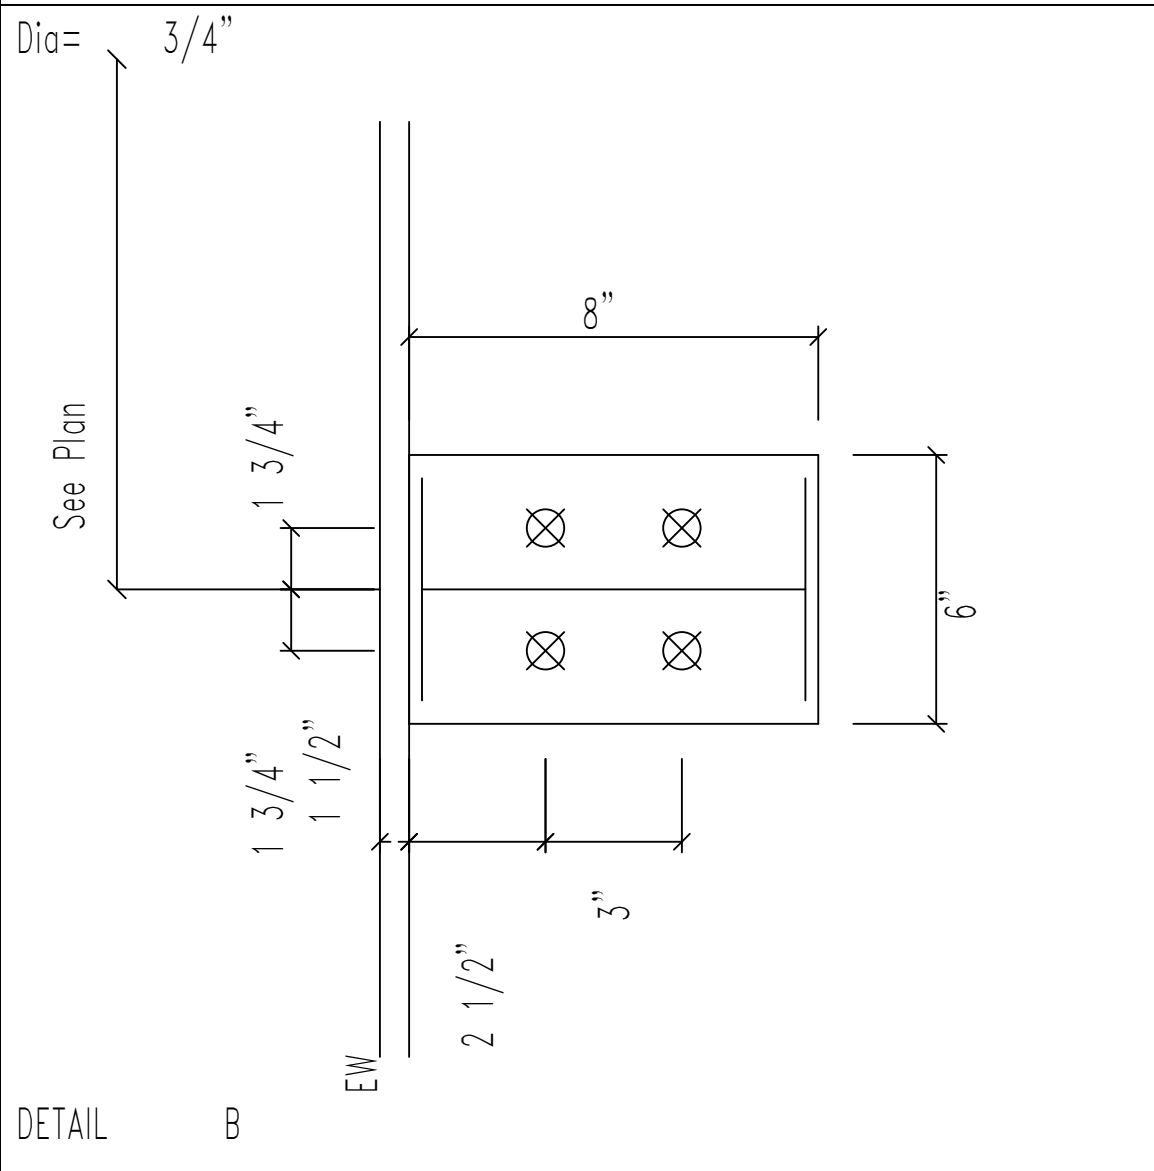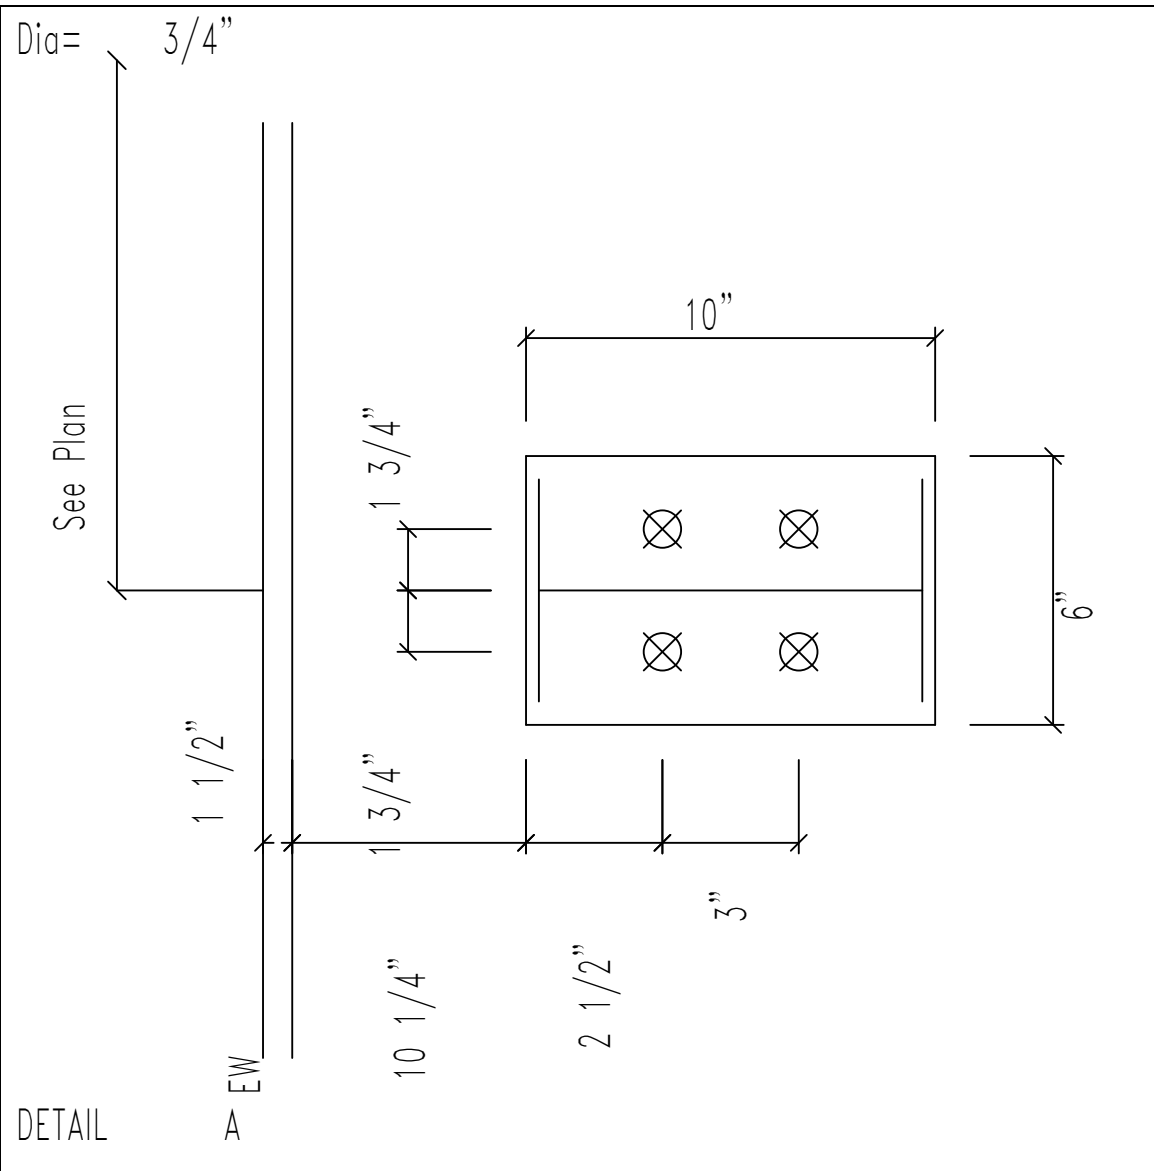

DESCRIPTION:

ANCHOR BOLT DETAILS						
CUSTOMER: CUSTOMER					PROJECT: BRANDON CUTTS	
LOCATION:						
DRN. BY	CK'D BY	DATE	SCALE	REV.	QUOTATION NO.	SHEET NO.
ART	AER	3/ 3/26	N.T.S.	00	Q25-0843B	OF

NOTES FOR REACTIONS

- All loading conditions are examined and only maximum/minimum H or V and the corresponding H or V are reported.
- Positive reactions are as shown in the sketch. Foundation loads are in opposite directions.
- Bracing reactions are in the plane of the brace with the H pointing away from the braced bay. The vertical reaction is downward.
- Building reactions are based on the following building data:

Width	(ft)	=	90.0
Length	(ft)	=	225.0
Eave Height	(ft)	=	20.5/ 24.0
Roof Slope	(rise/12)	=	1.00/ 1.00
Roof Dead Load	(psf)	=	2.5
Wall Dead Load			
Left Endwall	(psf)	=	2.0
Right Endwall	(psf)	=	2.0
Front Sidewall	(psf)	=	2.0
Back Sidewall	(psf)	=	2.0
Roof Live Load	(psf)	=	20.0
Frame Live Load	(psf)	=	12.0
Collateral Load	(psf)	=	3.0
Snow Load	(psf)	=	7.0
Minimum Snow	(psf)	=	10.0
Wind Speed	(mph)	=	110.0
Wind Code		=	IBC 18
Exposure		=	C
Closure		=	Enclosed
Internal Wind Coeff		=	-0.18, +0.18
Risk Category		=	II - Normal
Importance - Wind		=	1.00
Importance - Seismic		=	1.00
Seismic Design Category		=	C
Seismic Coeff	(Sms)	=	0.50

5. Loading conditions are:

- Dead+Collateral+Live
- Dead+Collateral+0.75Live+0.45Wind_Right2
- Dead+Collateral+0.75Live+0.45Wind_Long1R
- Dead+Collateral+0.75Live+0.45Wind_Long2L
- Dead+Collateral+0.75Snow+0.45Wind_Left1
- Dead+Collateral+0.75Snow+0.45Wind_Left1+0.75Snow_Drift
- Dead+Collateral+0.75Snow+0.45Wind_Left1+0.75Slide_Snow
- 0.6Dead+0.6Wind_Left1
- 0.6Dead+0.6Wind_Right1
- 0.6Dead+0.6Wind_Left2
- 0.6Dead+0.6Wind_Right2
- 0.6Dead+0.6Wind_Long1L
- 0.6Dead+0.6Wind_Long1R
- 0.6Dead+0.6Wind_Long2R
- 1.03Dead+1.03Collateral+0.52Seismic_LongR
- Dead+Collateral+F3UNB_SL_R
- Dead+Collateral+F3PAT_LL_1
- Dead+Collateral+F3PAT_LL_2
- Dead+Collateral+F3PAT_LL_3
- Dead+Collateral+F3PAT_LL_5
- 0.6Dead+0.6Wind_Right2+0.6Wind_Suction
- 0.6Dead+0.6Wind_Pressure+0.6Wind_Long2L
- 0.6Dead+0.6Wind_Left1+0.6Wind_Suction
- 0.6Dead+0.6Wind_Pressure+0.6Wind_Long1L
- 0.6Dead+0.6Wind_Suction+0.6Wind_Long2L
- 0.6Dead+0.6Wind_Right1+0.6Wind_Suction

RIGID FRAME:

BASIC COLUMN REACTIONS (k)

Frame Line	Column Line	-----Dead-----	--Collateral--	-----Live-----	-----Snow-----	--Wind_Left1--	--Wind_Right1--
1	G	Horz 1.7 Vert 2.7	Horz 1.3 Vert 1.7	Horz 5.0 Vert 6.9	Horz 3.0 Vert 4.0	Horz -12.9 Vert -13.9	Horz -3.9 Vert -9.0
1	A	Horz -1.7 Vert 3.7	Horz 1.3 Vert 2.6	Horz -5.0 Vert 9.8	Horz -3.0 Vert 5.1	Horz 7.2 Vert -13.0	Horz 10.7 Vert -19.4

Frame Line	Column Line	--Wind_Left2--	--Wind_Right2--	--Wind_Long1--	--Wind_Long2--	--Seismic_Left--	Seismic_Right
1	G	Horz -10.4 Vert -10.9	Horz -1.4 Vert -4.0	Horz -9.4 Vert -16.4	Horz -6.1 Vert -10.3	Horz -0.7 Vert -0.3	Horz 0.7 Vert 0.3
1	A	Horz 4.7 Vert -8.1	Horz 8.1 Vert -14.4	Horz 10.4 Vert -14.0	Horz 5.8 Vert -13.1	Horz -0.7 Vert 0.3	Horz 0.7 Vert -0.3

Frame Line	Column Line	--MIN_SNOW--	F1UNB_SL_L--	F1UNB_SL_R--
1	G	Horz 4.3 Vert 5.8	Horz 3.3 Vert 4.2	Horz 1.7 Vert 1.7
1	A	Horz -4.3 Vert 7.2	Horz -3.3 Vert 3.8	Horz -1.7 Vert 5.8

Frame Line	Column Line	-----Dead-----	--Collateral--	-----Live-----	-----Snow-----	--Wind_Left1--	--Wind_Right1--
2*	G	Horz 3.1 Vert 4.6	Horz 2.5 Vert 3.3	Horz 10.2 Vert 13.2	Horz 6.0 Vert 7.8	Horz -19.1 Vert -22.3	Horz -6.5 Vert -13.5
2*	A	Horz -3.1 Vert 6.3	Horz -2.5 Vert 5.0	Horz -10.2 Vert 18.8	Horz -6.0 Vert 9.7	Horz 9.4 Vert -18.5	Horz 15.4 Vert -28.2

Frame Line	Column Line	--Wind_Left2--	--Wind_Right2--	--Wind_Long1--	--Wind_Long2--	--Seismic_Left--	Seismic_Right
2*	G	Horz -14.5 Vert -12.8	Horz -1.3 Vert -4.0	Horz -19.3 Vert -34.6	Horz -12.5 Vert -23.0	Horz -1.1 Vert -0.5	Horz 1.1 Vert 0.5
2*	A	Horz 4.8 Vert -9.0	Horz 10.2 Vert -18.6	Horz 21.1 Vert -32.5	Horz 12.0 Vert -30.9	Horz -1.1 Vert 0.5	Horz 1.1 Vert -0.5

Frame Line	Column Line	Seismic_Long1	Seismic_Long2	--MIN_SNOW--	F2UNB_SL_L--	F2UNB_SL_R--
2*	G	Horz 0.0 Vert -3.4	Horz 0.0 Vert 3.4	Horz 8.6 Vert 11.1	Horz 6.6 Vert 8.2	Horz 3.5 Vert 3.4
2*	A	Horz 0.0 Vert -5.2	Horz 0.0 Vert 5.2	Horz -8.6 Vert 13.9	Horz -6.6 Vert 7.3	Horz -3.5 Vert 11.2

Frame Line	Column Line	-----Dead-----	--Collateral--	-----Live-----	-----Snow-----	--Wind_Left1--	--Wind_Right1--
10	G	Horz 0.0 Vert 0.5	Horz 0.0 Vert 0.2	Horz 0.0 Vert 0.9	Horz 0.0 Vert 0.5	Horz -2.7 Vert -4.6	Horz 4.0 Vert 2.6
10	A	Horz 0.0 Vert 0.6	Horz 0.0 Vert 0.2	Horz 0.0 Vert 0.9	Horz 0.0 Vert 0.5	Horz -2.7 Vert -0.1	Horz 3.0 Vert -5.1
10	F	Horz 0.0 Vert 1.1	Horz 0.0 Vert 0.7	Horz 0.0 Vert 2.8	Horz 0.0 Vert 1.7	Horz 0.0 Vert -4.0	Horz 0.0 Vert -0.5
10	D	Horz 0.0 Vert 1.2	Horz 0.0 Vert 0.8	Horz 0.0 Vert 3.1	Horz 0.0 Vert 1.8	Horz 0.0 Vert -8.2	Horz 0.0 Vert -3.2
10	C	Horz 0.0 Vert 1.2	Horz 0.0 Vert 0.8	Horz 0.0 Vert 3.1	Horz 0.0 Vert 1.8	Horz 0.0 Vert -4.6	Horz 0.0 Vert -5.2
10	B	Horz 0.0 Vert 1.1	Horz 0.0 Vert 0.7	Horz 0.0 Vert 2.8	Horz 0.0 Vert 1.7	Horz 0.0 Vert -5.1	Horz 0.0 Vert -9.0

Frame Line	Column Line	--Wind_Left2--	--Wind_Right2--	--Wind_Press--	--Wind_Suct--	--Wind_Long1--	--Wind_Long2--
10	G	Horz -3.6 Vert -3.7	Horz 3.1 Vert 3.5	Horz 0.0 Vert 0.0	Horz 0.0 Vert 0.0	Horz 2.3 Vert 1.6	Horz 1.5 Vert -2.0
10	A	Horz -1.7 Vert 1.2	Horz 3.9 Vert -3.8	Horz 0.0 Vert 0.0	Horz 0.0 Vert 0.0	Horz -1.3 Vert -3.2	Horz -1.8 Vert -3.3
10	F	Horz 0.0 Vert -2.1	Horz 0.0 Vert -6.6	Horz -3.6a Vert 0.0	Horz 4.0a Vert 0.0	Horz 0.0 Vert -7.8	Horz 0.0 Vert -3.0
10	D	Horz 0.0 Vert -5.9	Horz 0.0 Vert -1.0	Horz -4.5a Vert 0.0	Horz 4.9a Vert 0.0	Horz 0.0 Vert -7.4	Horz 0.0 Vert -4.4
10	C	Horz 0.0 Vert -2.5	Horz 0.0 Vert -3.1	Horz -4.8a Vert 0.0	Horz 5.3a Vert 0.0	Horz 0.0 Vert -7.5	Horz 0.0 Vert -4.4
10	B	Horz 0.0 Vert -3.9	Horz 0.0 Vert -1.8	Horz -4.2a Vert 0.0	Horz 4.7a Vert 0.0	Horz 0.0 Vert -2.0	Horz 0.0 Vert -5.4

Frame Line	Column Line	--Seismic_Left	Seismic_Right	Seismic_Long1	--MIN_SNOW--	F3PAT_LL_1--	F3PAT_LL_2--
10	G	Horz -0.8 Vert -1.2	Horz 0.8 Vert 1.2	Horz 0.0 Vert 0.0	Horz -1.2 Vert 0.0	Horz 0.0 Vert 0.8	Horz 0.0 Vert -0.2
10	A	Horz -0.5 Vert 0.9	Horz -0.9 Vert 0.5	Horz 0.0 Vert 0.0	Horz 0.0 Vert 0.8	Horz 0.0 Vert 0.9	Horz 0.0 Vert 0.0
10	F	Horz 0.0 Vert 1.4	Horz 0.0 Vert -1.4	Horz 0.0 Vert 0.0	Horz 2.4 Vert 0.0	Horz 0.0 Vert 3.1	Horz 0.0 Vert 1.5
10	D	Horz 0.0 Vert -0.3	Horz 0.0 Vert 0.3	Horz 0.0 Vert 0.0	Horz 2.6 Vert 0.0	Horz 0.0 Vert 1.6	Horz 0.0 Vert 3.4
10	C	Horz 0.0 Vert 0.3	Horz 0.0 Vert -0.3	Horz 0.1a Vert 0.0	Horz 2.6 Vert 0.0	Horz 0.0 Vert -0.2	Horz 0.0 Vert 1.5
10	B	Horz 0.0 Vert -1.1	Horz 0.0 Vert 1.1	Horz 0.0a Vert 0.0	Horz 2.4 Vert 0.0	Horz 0.0 Vert 0.0	Horz 0.0 Vert -0.2

Frame Line	Column Line	F3PAT_LL_3--	F3PAT_LL_4--	F3PAT_LL_5--	F3PAT_LL_6--	F3UNB_SL_L--	F3UNB_SL_R--
10	G	Horz 0.0 Vert 0.0	Horz 0.0 Vert 0.0	Horz 0.1 Vert 1.2	Horz 0.0 Vert -0.3	Horz 0.0 Vert 0.5	Horz 0.0 Vert 0.2
10	A	Horz 0.0 Vert -0.2	Horz 0.0 Vert 0.8	Horz -0.1 Vert 1.2	Horz -0.3 Vert 0.0	Horz 0.1 Vert 0.0	Horz 0.0 Vert 0.9
10	F	Horz 0.0 Vert -0.2	Horz 0.0 Vert 0.0	Horz 0.0 Vert 0.9	Horz 1.9 Vert 0.0	Horz 1.7 Vert 0.5	Horz 0.0 Vert 0.5
10	D	Horz 0.0 Vert 1.6	Horz 0.0 Vert -0.2	Horz 0.0 Vert 1.6	Horz 0.0 Vert 1.5	Horz 0.0 Vert 1.7	Horz 0.0 Vert 0.5
10	C	Horz 0.0 Vert 3.4	Horz 0.0 Vert -4.6	Horz 0.0 Vert 1.6	Horz 0.0 Vert 2.2	Horz 0.0 Vert 2.2	Horz 0.0 Vert 0.8
10	B	Horz 0.0 Vert 1.5	Horz 0.0 Vert 3.1	Horz 0.0 Vert 0.9	Horz 1.9 Vert 0.0	Horz 0.0 Vert 0.9	Horz 0.0 Vert 3.5

2* Frame lines: 2 3 4 5 6 7 8 9

a - Out-Of-Plane Horizontal Load

ENDWALL COLUMN:

BASIC COLUMN REACTIONS (k)

Frame Line	Col Line	Dead	Wind Press	Wind Suct	Seis Long
1	E	Horz 0.2 Vert 2.3	Horz 2.5 Vert 0.0		

ENDWALL COLUMN:

MAXIMUM REACTIONS, ANCHOR BOLTS, & BASE PLATES

Frame Line	Col Line	Load Id	Column_Reactions(k)	Load Id	Hmin	V	Bolt(in)	Dia	Base_Plate(in)	Thick	Grout (in)
			Hmax Vmax		H	Vmin	Qty		Width	Length	
1	E	21 15	1.5 0.0	22	-1.4	0.1	4	0.750	6.000	10.00	0.250 0.0


BUILDING BRACING REACTIONS

Wall	Col	± Reactions(k)	Panel_Shear (lb/ft)	Note
Loc	Line	Wind Horz Vert	Seismic Horz Vert	
L_EW	1			(h)
F_SW	A	2.3 3.4	6.3 5.6	5.8 5.2
R_EW	10			(h)
B_SW	G	8.7 4.3	4.2 3.1	4.6 3.4


(h)Rigid frame at endwall

Reactions for seismic represent shear force, Eh
Reaction values shown are unfactored

FRAME LINES: 1 2 3 4 5 6 7 8 9

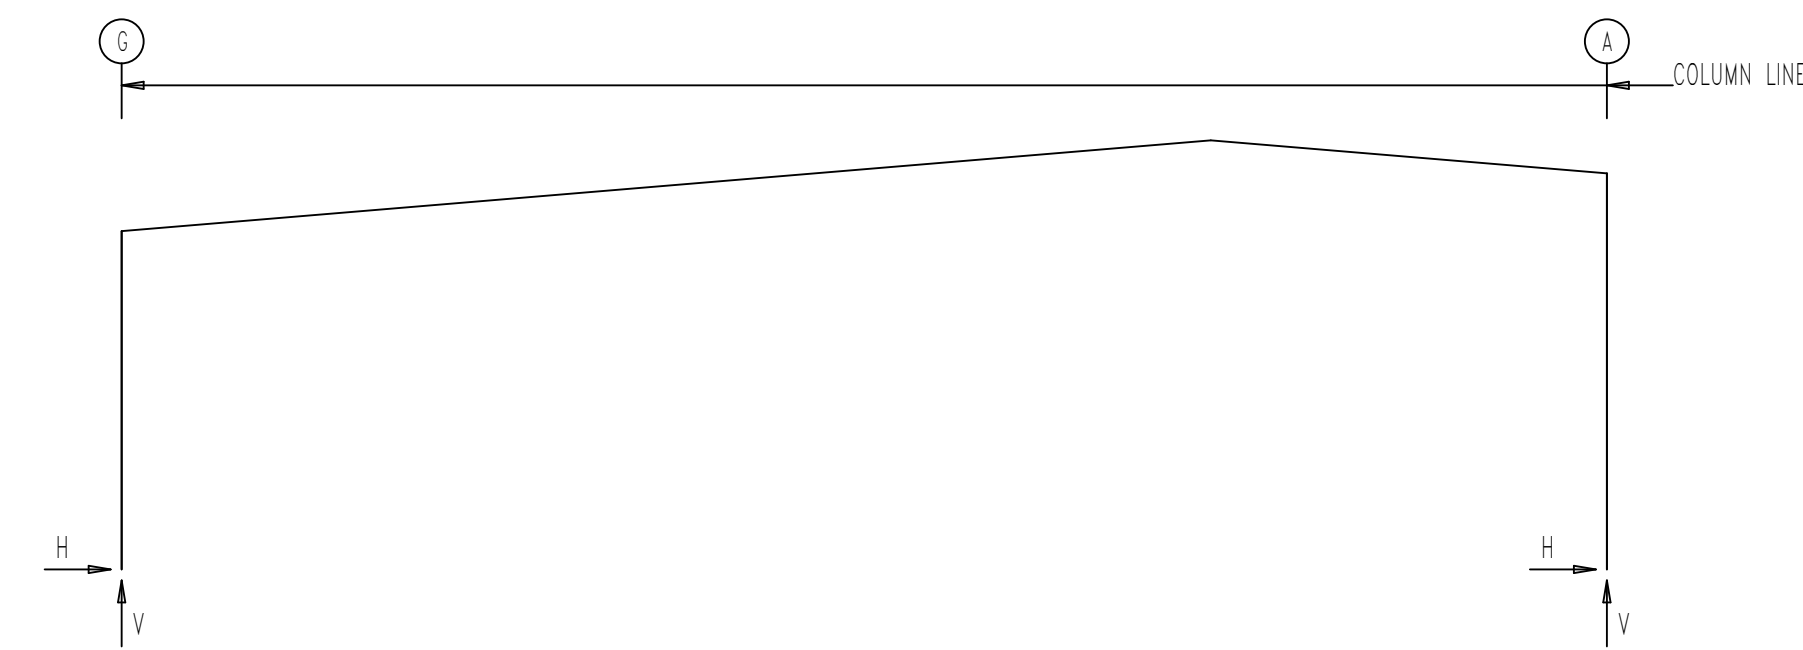

FRAME LINES: 10

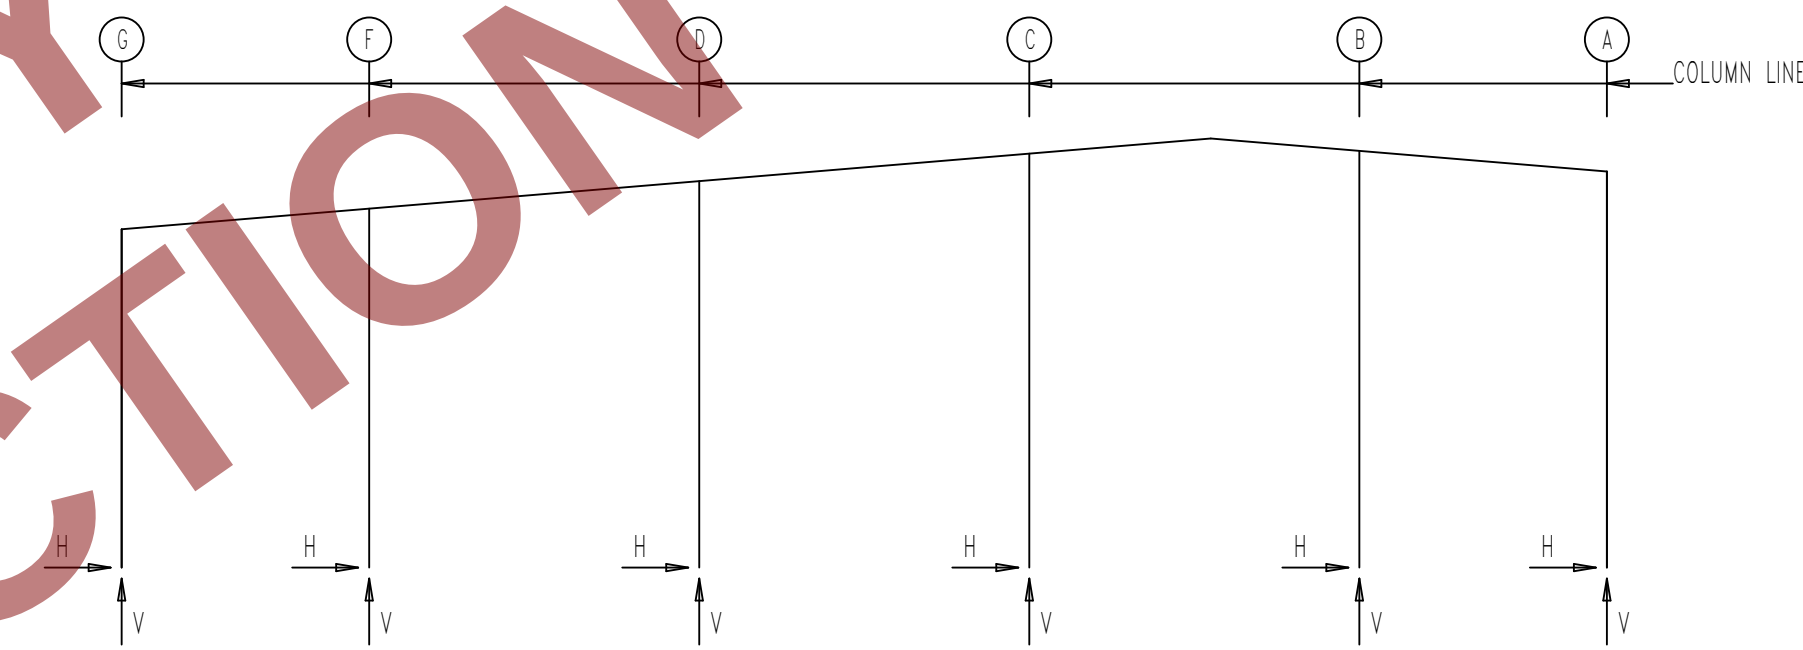

RIGID FRAME:

MAXIMUM REACTIONS, ANCHOR BOLTS, & BASE PLATES

Frame Line	Col Line	Load Id	Column_Reactions(k)	Load Id	Hmin	V	Bolt(in)	Dia	Base_Plate(in)	Thick	Grout (in)
			Hmax Vmax		H	Vmin	Qty		Width	Length	
1	G	1	8.0 11.3	8	-6.7 13	-7.9 -8.2	4	0.750	6.000	8.500	0.500 0.0
1	A	9 1	5.4 -9.4 16.0	1 9	-8.0 5.4	16.0 -9.4	4	0.750	6.000	9.000	0.500 0.0

RIGID FRAME:

MAXIMUM REACTIONS, ANCHOR BOLTS, & BASE PLATES

Frame Line	Col Line	Load Id	Column_Reactions(k)	Load Id	Hmin	V	Bolt(in)	Dia	Base_Plate(in)	Thick	Grout (in)
			Hmax Vmax		H	Vmin	Qty		Width	Length	
2*	G	1	15.8 21.0	12	-9.7 -18.0		4	0.750	6.000	8.500	0.625 0.0
2*	A	12 1	10.8 -15.8 30.1	1 12	-15.8 10.8	30.1 -15.7	4	0.750	6.000	9.000	0.625 0.0
2*	Frame lines:	2 3 4 5 6 7 8 9									

RIGID FRAME:

MAXIMUM REACTIONS, ANCHOR BOLTS, & BASE PLATES

Frame Line	Col Line	Load Id	Column_Reactions(k)	Load Id	Hmin	V	Bolt(in)	Dia	Base_Plate(in)	Thick	Grout (in)
			Hmax Vmax		H	Vmin	Qty		Width	Length	
10	G	9 2	2.4 1.4 3.0	10 8	-2.2 -1.6	-1.9 -2.4	4	0.750	6.000	10.50	0.500 0.0
10	A	11 20	2.3 -0.1 2.1	8 9	-1.9 1.8	0.3 -2.7	4	0.750	6.000	10.50	0.500 0.0
10	F	5 17	2.4 0.0 4.9	4 9	-2.2 0.0	-3.6 -4.4	4	0.750	6.000	8.000	0.500 0.0
10	D	7 18	3.0 0.0 5.4	4 8	-2.7 0.0	-3.8 -4.2	4	0.750	6.000	8.000	0.500 0.0
10	C	5 19	3.2 0.0 5.4	4 13	-2.9 0.0	-3.5 -3.8	4	0.750	6.000	8.000	0.500 0.0
10	B	6 16	2.8 0.0 5.3	3 14	-2.5 0.0	-3.2 -2.6	4	0.750	6.000	8.000	0.500 0.0

ANCHOR BOLT SUMMARY

Qty	Locate	Dia (in)	Type	Total Len (in)	Proj (in)
28	Jamb	5/8"	WEDGE	12.0	3.00
20	Endwall	3/4"	F1554	15.0	3.00
80	Frame	3/4"	F1554	15.0	3.00

STORAGE MATERIALS

1851 Madison Avenue #300 Council Bluffs, IA 51503
(888) 968-1222 <https://storagematerials.com>

DESCRIPTION: ANCHOR BOLT REACTIONS

CUSTOMER: CUSTOMER

PROJECT: BRANDON CUTTS

LOCATION:

DRN. BY

CK'D BY

DATE

SCALE

REV.

QUOTATION NO.

SHEET NO.

ART

AER

3/ 3/26

N.T.S.

00


Q25-0843B

OF

SPECIAL BOLTS					
ROOF PLAN					
◇ ID	QUAN	TYPE	DIA	LENGTH	WASH
1	4	A307	1/2"	1 1/4"	0
2	4	A325	1/2"	1 1/4"	2
3	4	A307	1/2"	1 1/4"	2

MEMBER TABLE		
ROOF PLAN		
MARK	PART	LENGTH
EB-1	BEAM	10'-0 5/16"
EB-2	BEAM	10'-0 3/16"
EB-3	BEAM	10'-0 3/16"
P-1	Z82512	28'-1 1/2"
P-2	Z82514	31'-3 1/2"
P-3	Z82516	31'-3 1/2"
P-4	Z82512	28'-1 1/2"
P-5	Z82512	28'-1 1/2"
P-6	Z82512	28'-1 1/2"
P-7	Z82512	27'-1 1/2"
P-8	Z82512	29'-3 1/2"
P-9	Z82514	29'-3 1/2"
P-10	Z82512	27'-5 1/2"
P-11	Z82516	25'-7 1/2"
P-12	Z82514	25'-7 1/2"
E-1	08532DU1	24'-11 1/2"
E-2	08532DU1	24'-11 1/2"
E-3	08534DU1	24'-11 1/2"
E-4	08534DU1	24'-11 1/2"
E-5	08534DU1	24'-11 1/2"
E-6	08534DU1	24'-11 1/2"
E-7	08534DU1	24'-11 1/2"
E-8	08532DU1	24'-11 1/2"
E-9	08532DU1	25'-3 1/2"
CB-3	CB0250	28'-4"
CB-4	CB0250	34'-2"
CB-5	CB0250	31'-8"
CB-6	CB0250	31'-5"
CB-7	CB0250	28'-10"
CB-8	CB0313	28'-4"
CB-9	CB0313	28'-10"
CB-10	CB0250	27'-1"

CONNECTION PLATES	
ROOF PLAN	
☐ ID	MARK/PART
1	CL-18

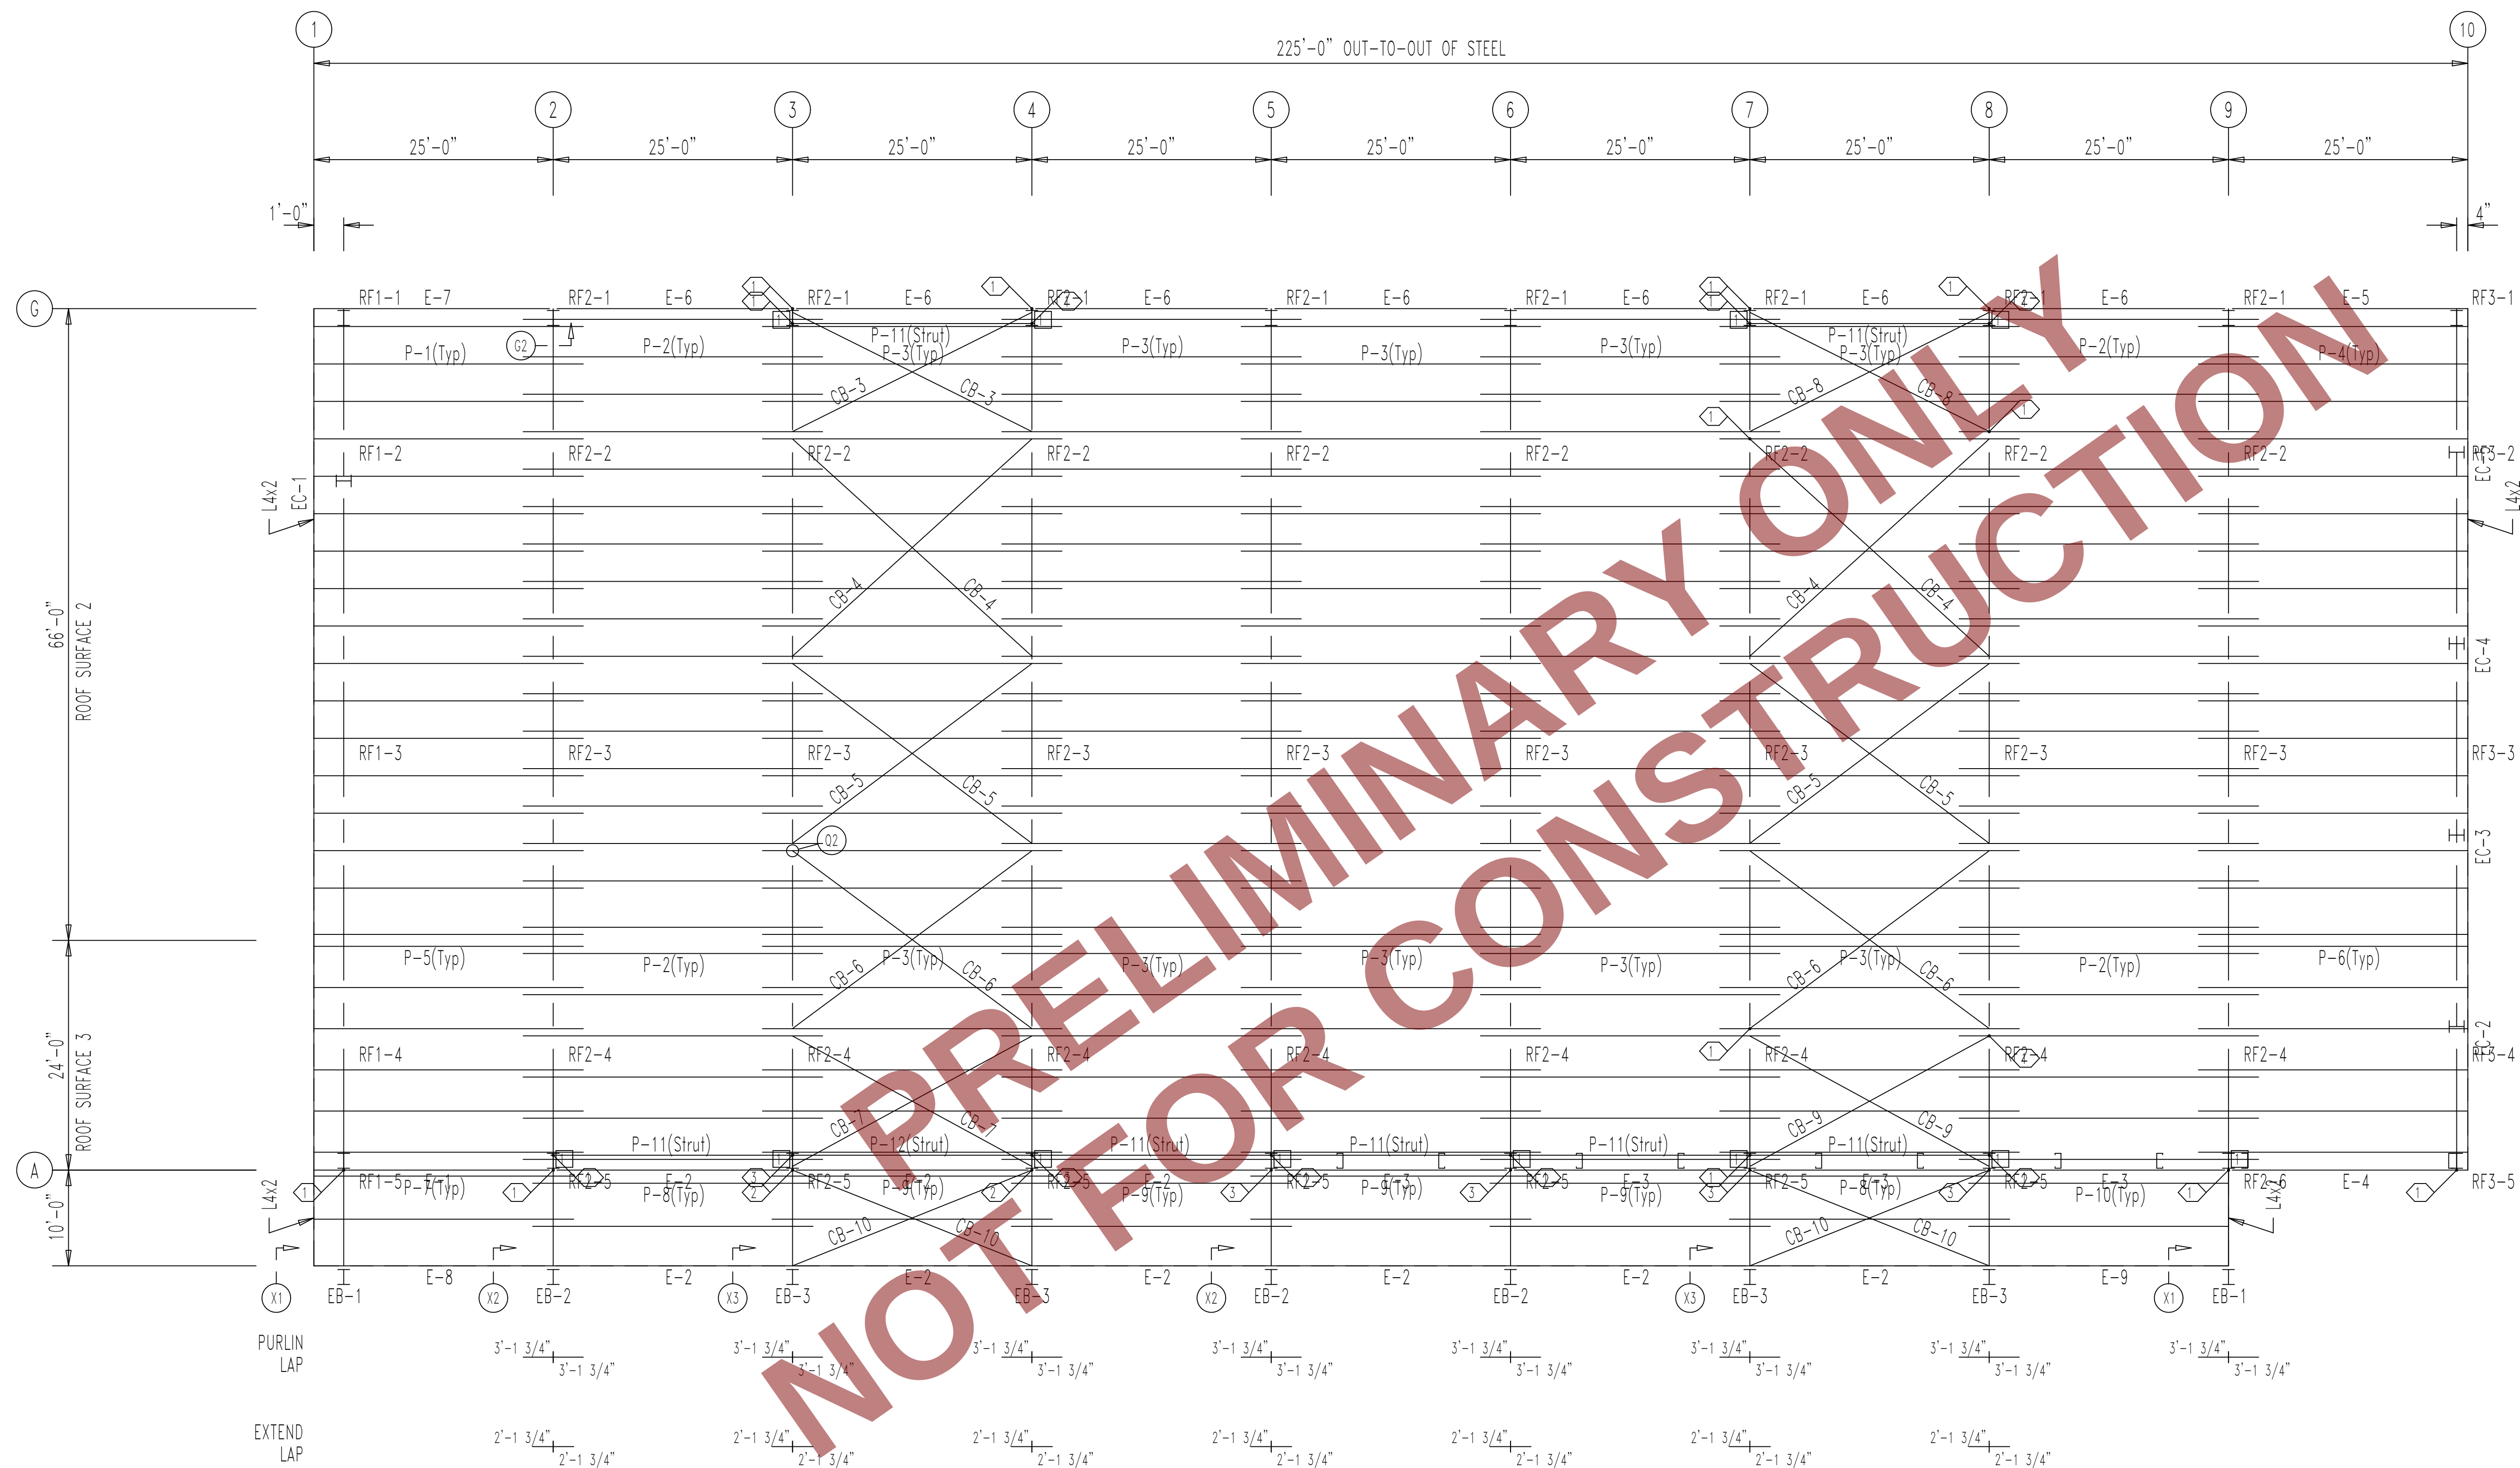


ROOF FRAMING PLAN

STORAGE MATERIALS

1851 Madison Avenue #300 Council Bluffs, IA 51503
(888) 968-1222 <https://storagematerials.com>

DESCRIPTION: ROOF FRAMING							
CUSTOMER:					PROJECT: BRANDON CUTTS		
LOCATION:							
DRN. BY	CK'D BY	DATE	SCALE	REV.	QUOTATION NO.		SHEET NO.
ART	AER	3/ 3/26	N.T.S.	00	Q25-0843B		OF

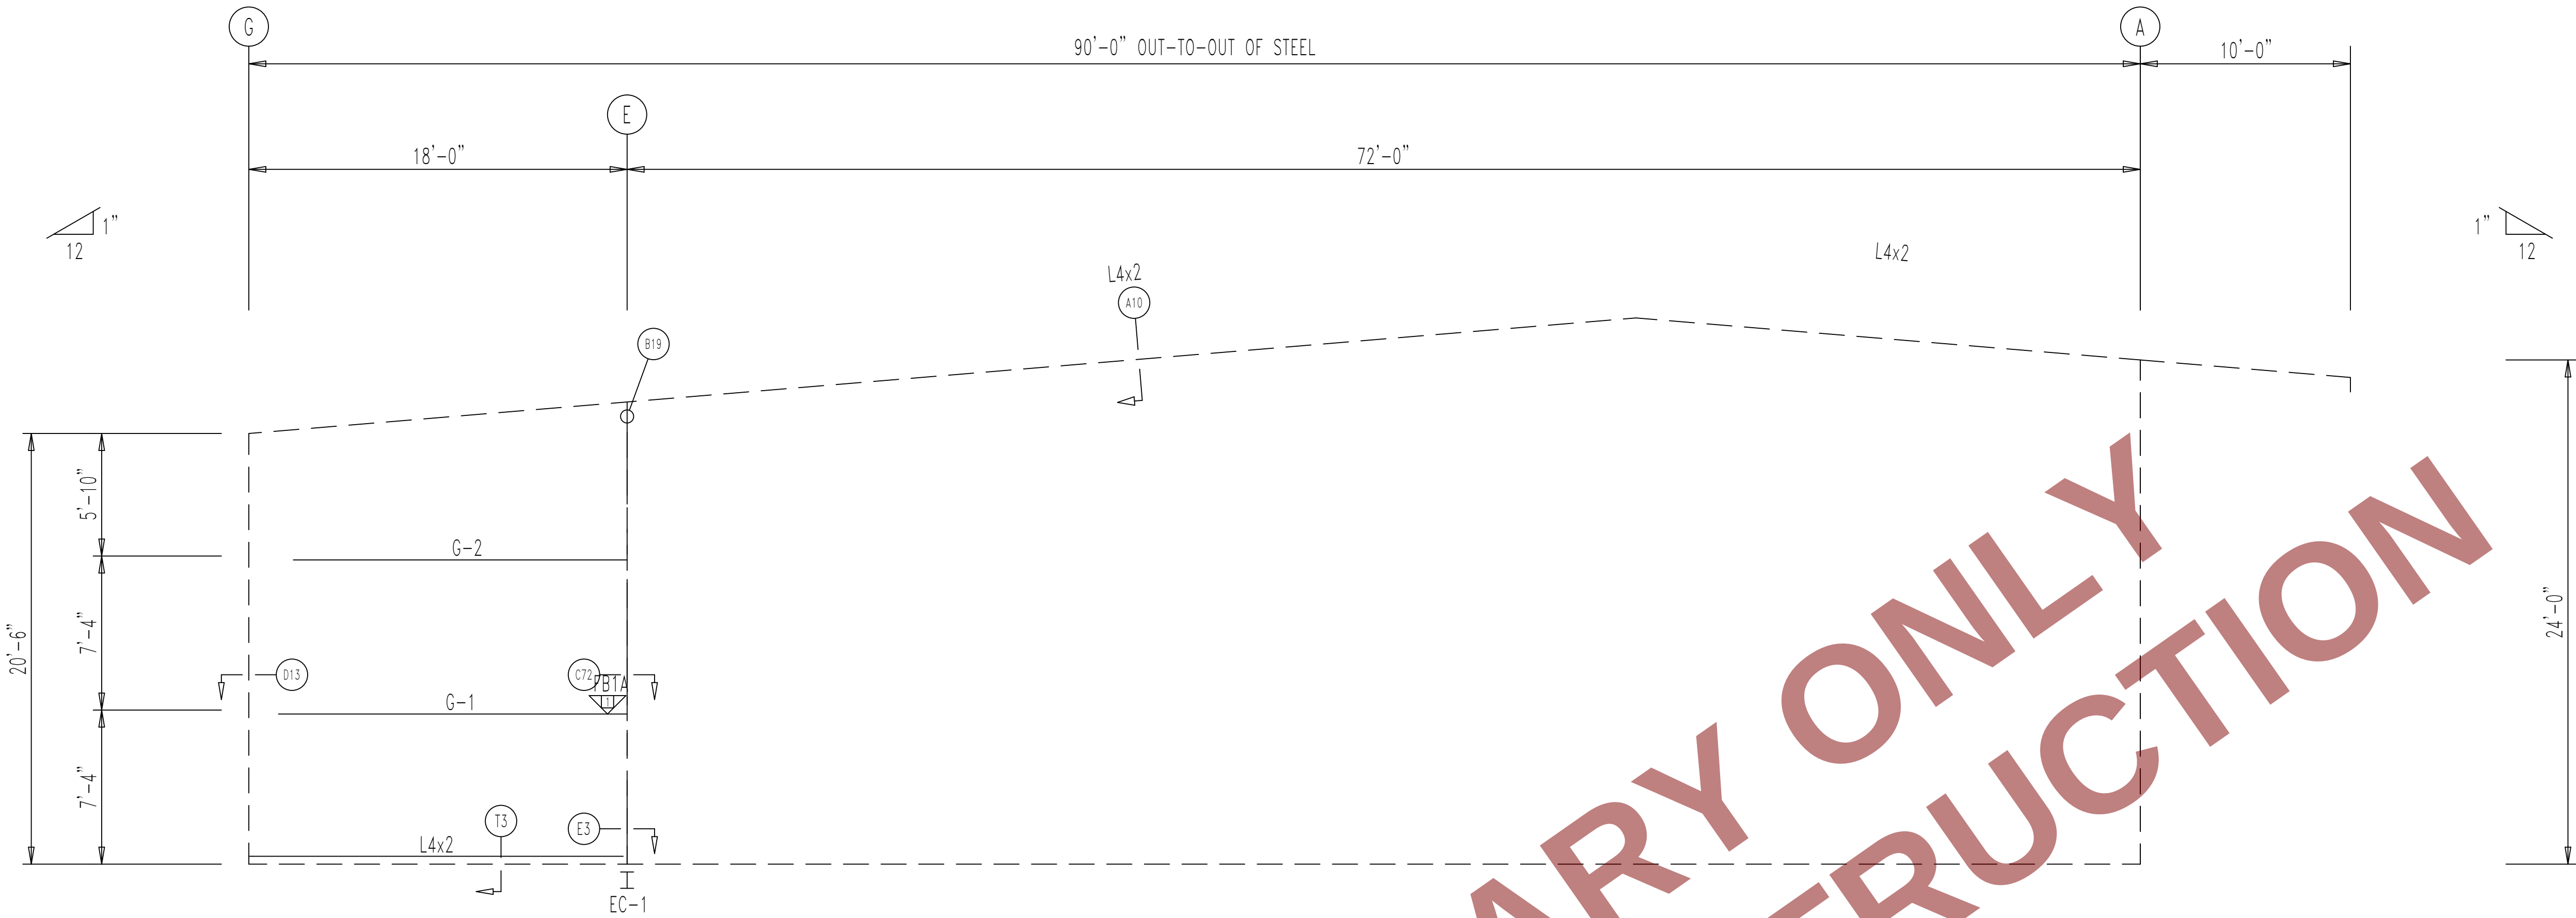

ENDWALL FRAMING: FRAME LINE 1



ENDWALL SHEETING & TRIM: FRAME LINE 1

PANELS: 26 Ga. RL - Need SMP Lifetime Color

BOLT TABLE FRAME LINE 1				
LOCATION	QUAN	TYPE	DIA	LENGTH
Columns/Raf	2	A325	5/8"	1' 1/4"

TRIM TABLE FRAME LINE 1			
◇ ID	PART	LENGTH	DETAIL
1	OU6102	10'-2"	TRIM_26
2	OU6	12'-2"	TRIM_26
3	JA6	12'-2"	TRIM_31
4	RGC6	18'-2"	
5	RA6	14'-2"	TRIM_18
6	RA6	18'-2"	TRIM_18
7	REND6	1'-0"	
8	PBOXF6	1'-0"	

MEMBER TABLE FRAME LINE 1		
MARK	PART	LENGTH
EC-1	W10X12	19'-8 7/8"
G-1	Z102516	16'-6 9/16"
G-2	Z102516	15'-10 1/8"

FLANGE BRACE TABLE FRAME LINE 1		
▽ ID	MARK	LENGTH
1	FB1A	2'-9 1/4"

CONNECTION PLATES FRAME LINE 1		
□ ID	MARK/PART	
1	h1	


STORAGE MATERIALS

1851 Madison Avenue #300 Council Bluffs, IA 51503
(888) 968-1222 <https://storagematerials.com>

DESCRIPTION:

ENDWALL FRAMING

CUSTOMER: CUSTOMER				PROJECT: BRANDON CUTTS		
LOCATION:						
DRN. BY ART	CK'D BY AER	DATE 3/ 3/26	SCALE N.T.S.	REV. 00	QUOTATION NO. Q25-0843B	SHEET NO. OF

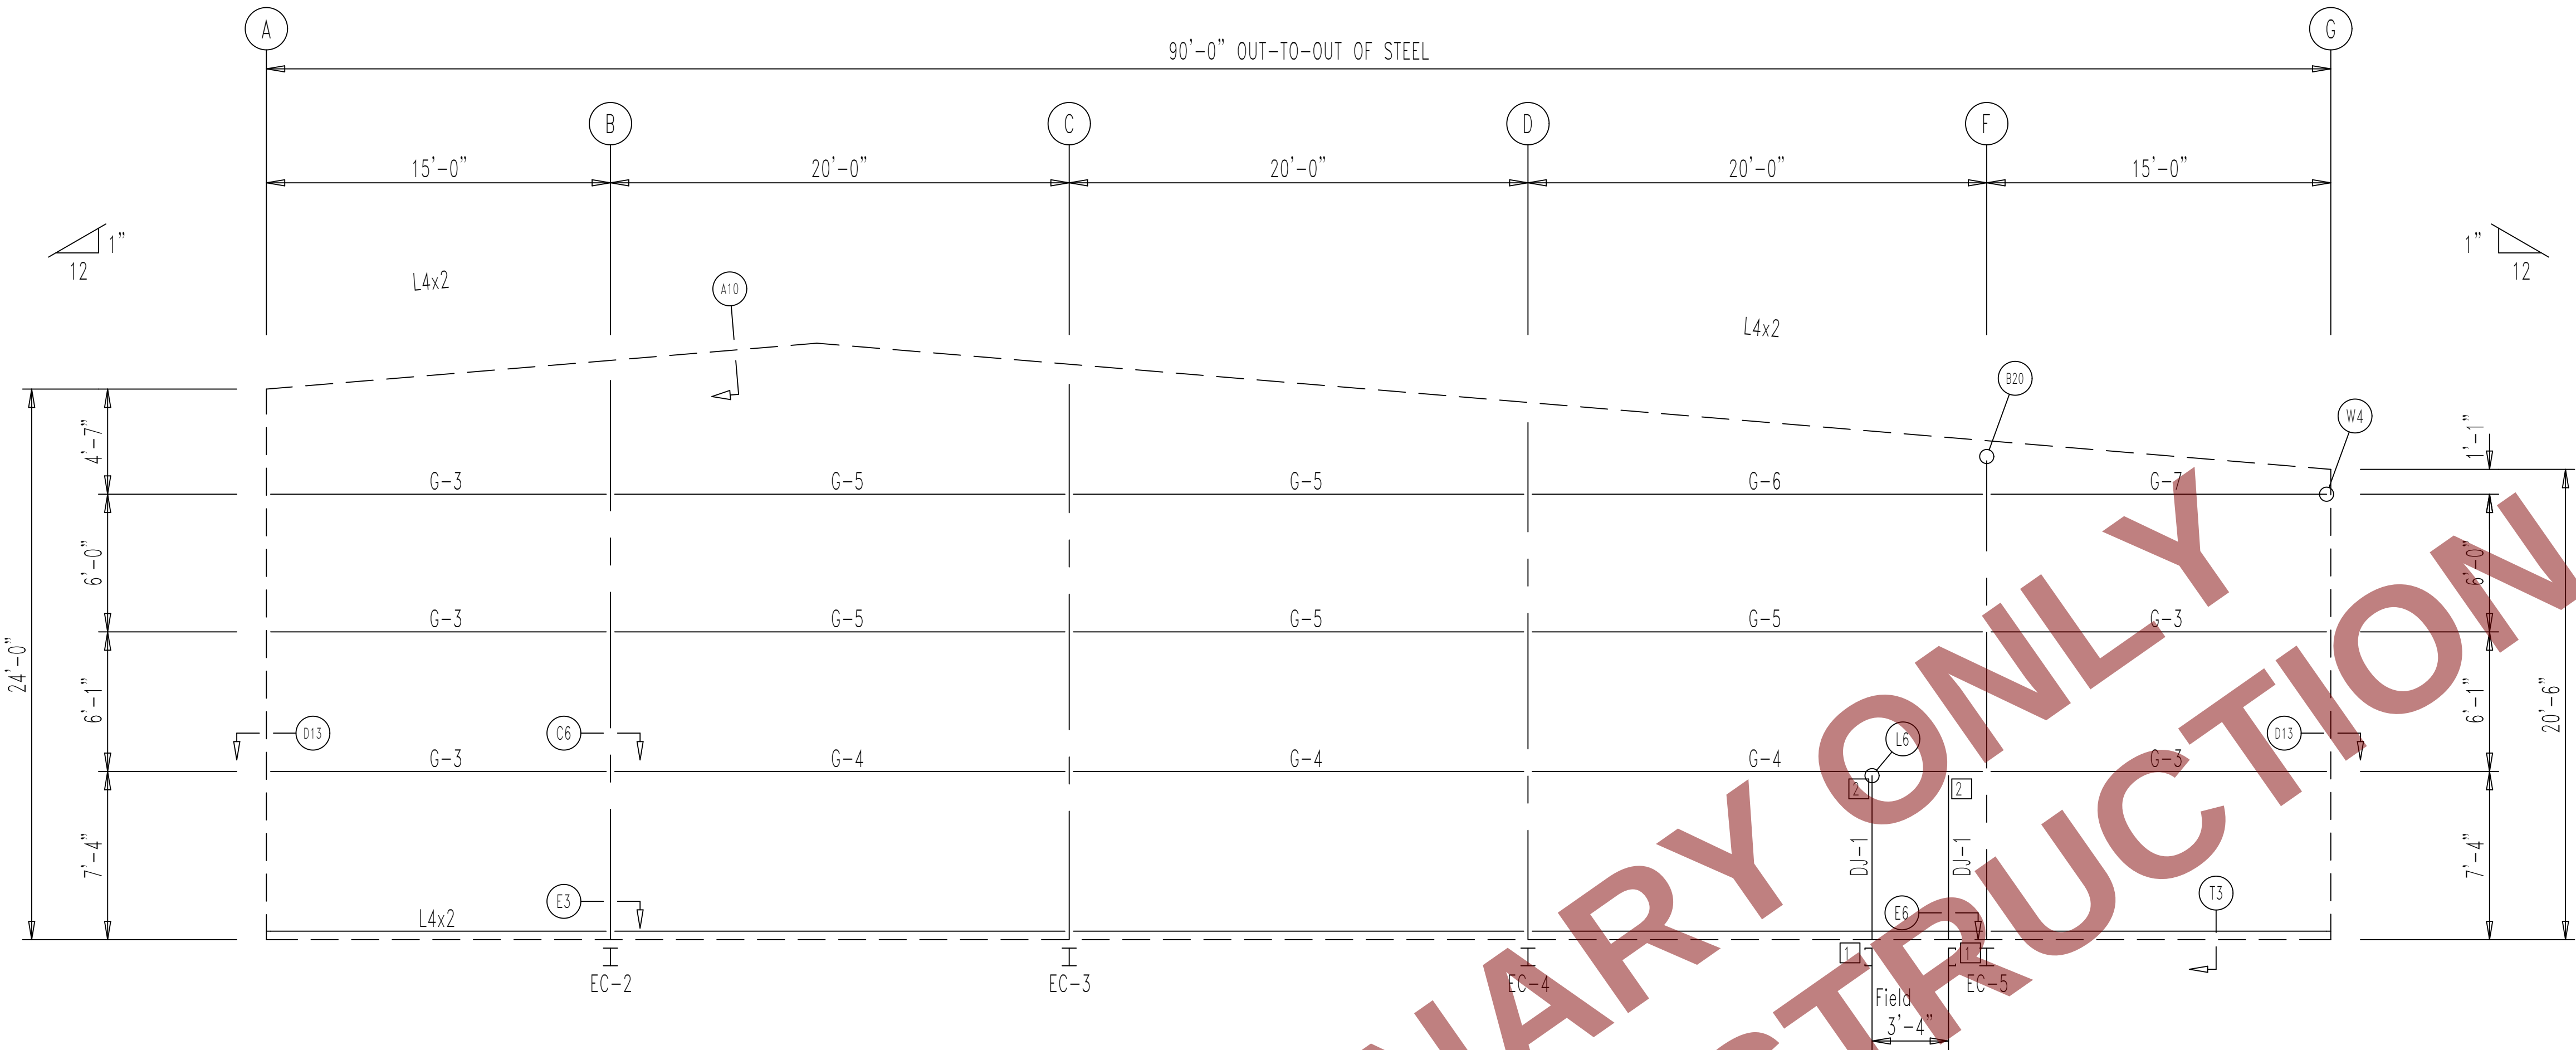

ENDWALL FRAMING: FRAME LINE 10



ENDWALL SHEETING & TRIM: FRAME LINE 10

PANELS: 26 Ga. RL - Need SMP Lifetime Color

BOLT TABLE				
FRAME LINE 10				
LOCATION	QUAN	TYPE	DIA	LENGTH
Columns/Raf	4	A325	5/8"	1' 1/2"

TRIM TABLE			
FRAME LINE 10			
ID	PART	LENGTH	DETAIL
1	OU6	12'-2"	TRIM_26
2	OU6102	10'-2"	TRIM_26
3	RA6	14'-2"	TRIM_18
4	RA6	12'-2"	TRIM_18
5	REND6	1'-0"	
6	RA6	18'-2"	TRIM_18
7	PBOXF6	1'-0"	
8	JA6102	10'-2"	TRIM_31
9	HE6	6'-3"	TRIM_33


MEMBER TABLE		
FRAME LINE 10		
MARK	PART	LENGTH
EC-2	W08541	23'-8 3/8"
EC-3	W08541	23'-6 3/8"
EC-4	W08541	21'-10 3/8"
EC-5	W08541	20'-2 3/8"
DJ-1	C83516	6'-11 3/4"
G-3	Z82516	13'-9 1/4"
G-4	Z83514	19'-4"
G-5	Z82514	19'-4"
G-6	Z82516	19'-4"
G-7	Z82516	8'-7"

CONNECTION PLATES	
FRAME LINE 10	
ID	MARK/PART
1	CL-104
2	i1


STORAGE MATERIALS

1851 Madison Avenue #300 Council Bluffs, IA 51503
(888) 968-1222 <https://storagematerials.com>

DESCRIPTION: ENDWALL FRAMING							
CUSTOMER: CUSTOMER					PROJECT: BRANDON CUTTS		
LOCATION:							
DRN. BY ART	CK'D BY AER	DATE 3/ 3/26	SCALE N.T.S.	REV. 00	QUOTATION NO. Q25-0843B		SHEET NO. OF

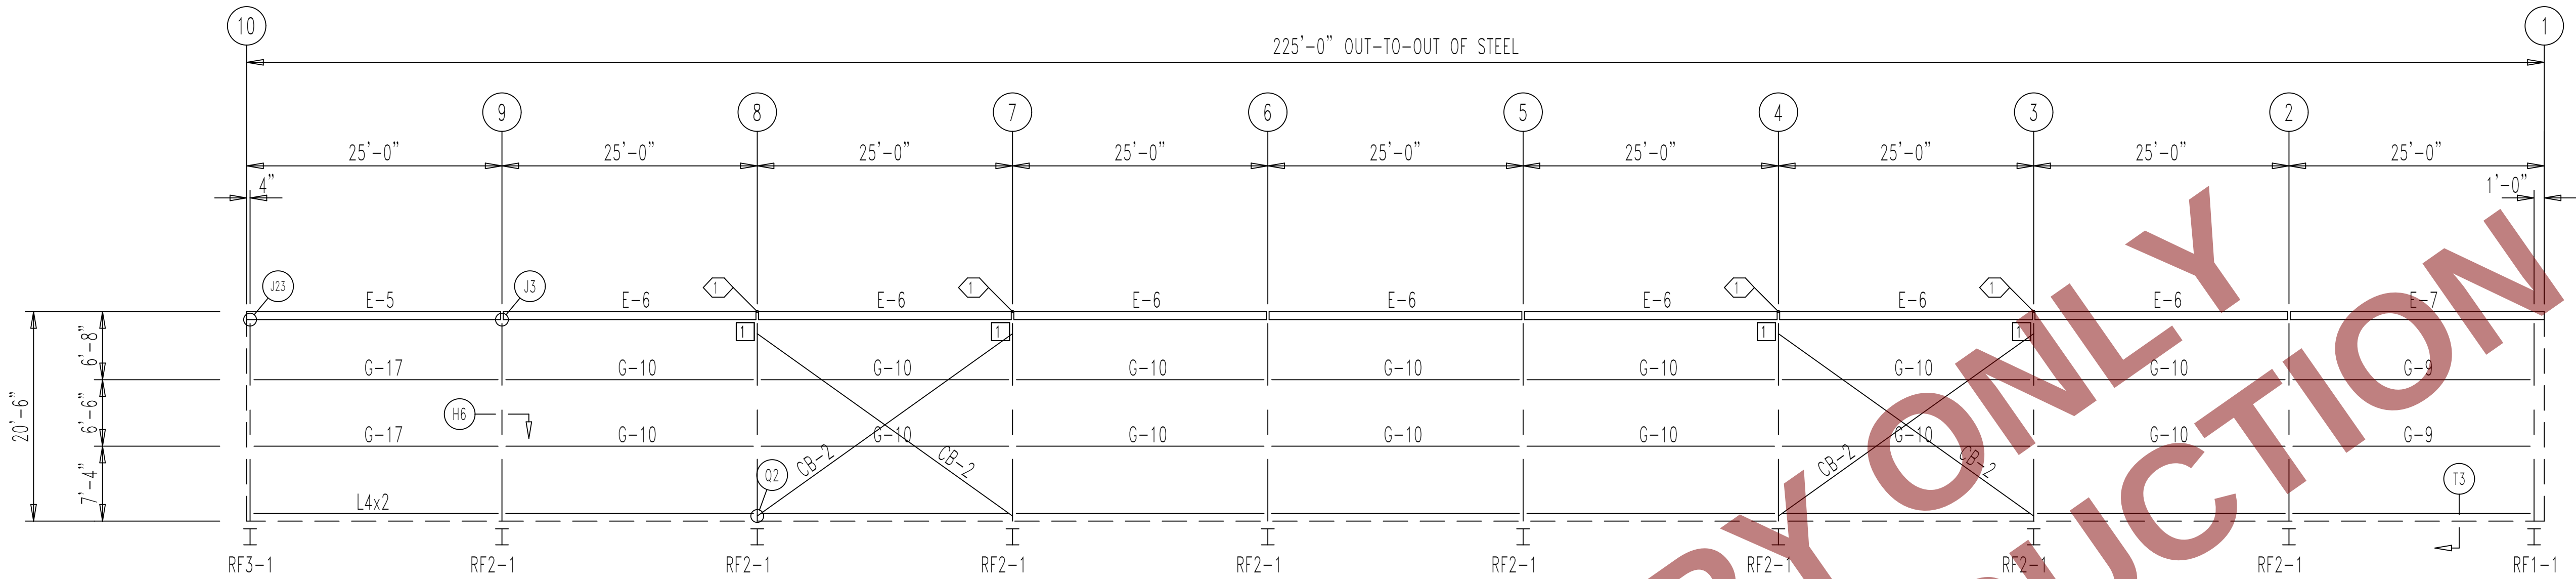

SIDEWALL FRAMING: FRAME LINE G

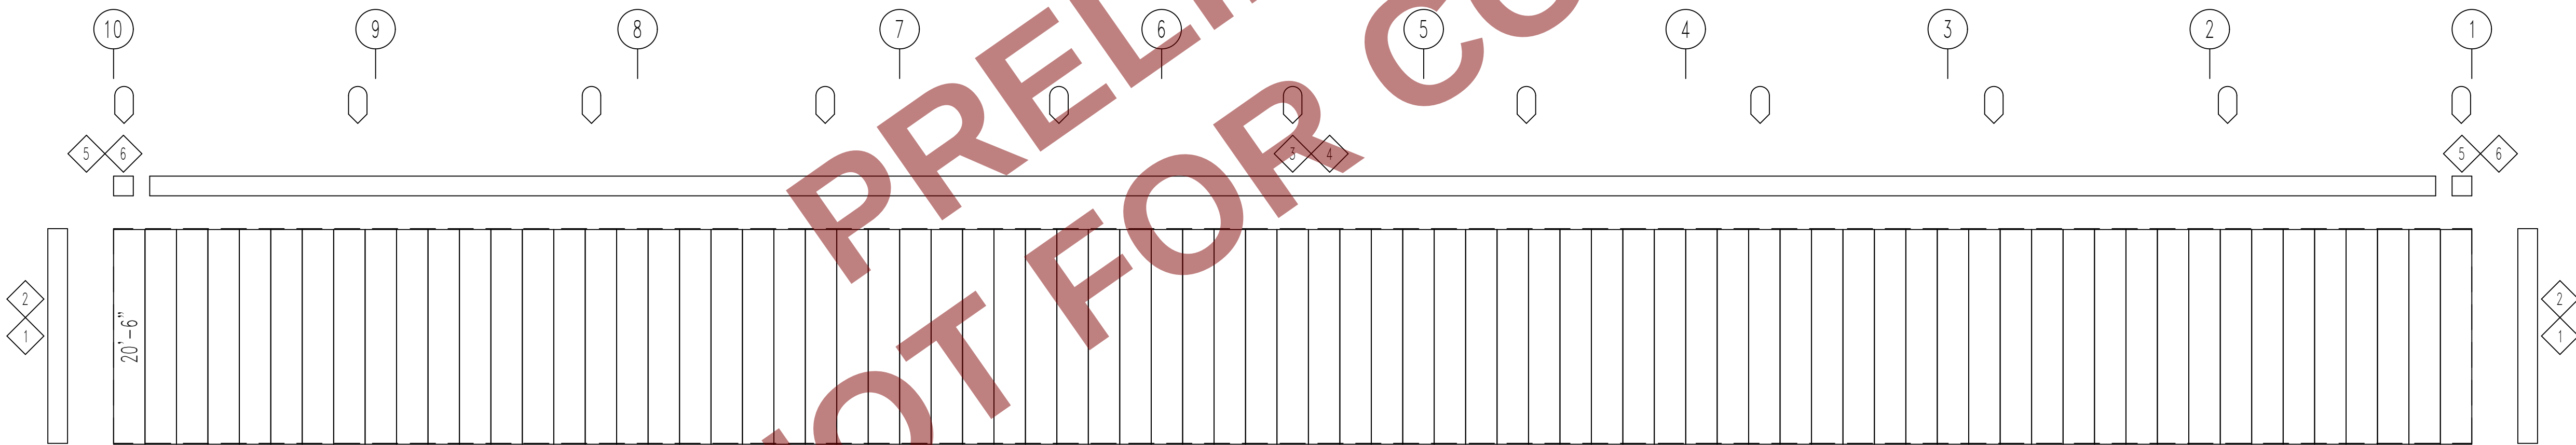

SIDEWALL SHEETING & TRIM: FRAME LINE G

PANELS: 26 Ga. RL - Need SMP Lifetime Color

TRIM TABLE FRAME LINE G			
◇ ID	PART	LENGTH	DETAIL
1	OU6102	10'-2"	TRIM_26
2	OU6	12'-2"	TRIM_26
3	RLGU6	20'-4"	TRIM_15
4	RLGU6102	10'-2"	TRIM_15
5	GEN6	1 1/2"	
6	OCB6	10"	

SPECIAL BOLTS					
◇ ID	QUAN	TYPE	DIA	LENGTH	WASH
1	4	A307	1/2"	1 1/4"	0

MEMBER TABLE FRAME LINE G		
MARK	PART	LENGTH
E-5	08534DU1	24'-11 1/2"
E-6	08534DU1	24'-11 1/2"
E-7	08534DU1	24'-11 1/2"
G-9	Z82512	23'-4"
G-10	Z82512	24'-4"
G-17	Z82512	24'-0"
CB-2	CB0500	31'-8"



CONNECTION PLATES FRAME LINE G	
□ ID	MARK/PART
1	CL-18

STORAGE MATERIALS

1851 Madison Avenue #300 Council Bluffs, IA 51503
(888) 968-1222 <https://storagematerials.com>

DESCRIPTION:

SIDEWALL FRAMING							
CUSTOMER: CUSTOMER					PROJECT: BRANDON CUTTS		
LOCATION:							
DRN. BY ART	CK'D BY AER	DATE 3/ 3/26	SCALE N.T.S.	REV. 00	QUOTATION NO. Q25-0843B		SHEET NO. OF

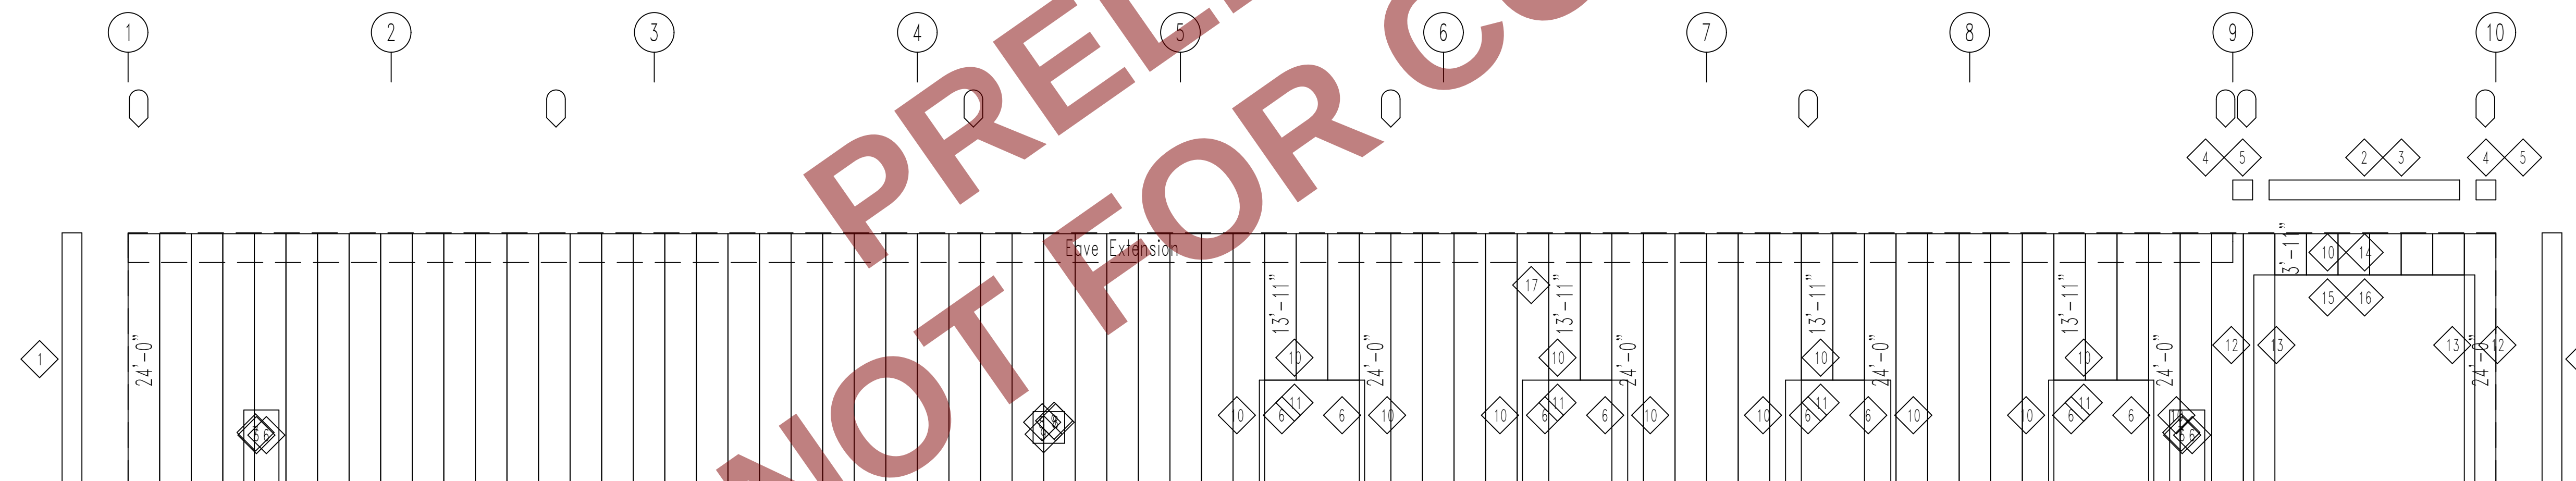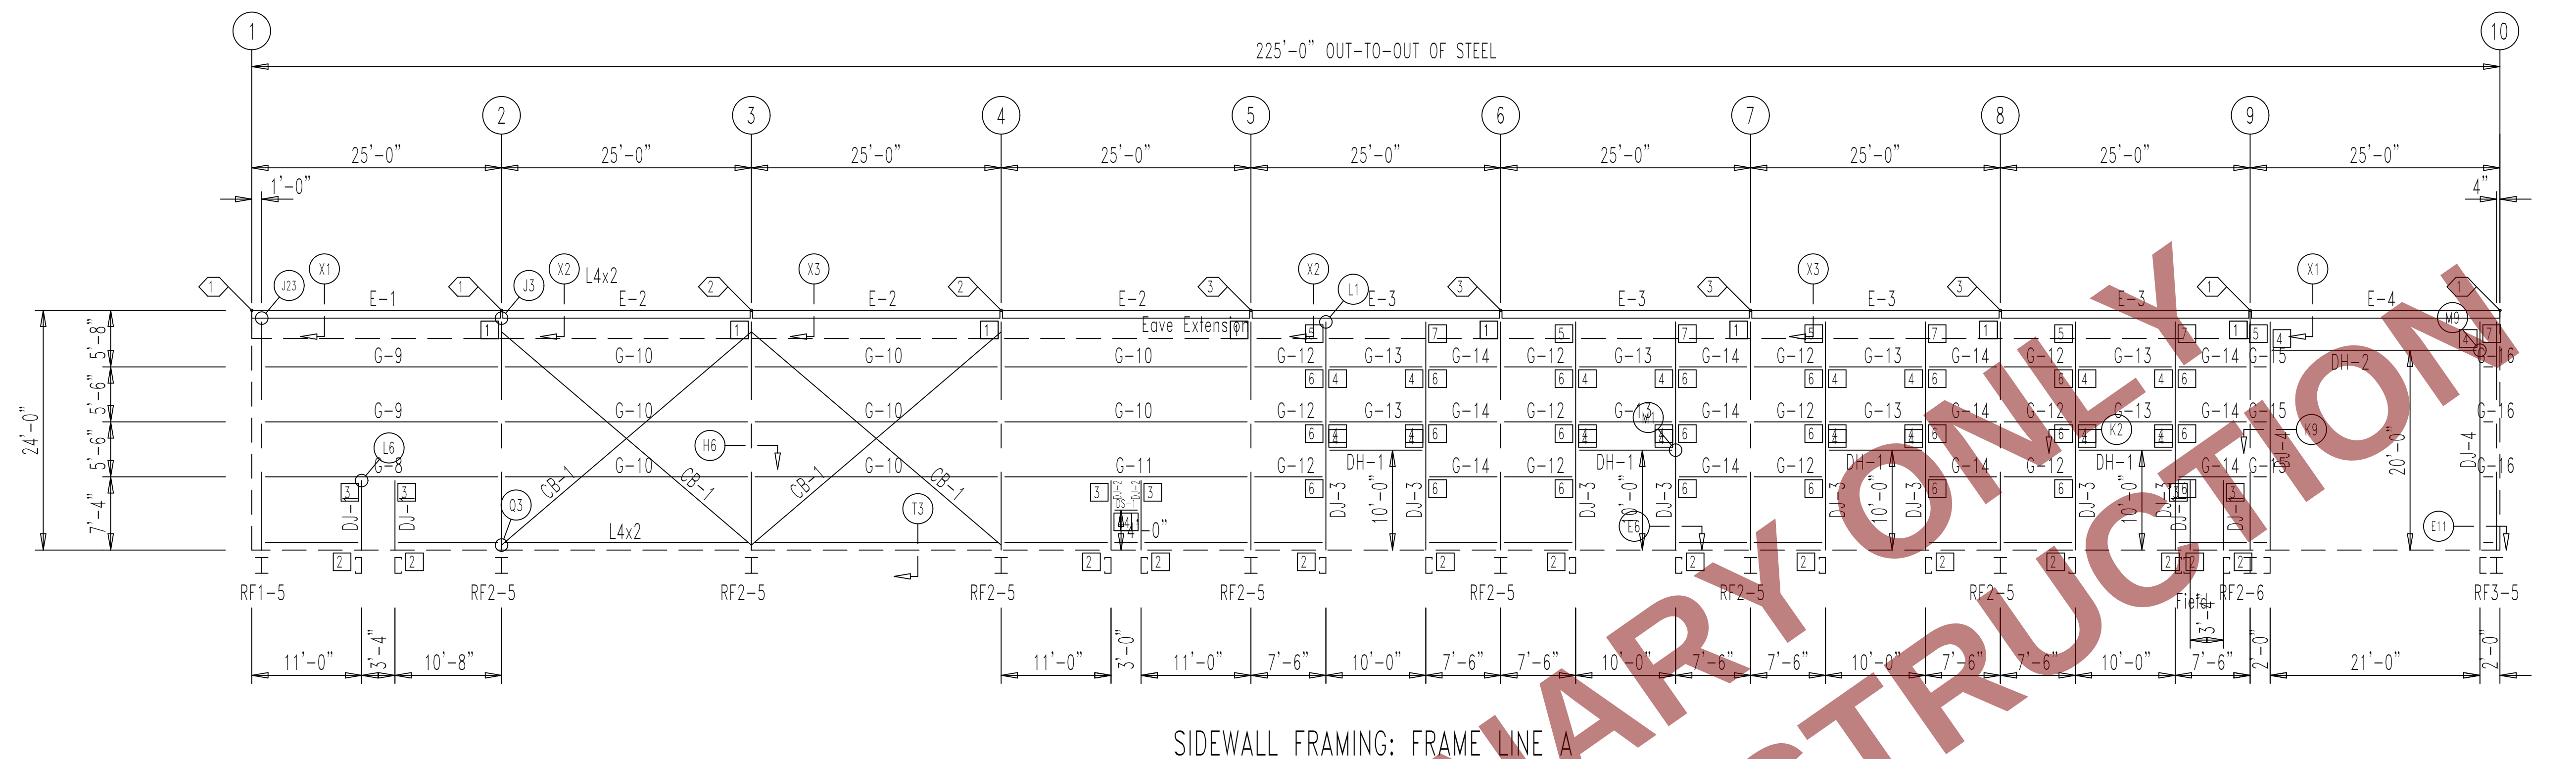

SIDEWALL SHEETING & TRIM: FRAME LINE A

PANELS: 26 Ga. RL - Need SMP Lifetime Color

TRIM TABLE			
FRAME		LINE A	
◇ ID	PART	LENGTH	DETAIL
1	OU6	12'-2"	TRIM_26
2	RLGU6	12'-2"	TRIM_15
3	RLGU6	14'-2"	TRIM_15
4	GEN6	1/2"	
5	OCB6	10'	
6	JA6102	10'-2"	TRIM_31
7	HE6	6'-3"	TRIM_33
8	JA6	7'-2"	TRIM_31
9	HE6	3'-6"	TRIM_33
10	JH6102	10'-2"	
11	HE6	10'-3"	TRIM_33
12	JH6	20'-4"	
13	JA6	20'-4"	TRIM_31
14	JH6	12'-2"	
15	HE6102	10'-2"	TRIM_33
16	HE6	12'-3"	TRIM_33
17	HE6102	10'-2"	TRIM_40

SPECIAL BOLTS					
⊙ ID	QUAN	TYPE	DIA	LENGTH	WASH
1	4	A307	1/2"	1 1/4"	0
2	4	A325	1/2"	1 1/4"	2
3	4	A307	1/2"	1 1/4"	2

MEMBER TABLE FRAME LINE A		
MARK	PART	LENGTH
DJ-1	C83516	6'-11 3/4"
DJ-2	C83516	6'-11 3/4"
DJ-3	C83512	23'-3 1/4"
DJ-4	C8X11.5	23'-3 1/2"
DH-1	C82516	9'-11 1/2"
DH-2	C82516	20'-11 1/2"
DS-1	C82516	2'-11 1/2"
E-1	08532DU1	24'-11 1/2"
E-2	08532DU1	24'-11 1/2"
E-3	08534DU1	24'-11 1/2"
E-4	08534DU1	24'-11 1/2"
G-8	Z82512	23'-4"
G-9	Z82512	23'-4"
G-10	Z82512	24'-4"
G-11	Z82512	24'-4"
G-12	Z82516	6'-10"
G-13	Z82516	9'-11 1/2"
G-14	Z82516	6'-10"
G-15	Z82516	1'-4"
G-16	Z82516	1'-0"
CB-1	RD1000	33'-4"

CONNECTION PLATES	
FRAME LINE A	
☐ ID	MARK/PART
1	CL-18
2	CL-104
3	j1
4	CL-100
5	e1
6	CL-103
7	e2

STORAGE MATERIALS

1851 Madison Avenue #300 Council Bluffs, IA 51503
(888) 968-1222 <https://storagematerials.com>

DESCRIPTION:	SIDEWALL FRAMING
--------------	------------------

CUSTOMER: CUSTOMER	PROJECT: BRANDON CUTTS
--------------------	------------------------

LOCATION:	
-----------	--

DRN. BY ART	CK'D BY AER	DATE 3/ 3/26	SCALE N.T.S.	REV. 00	QUOTATION NO. Q25-0843B	SHEET NO. OF
----------------	----------------	-----------------	-----------------	------------	----------------------------	-----------------


SPLICE PLATE & BOLT TABLE									
Mark	Qty Top	Qty Bot	Int	Type	Dia	Length	Width	Thick	Length
SP1	4	4	2	A325	0.625	2.25	6"	5/8"	2'-11 5/16"
SP2	4	4	0	A325	0.625	1.75	6"	3/8"	1'-7 1/4"
SP3	4	4	0	A325	0.625	1.75	6"	3/8"	2'-3 3/8"
SP4	4	4	2	A325	0.750	2.50	6"	3/4"	3'-1 5/16"

▽ FLANGE BRACES: Both Sides(U.N.)
FBxxA(1)
A - 2X2X14Ga

MEMBER TABLE							
Mark	Weight	Length	Web Depth		Web Plate	Outside Flange W x Thk x Length	Inside Flange W x Thk x Length
			Start/End	Thick	Length		
RF1-1	503	19'-9 3/4"	8.0/16.5	0.188	7'-4 9/16"	6 x 1/4" x 19'-9"	6 x 1/4" x 17'-4 1/2"
			16.5/28.0	0.188	9'-11"	6 x 1/4" x 2'-1 11/16"	
			28.0/25.4	0.188	2'-7 9/16"		
RF1-2	614	23'-11 11/16"	28.0/21.4	0.188	9'-11"	6 x 1/4" x 23'-10 11/16"	6 x 1/4" x 23'-11 1/16"
			21.4/14.7	0.188	9'-11"		
			14.7/12.0	0.188	4'-0 11/16"		
RF1-3	753	40'-0 3/4"	12.0/14.0	0.135	9'-11"	6 x 1/4" x 40'-0"	6 x 1/4" x 39'-10 1/2"
			14.0/16.0	0.135	9'-11"		
			16.0/18.0	0.135	9'-11"		
			18.0/19.6	0.135	8'-3"		
			19.6/20.0	0.135	2'-0"		
RF1-4	667	21'-8 3/4"	20.0/20.9	0.188	2'-0"	6 x 1/4" x 21'-7 9/16"	6 x 5/16" x 21'-5 15/16"
			20.9/25.4	0.188	9'-8 9/16"		
			25.4/30.0	0.188	9'-11"		
RF1-5	622	23'-3 3/4"	30.0/29.1	0.250	3'-5 9/16"	6 x 1/4" x 2'-3 1/2"	6 x 5/16" x 10'-8 7/16"
			29.1/18.6	0.188	7'-11 11/16"	6 x 1/4" x 21'-9 3/16"	6 x 5/16" x 10'-0 1/4"
			18.6/16.0	0.188	2'-0"		
			16.0/9.6	0.135	8'-0"		
			9.6/8.0	0.135	2'-0"		
EB-1	158	10'-0 5/16"	7.5/17.5	0.135	10'-0 5/16"	5 x 1/4" x 10'-0 5/16"	5 x 1/4" x 10'-0 5/16"

CONNECTION PLATES

ID	Mark/Part
1	h2

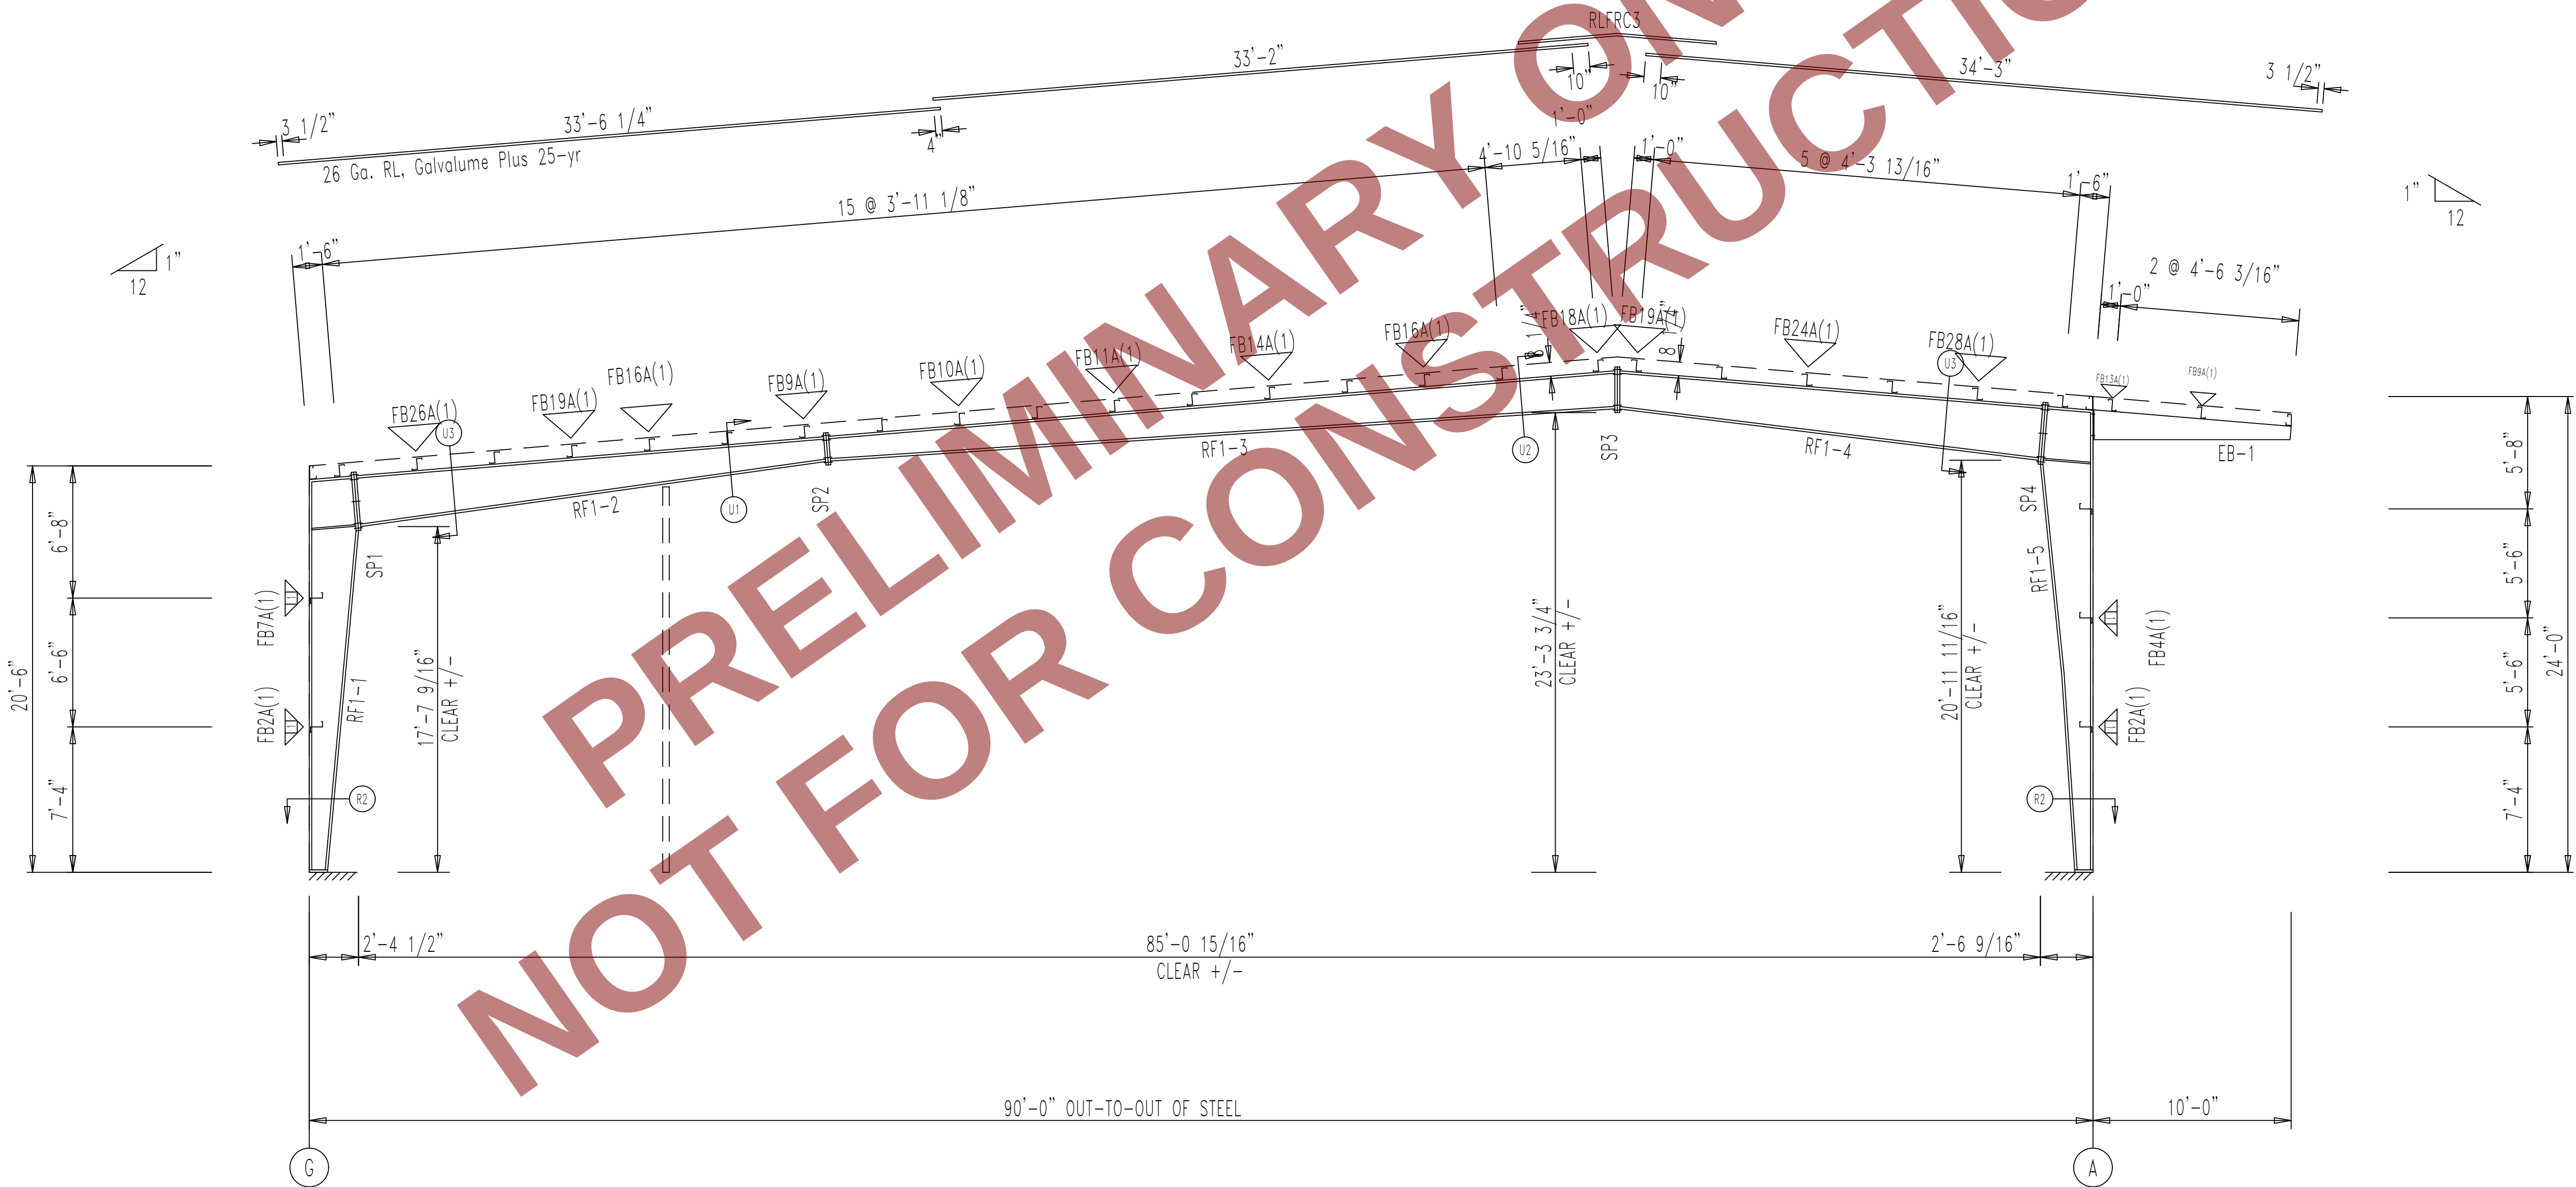

RIGID FRAME ELEVATION: FRAME LINE 1

STORAGE MATERIALS

1851 Madison Avenue #300 Council Bluffs, IA 51503
(888) 968-1222 <https://storagematerials.com>

DESCRIPTION: RIGID FRAME ELEVATION

CUSTOMER: CUSTOMER PROJECT: BRANDON CUTTS

LOCATION:							SHEET NO. OF
DRN. BY ART	CK'D BY AER	DATE 3/ 3/26	SCALE N.T.S.	REV. 00	QUOTATION NO. Q25-0843B		


SPLICE PLATE & BOLT TABLE									
Mark	Qty		Int	Type	Dia	Length	Width	Thick	Length
SP1	4	4	4	A325	0.750	2.50	6"	3/4"	3'-11 5/16"
SP2	4	4	0	A325	0.625	1.75	6"	3/8"	1'-11 5/16"
SP3	4	4	2	A325	0.625	1.75	6"	3/8"	2'-9 3/8"
SP4	4	4	4	A325	0.875	2.50	6"	5/8"	4'-3 5/16"

ALTERNATE MEMBER		
Frame Line	○ ID	Mark
9	A	RF2-6

▽ FLANGE BRACES: Both Sides(U.N.)
FBxxA(1)
A - 2X2X14Ga

MEMBER TABLE							
Mark	Weight	Length	Web Depth	Web Plate		Outside Flange W x Thk x Length	Inside Flange W x Thk x Length
			Start/End	Thick	Length		
RF2-1	742	19'-9 3/4"	8.0/20.6	0.250	6'-5 3/8"	6 x 1/4" x 19'-8 7/8"	6 x 1/4" x 16'-6 15/16"
			20.6/40.0	0.250	9'-11"	6 x 1/4" x 3'-0 3/4"	
			40.0/36.4	0.250	3'-7 9/16"		
			40.0/29.6	0.250	9'-11"	6 x 1/4" x 22'-11 3/8"	6 x 1/4" x 23'-0 3/8"
RF2-2	870	23'-0 1/2"	29.6/19.3	0.250	9'-11"		
			19.3/16.0	0.250	3'-1 3/8"		
			16.0/18.5	0.135	9'-11"	6 x 5/16" x 21'-0"	6 x 1/4" x 39'-10 1/8"
			18.5/20.5	0.135	8'-1"	6 x 1/4" x 19'-0"	
RF2-3	962	40'-0 3/4"	20.5/21.0	0.135	2'-0"		
			21.0/23.5	0.188	9'-11"		
			23.5/25.5	0.188	8'-1"		
			25.5/26.0	0.188	2'-0"		
RF2-4	933	20'-7 15/16"	26.0/27.6	0.250	2'-0"	6 x 1/4" x 20'-6 15/16"	6 x 5/16" x 20'-5 3/16"
			27.6/35.2	0.250	8'-7 15/16"		
			35.2/44.0	0.250	9'-11"		
			40.0/44.0	0.250	3'-11 9/16"	6 x 1/4" x 3'-4 7/16"	6 x 5/16" x 9'-8 3/4"
RF2-5	911	23'-3 3/4"	44.0/22.0	0.250	9'-6 11/16"	6 x 1/4" x 21'-9 1/16"	6 x 1/2" x 10'-0 3/4"
			22.0/10.8	0.188	8'-0"		
			10.8/ 8.0	0.188	2'-0"		
			7.5/17.5	0.135	10'-0 3/16"	5 x 1/4" x 10'-0 3/16"	5 x 1/4" x 10'-0 3/16"
EB-2	161	10'-0 3/16"	7.5/17.5	0.135	10'-0 3/16"	5 x 1/4" x 10'-0 3/16"	5 x 1/4" x 10'-0 3/16"
EB-3	161	10'-0 3/16"	7.5/17.5	0.135	10'-0 3/16"	5 x 1/4" x 10'-0 3/16"	5 x 1/4" x 10'-0 3/16"
EB-1	158	10'-0 5/16"	7.5/17.5	0.135	10'-0 5/16"	5 x 1/4" x 10'-0 5/16"	5 x 1/4" x 10'-0 5/16"

CONNECTION PLATES	
□ ID	Mark/Part
1	h2

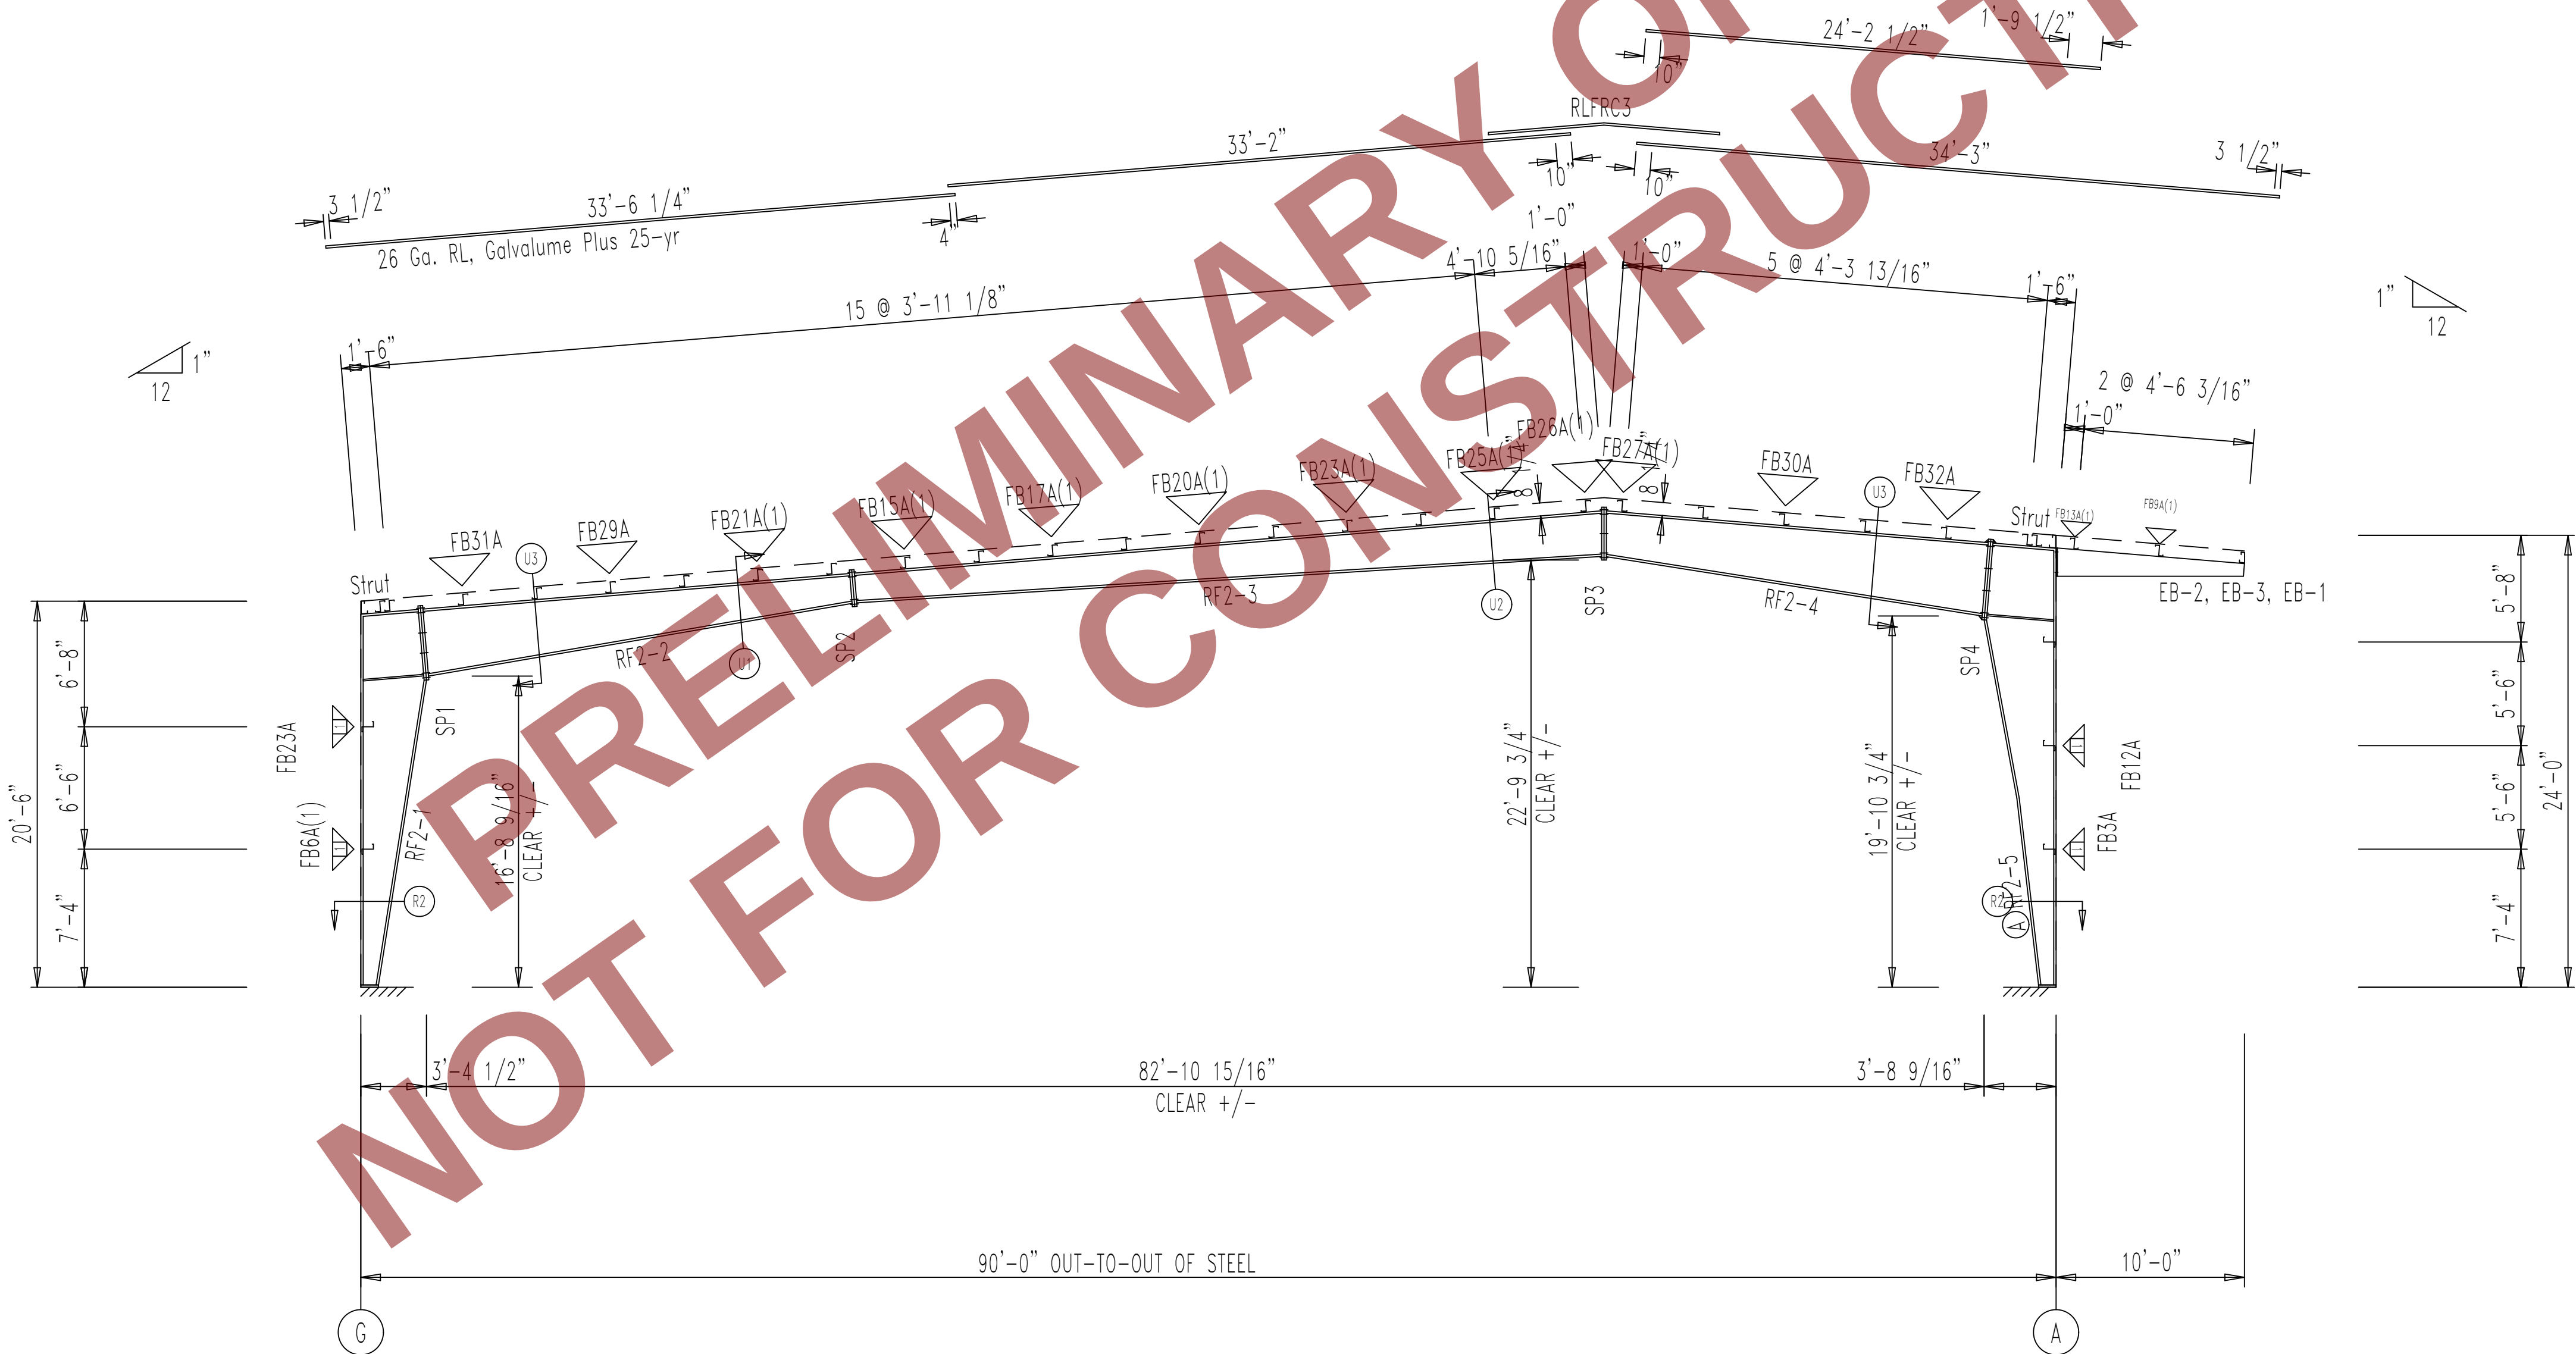



RIGID FRAME ELEVATION: FRAME LINE 2 3 4 5 6 7 8 9


STORAGE MATERIALS

1851 Madison Avenue #300 Council Bluffs, IA 51503
(888) 968-1222 <https://storagematerials.com>


DESCRIPTION: RIGID FRAME ELEVATION						
CUSTOMER: CUSTOMER				PROJECT: BRANDON CUTTS		
LOCATION:						
DRN. BY ART	CK'D BY AER	DATE 3/ 3/26	SCALE N.T.S.	REV. 00	QUOTATION NO. Q25-0843B	SHEET NO. OF

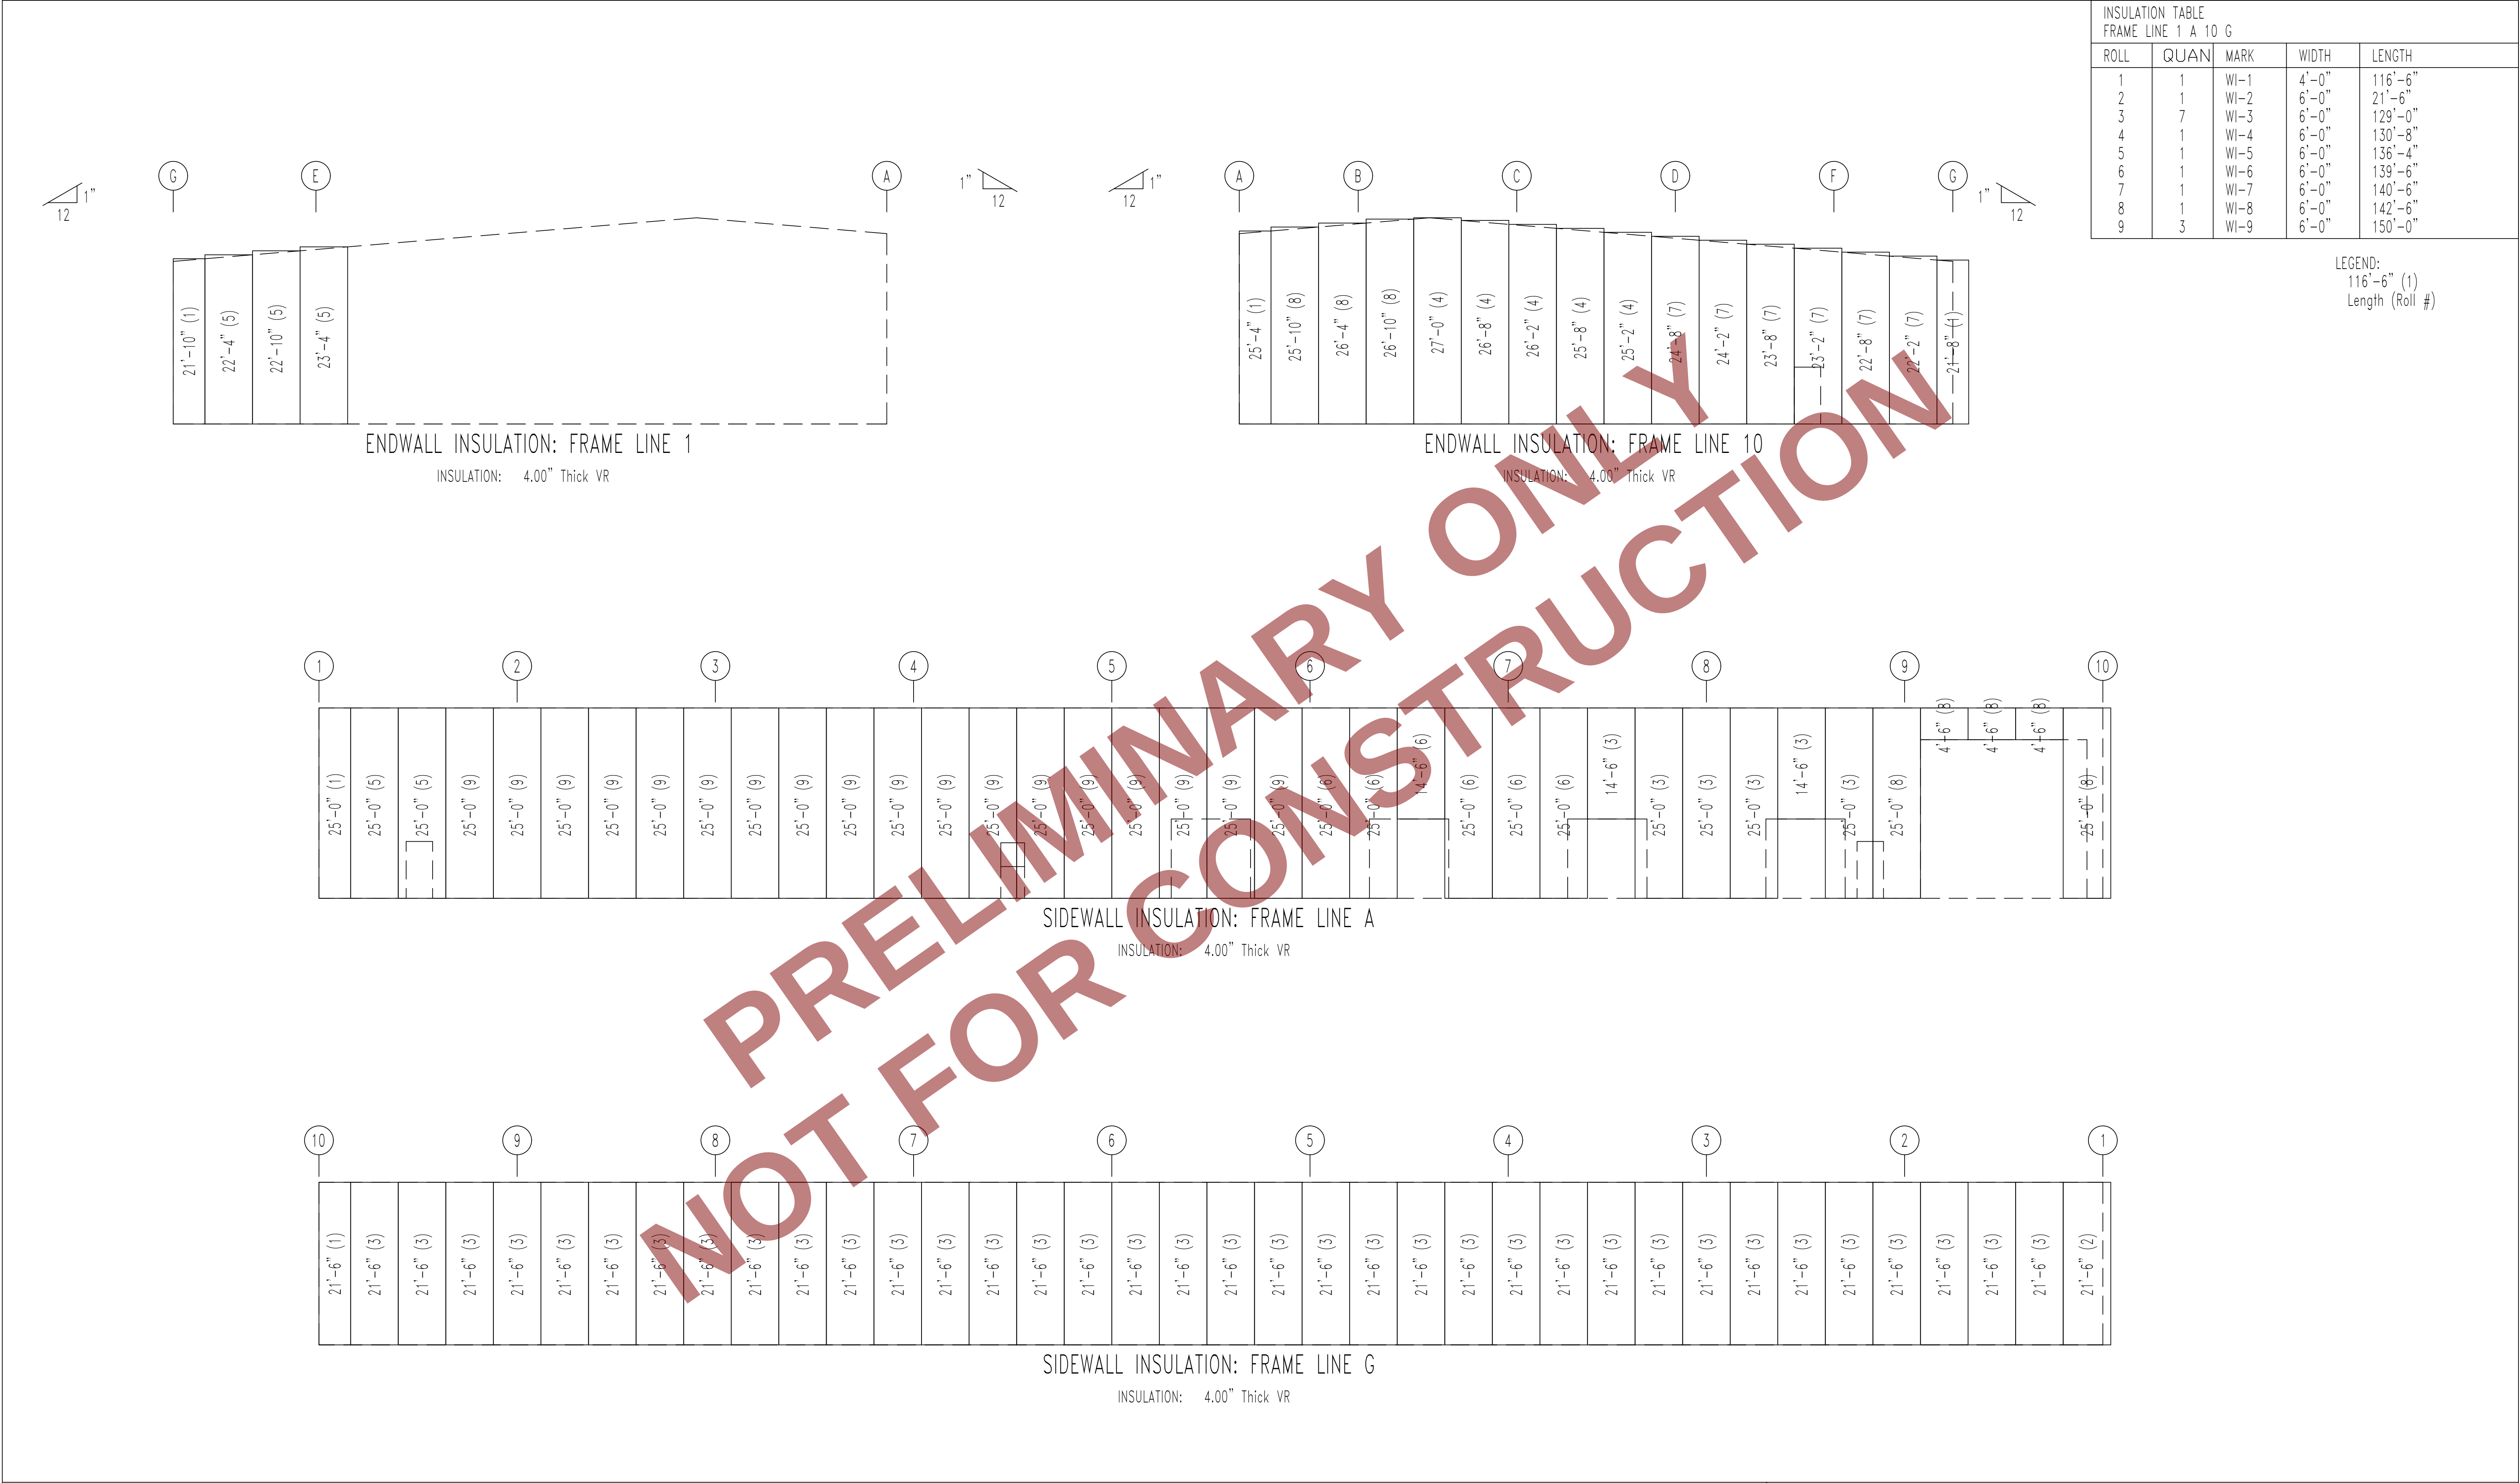

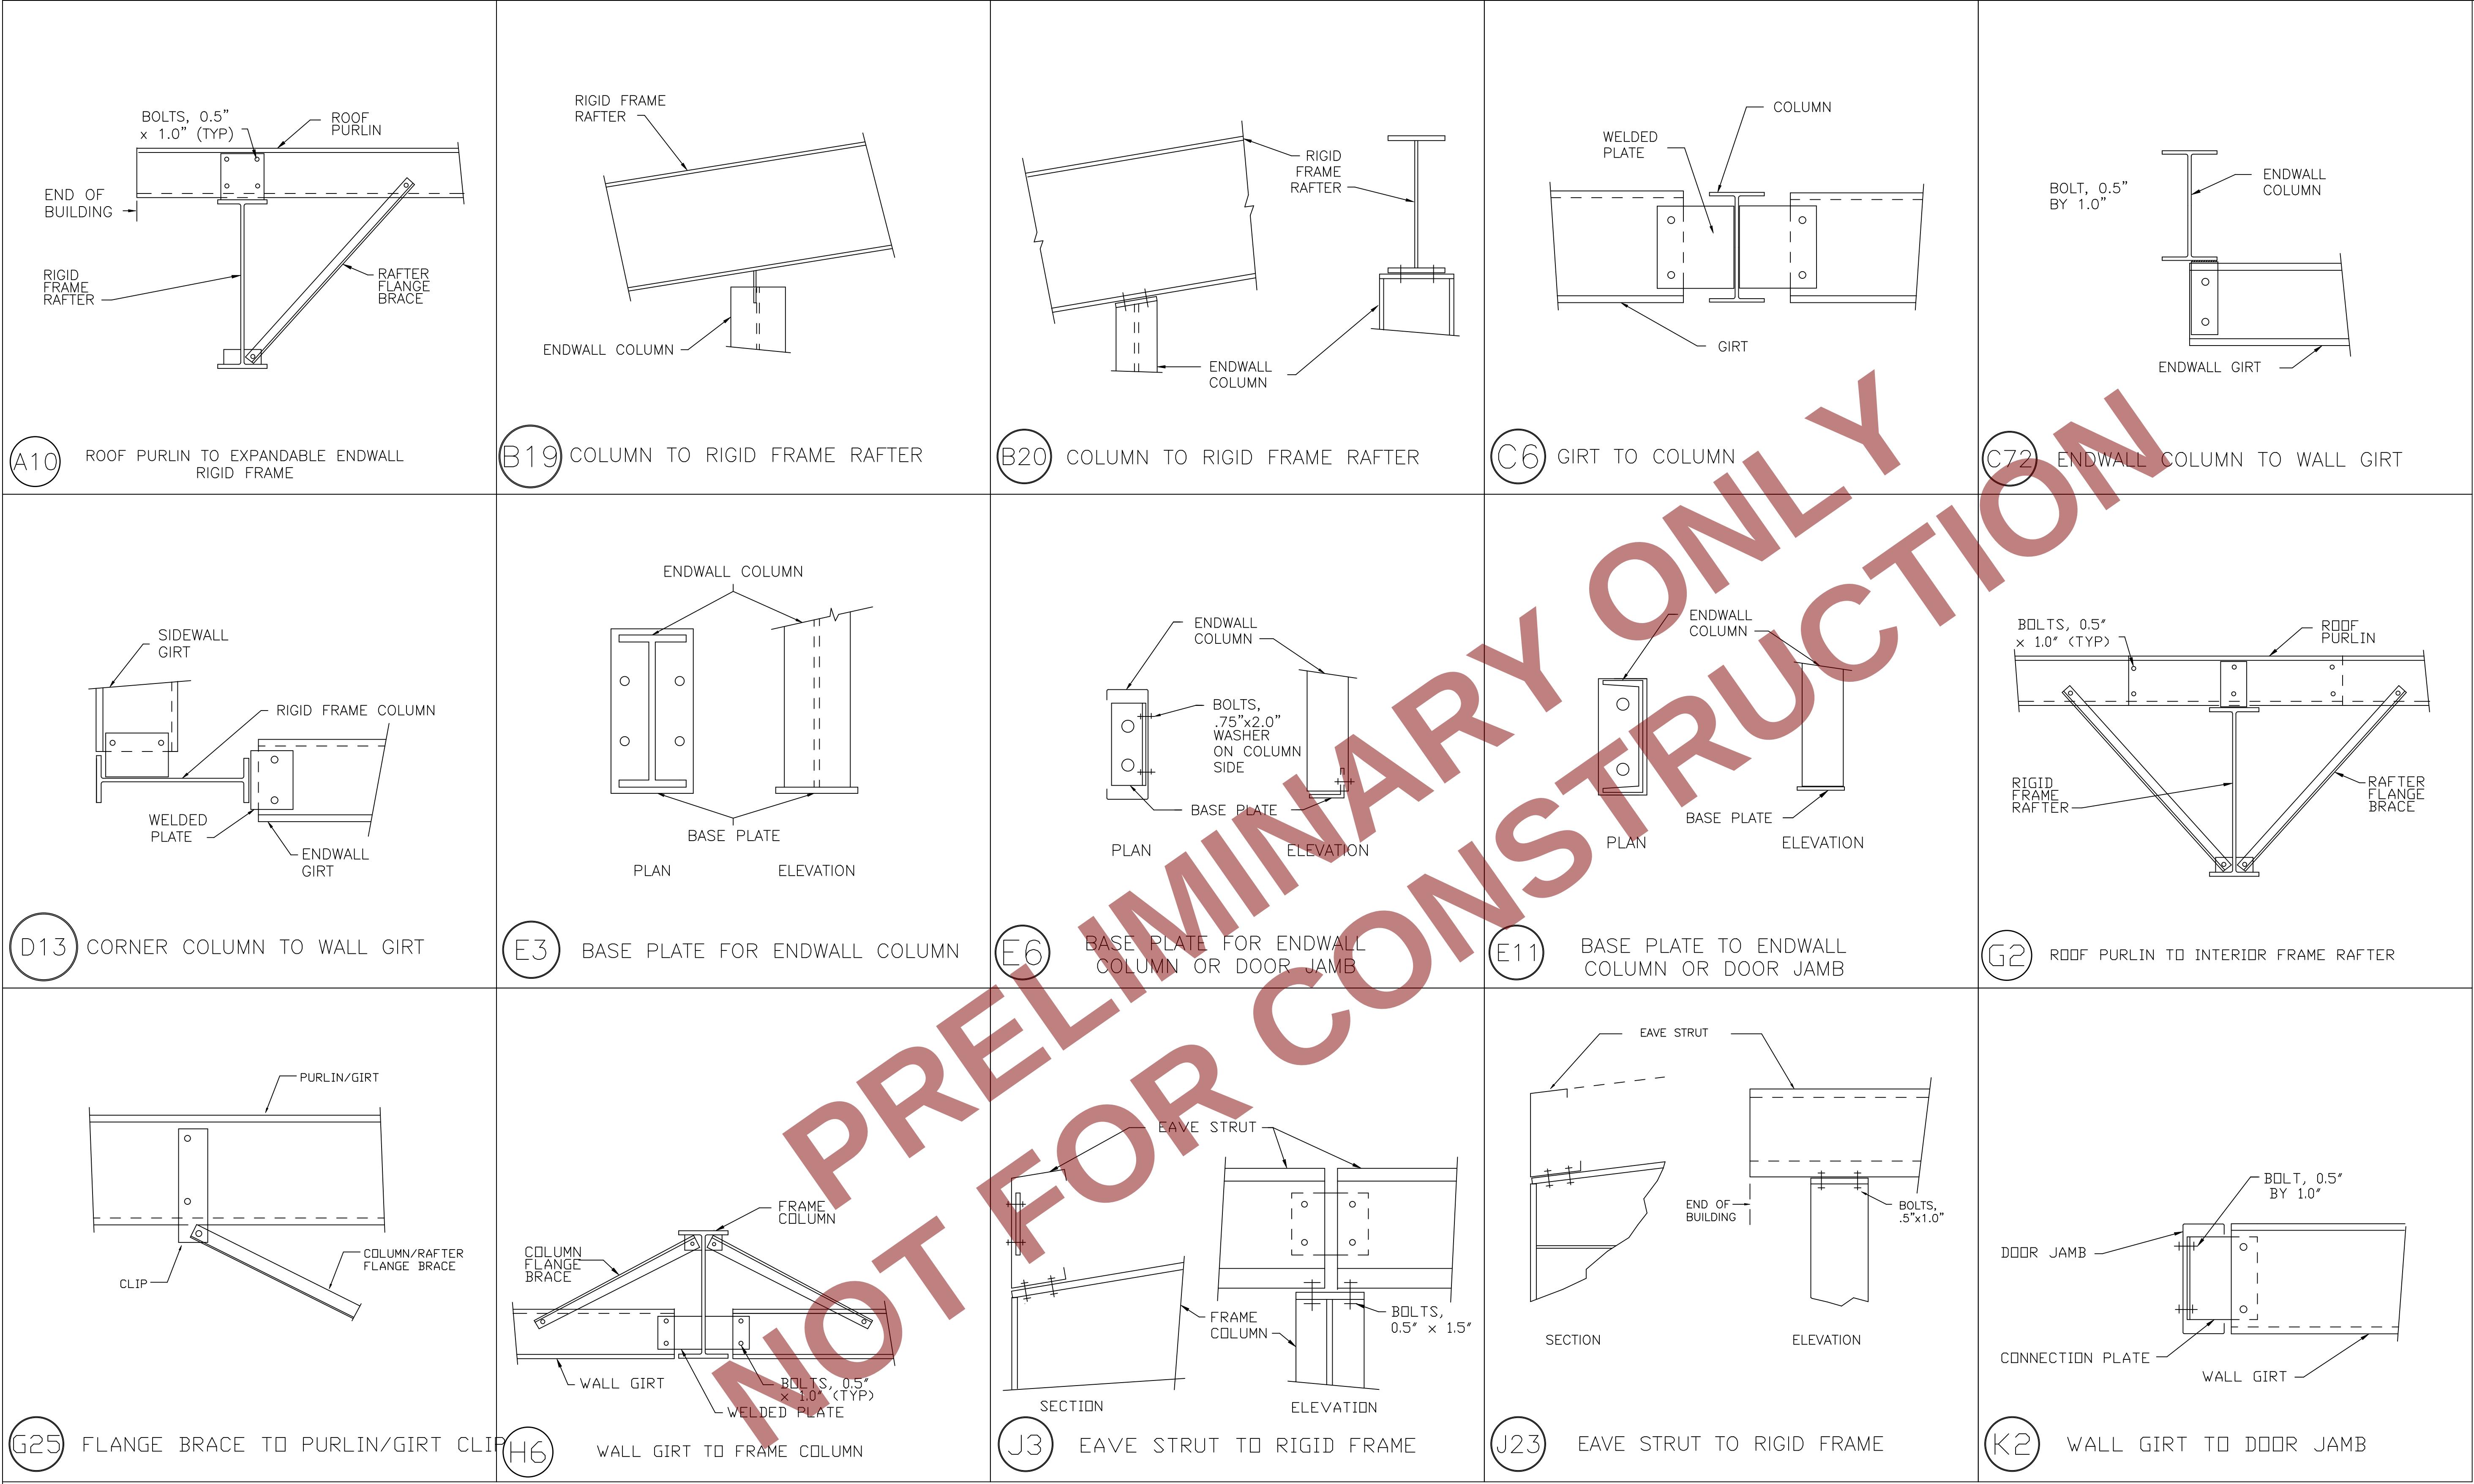


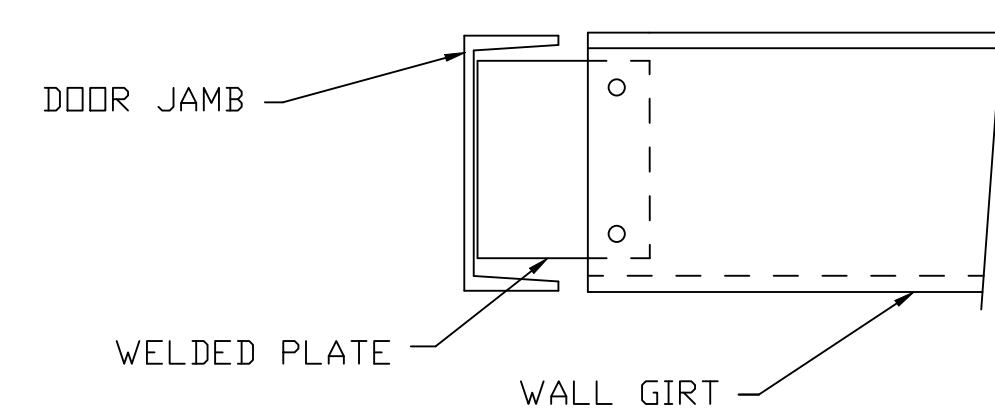


(K9) WALL GIRT TO DOOR JAMB

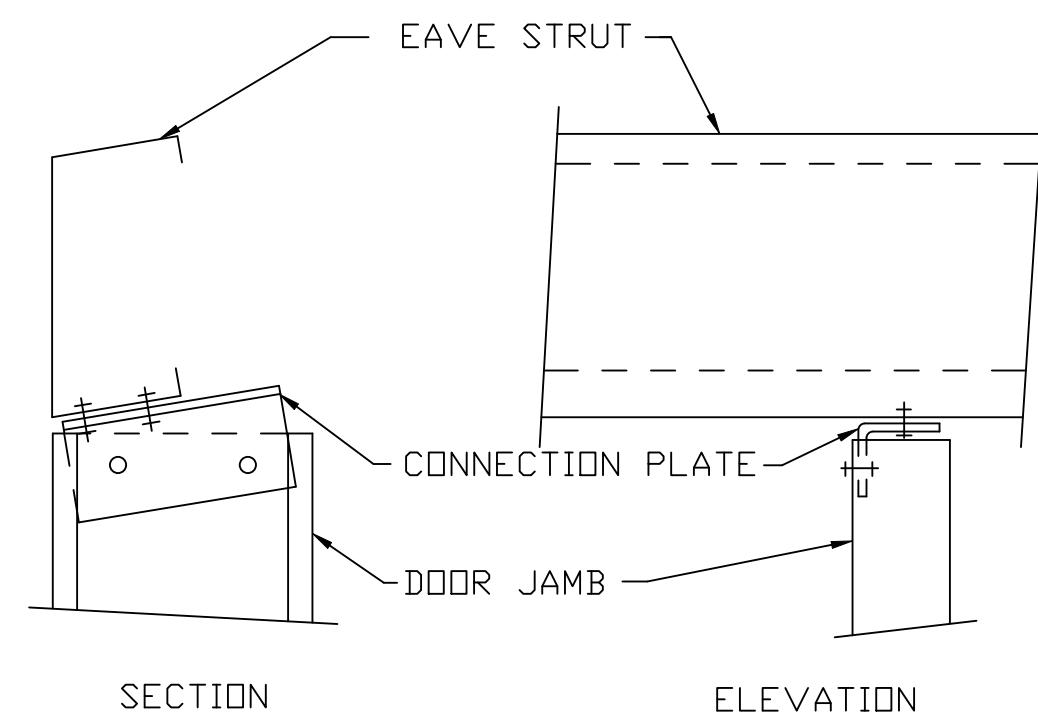


1) DOOR JAMB TO EAVE STRUT

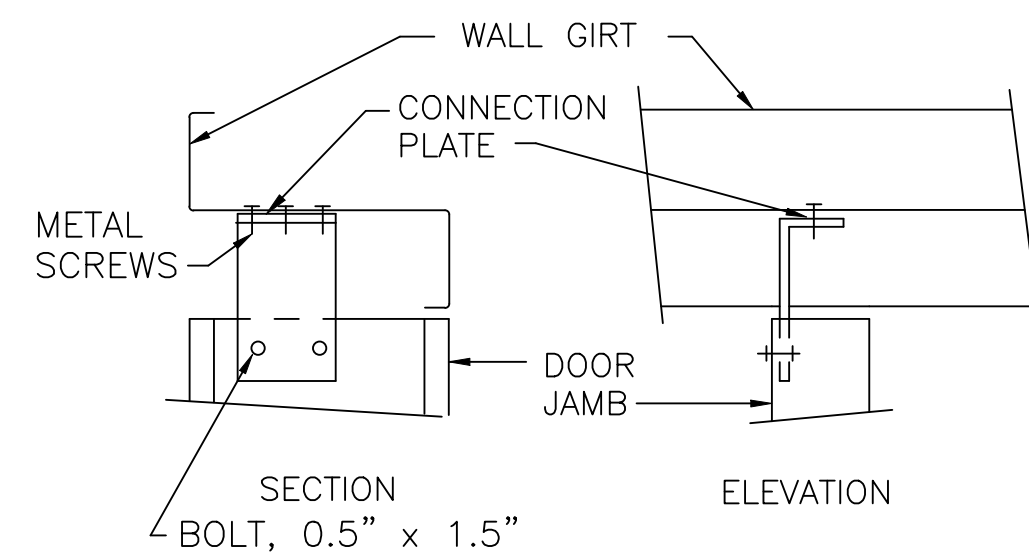


6) DOOR JAMB TO WALL GIRT

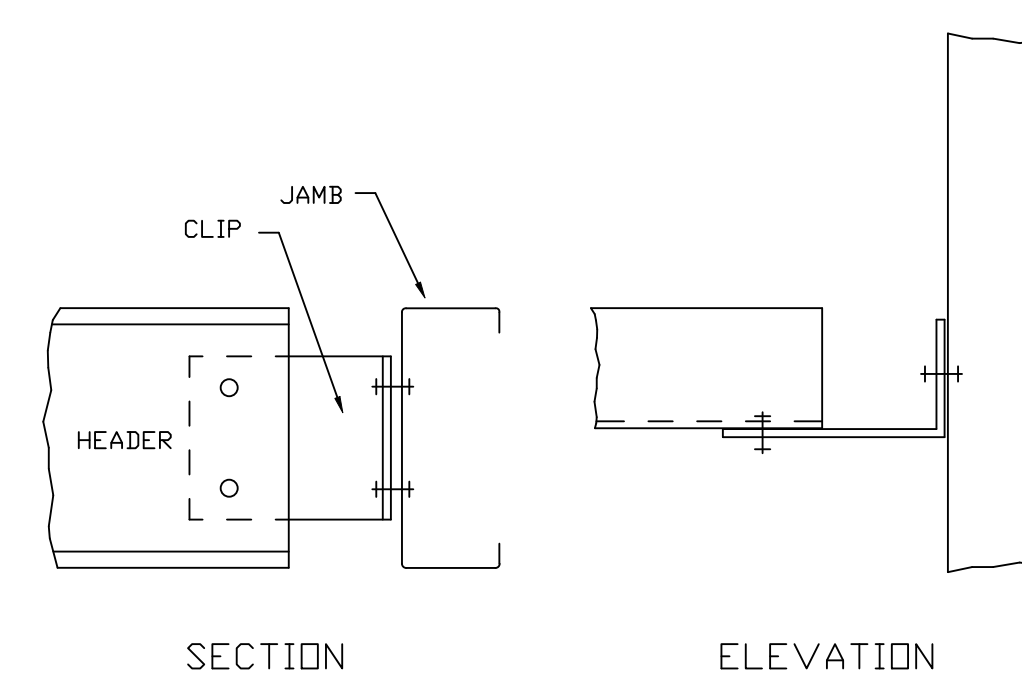


11) HEADER TO C JAMB

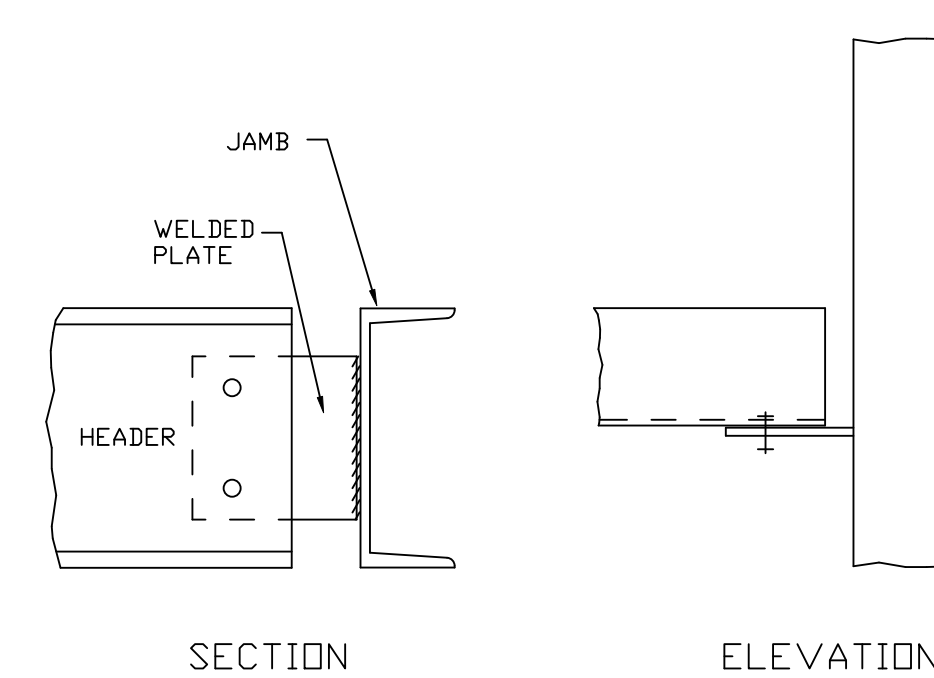


19) HEADER TO U JAMB

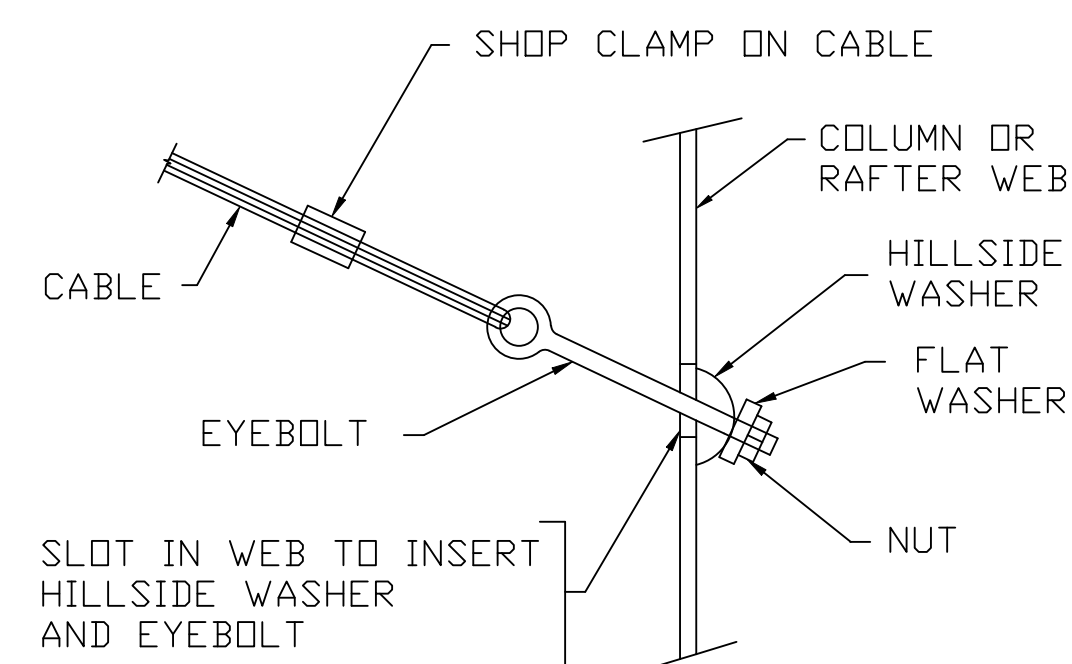


Q2) DIAGONAL CABLE, EYEBOLT END

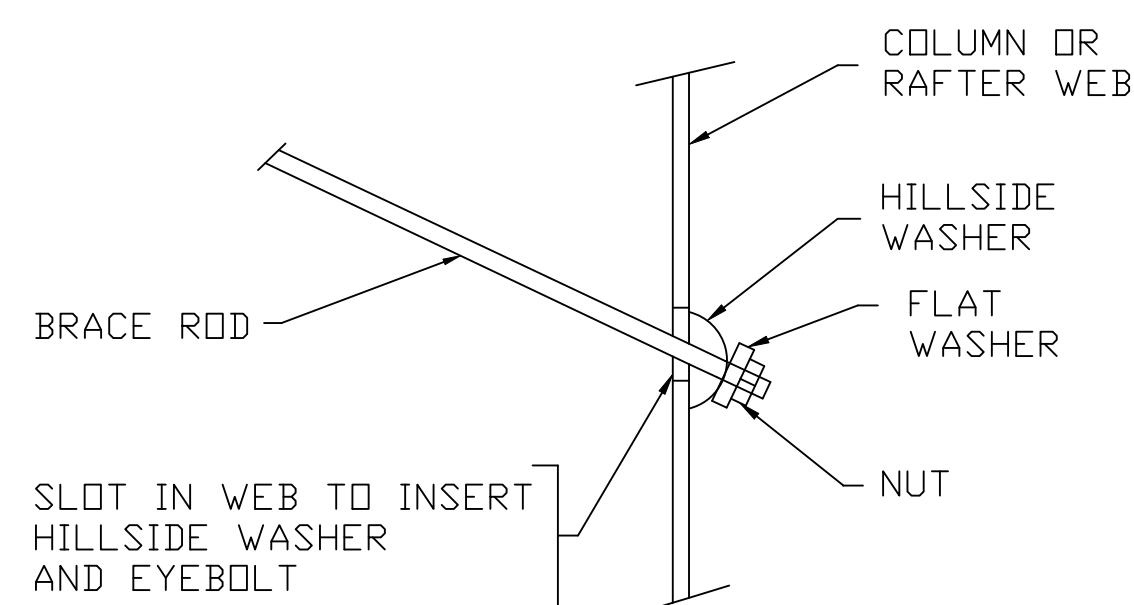


Q3) DIAGONAL BRACE ROD, NUT END

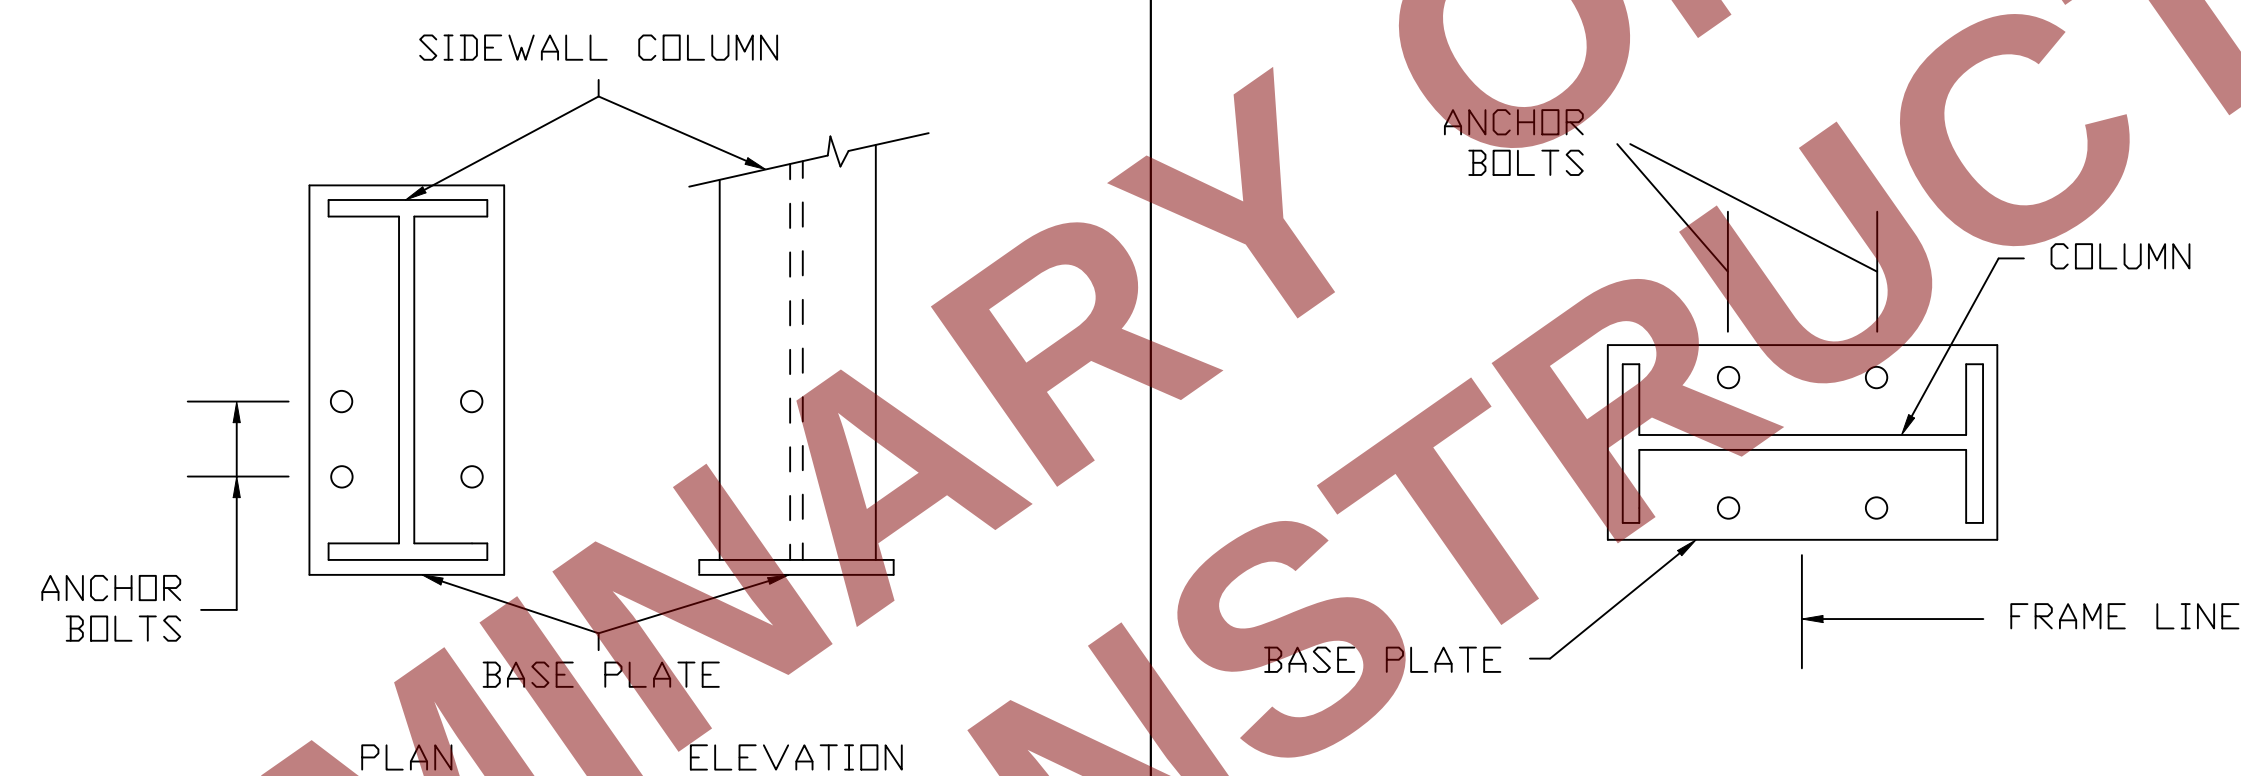


(R2) ANCHOR BOLTS AT SIDEWALL COLUMN

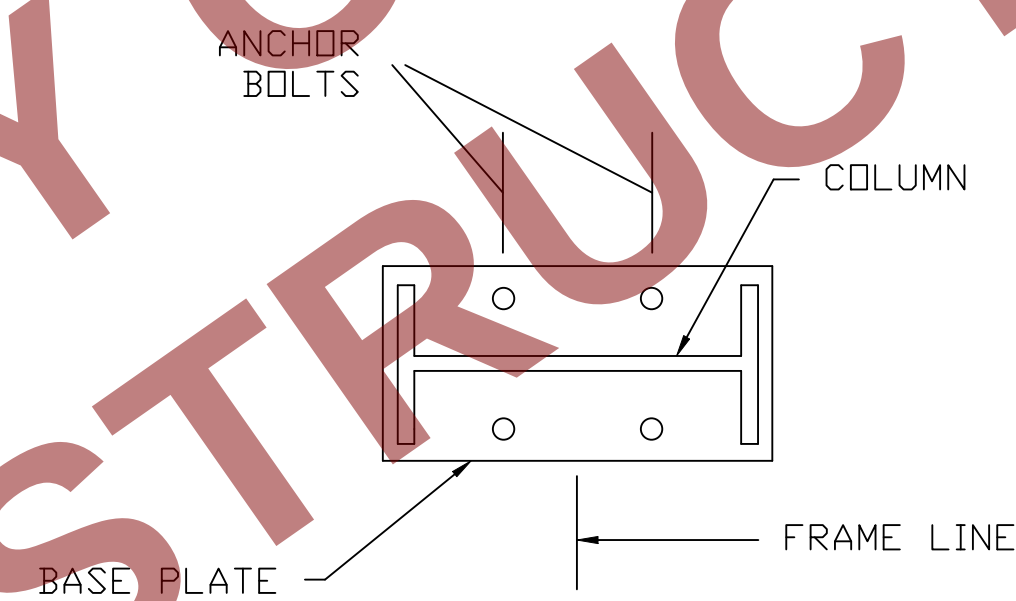


2) INTERIOR COLUMN ANCHOR BOLTS

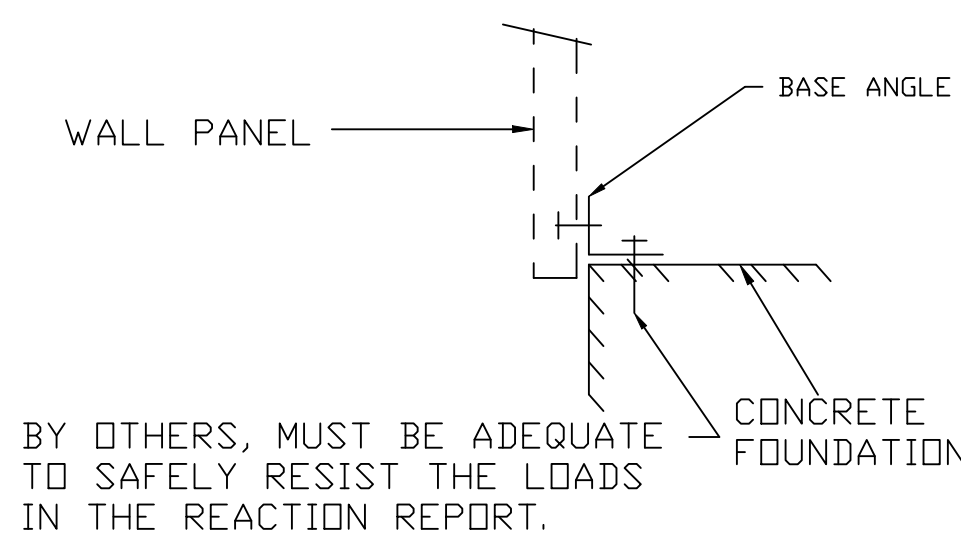


T3 SECTION THRU WALL PANEL
AND CONCRETE FOUNDATION

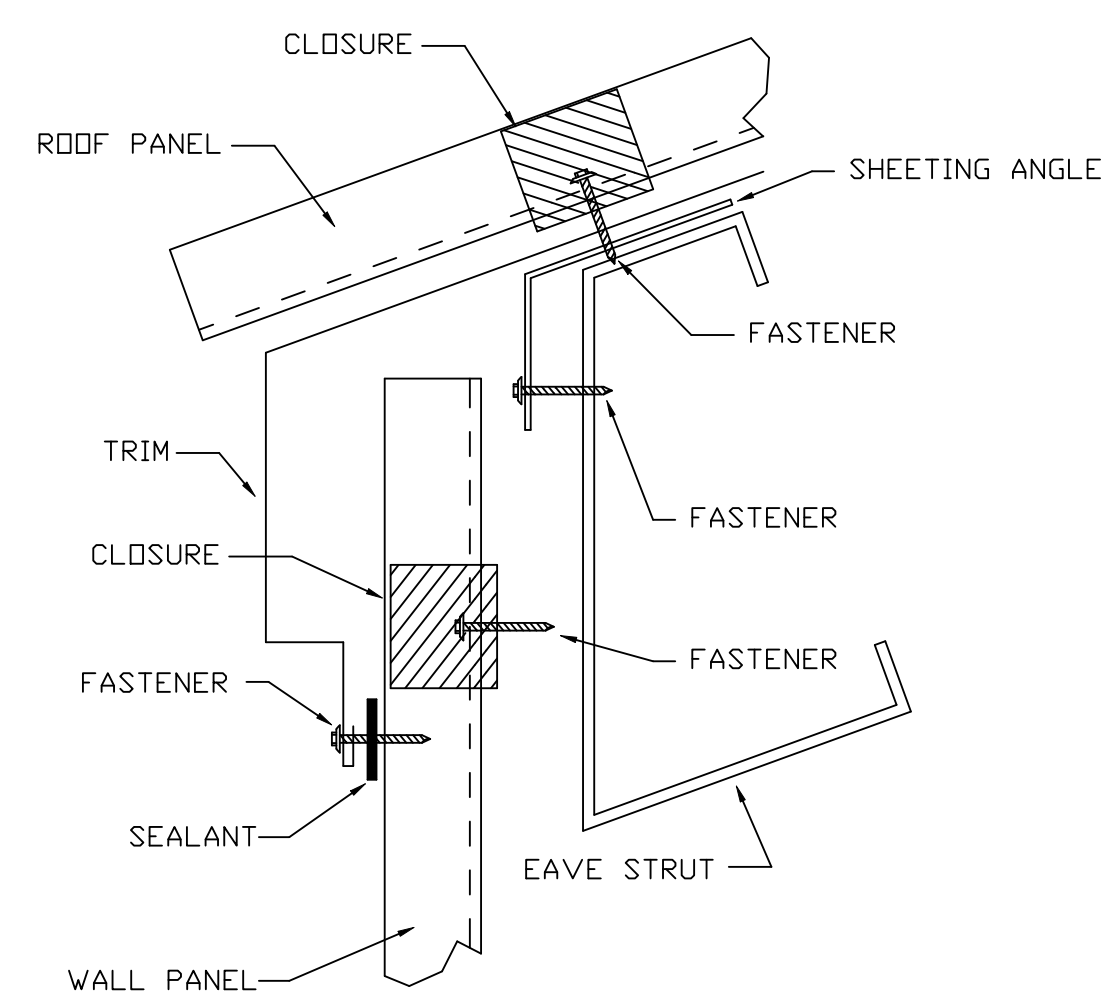


TRIM_1

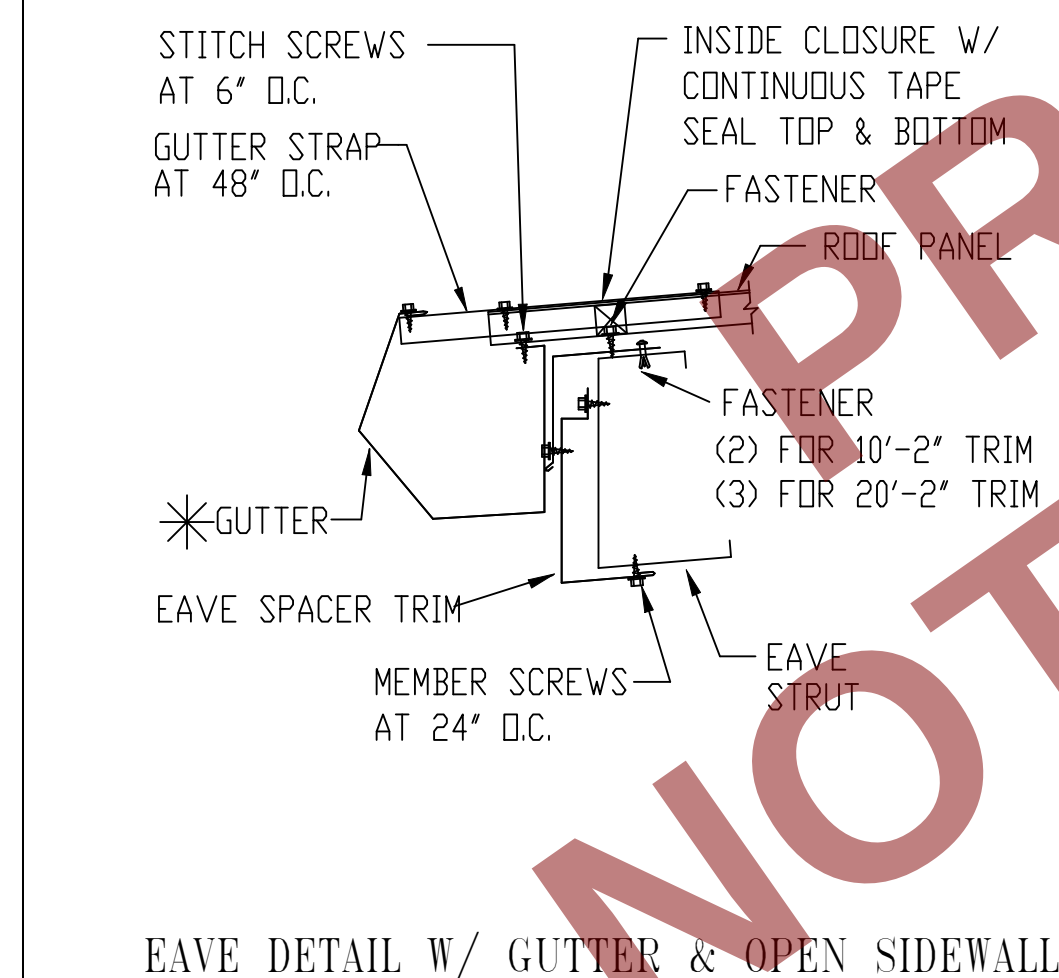


DRAWING NO. **TRIM 15** NOTE: TRIM PROFILE MAY VARY

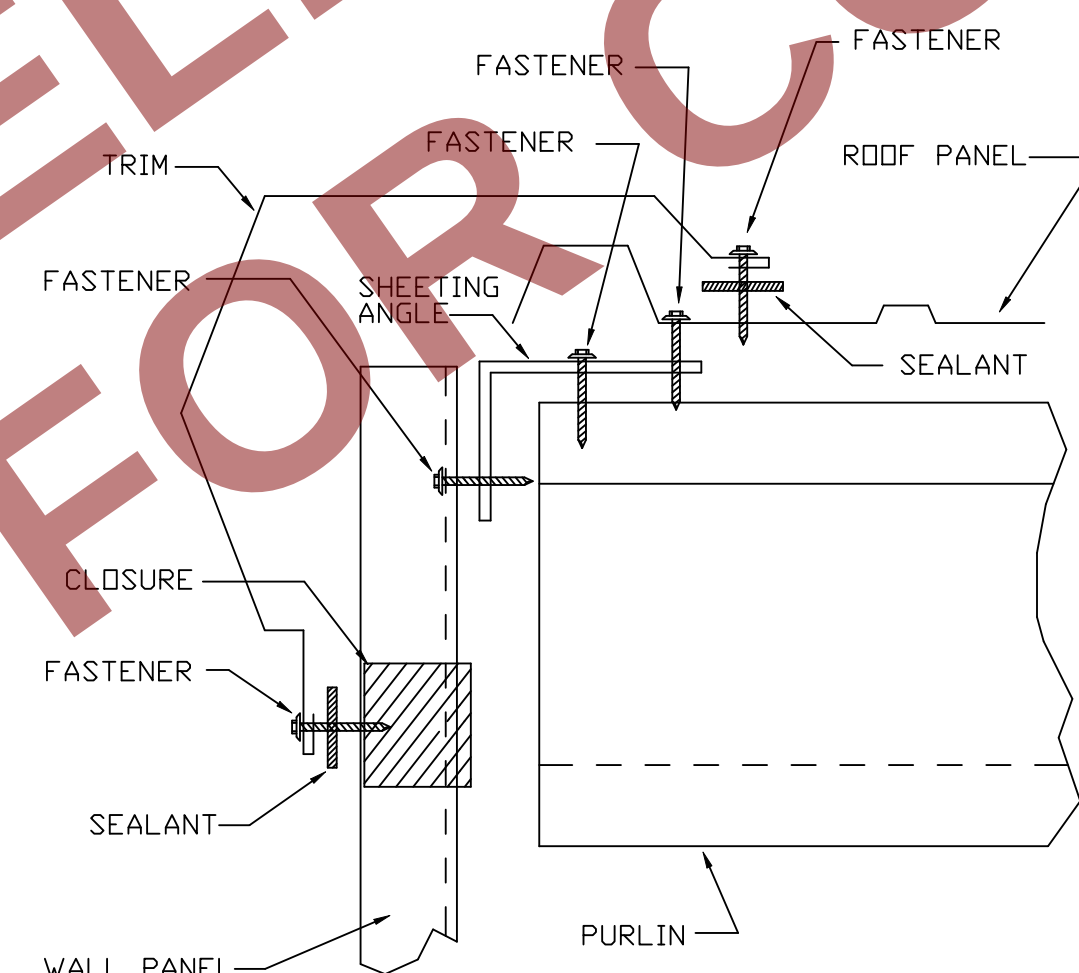

'TRIM_18'

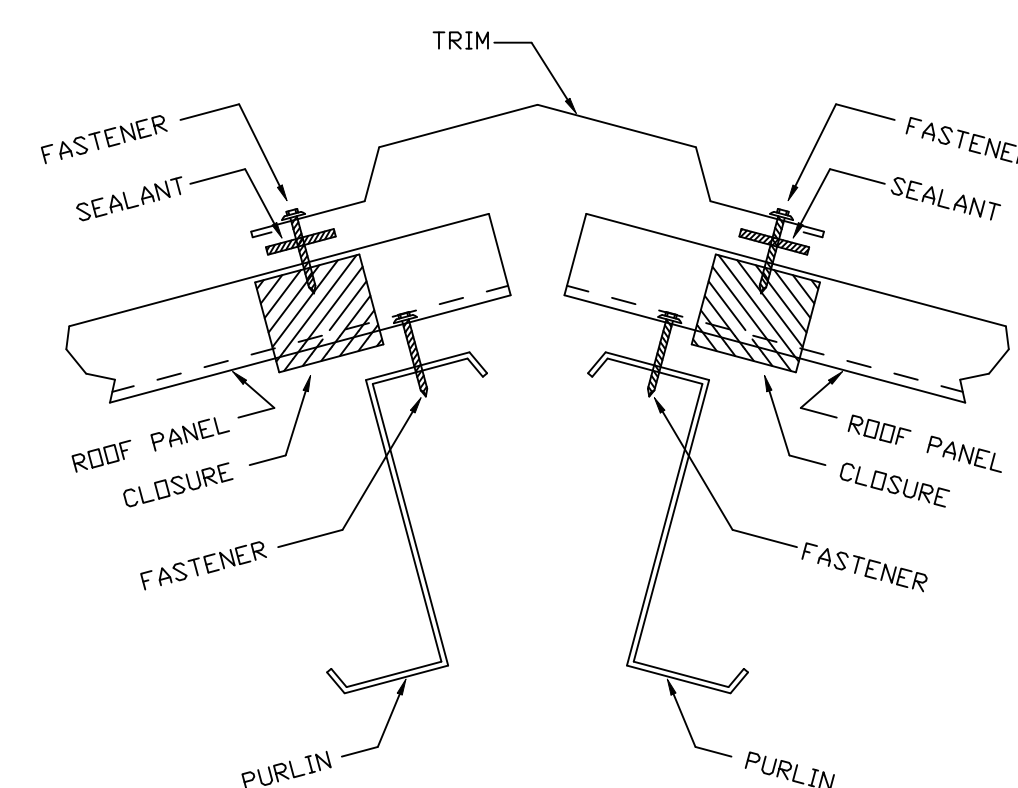

'TRIM_23'

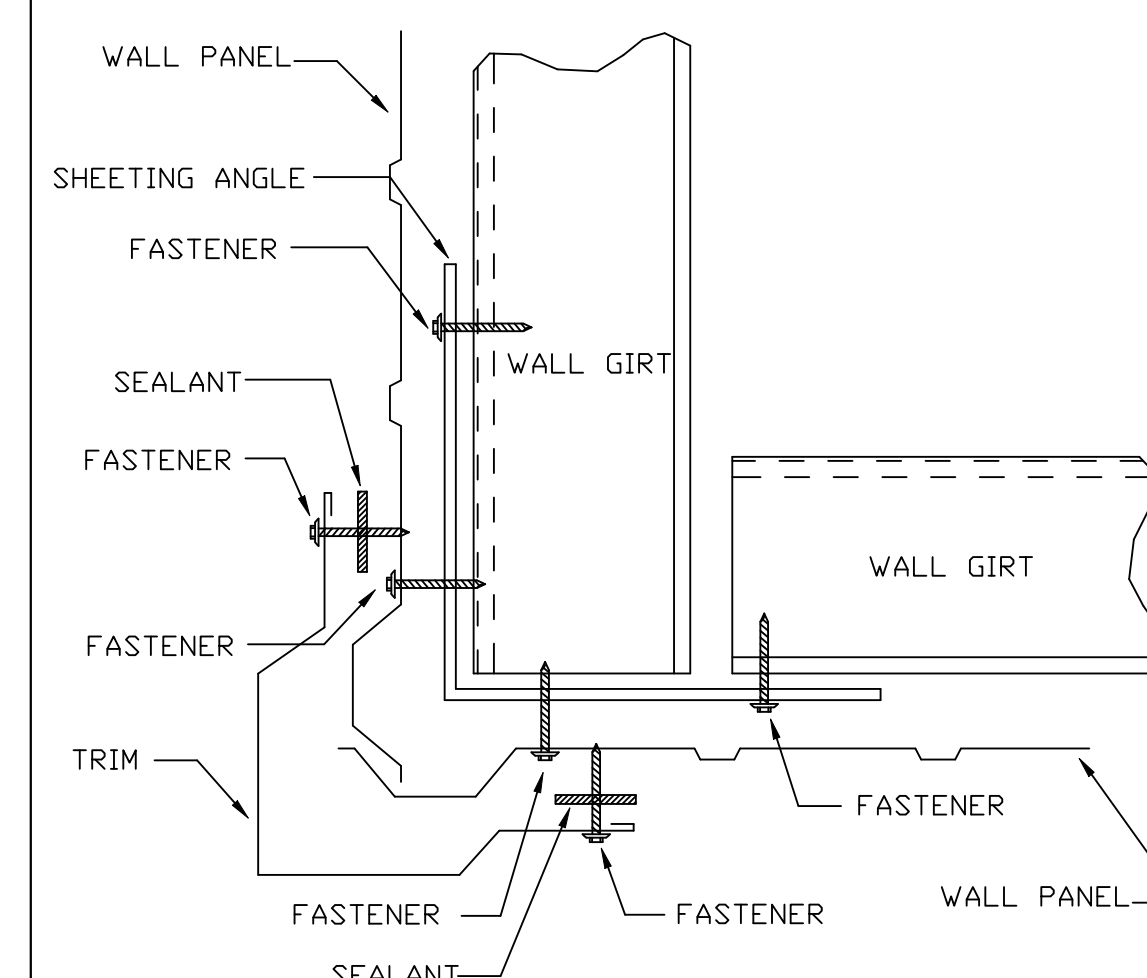

'TRIM_26'

STORAGE MATERIALS

1851 Madison Avenue #300 Council Bluffs, IA 51503
(888) 968-1222 <https://storagematerials.com>

DESCRIPTION:	DETAIL DRAWINGS
--------------	-----------------

CUSTOMER:	CUSTOMER
-----------	----------

PROJECT:	BRANDON CUTTS
----------	---------------

LOCATION:

DRN. BY
ART

CK'D BY	
AFR	

DATE
3 / 3 / 26

SCALE
N.T.S.

REV.	QUOTATION NO.
00	025-0843B

	SHEET NO.
	OF

